

Activity ID	Activity Name	Original Duration	At Completion Duration	Duration % Complete	Activity % Complete	Remaining Duration	Primary Constraint	Acrtual Start	Actual Finish	Currect Start	Current Finish	Late Start	Late Finish	Total Float	M38 Remarks
EP_SP_66_12-WP5A-M38 Programme for Design and Construction Works WP5A-M38		3467	3467	33.63%		2301		22-Nov-17 A	20-May-27	31-Jan-21	20-May-27	17-Jan-21	20-May-27	0	
EP_SP_66_12-WP5A-M38.01 Key Dates		3467	3467	33.63%		2301		22-Nov-17 A	20-May-27	31-Jan-21	20-May-27	28-Apr-22	20-May-27	0	
EP_SP_66_12-WP5A-M38.01.1 Contractual Key Dates		2794	2794	87.33%		354		22-Nov-17 A	16-Jul-25	27-Jul-24	16-Jul-25	27-Jul-24	16-Jul-25	0	
EP_SP_66_12-WP5A-M38.01.1.1 Design and Construction Phase		2738	2738	89.12%		298		22-Nov-17 A	21-May-25	27-Jul-24	21-May-25	27-Jul-24	21-May-25	0	
01-1000	Contract Award/Date of Acceptance of Tender	0	0	100%	100%	0	Mandato	22-Nov-17 A							
01-1010	Date of Commencement of the Design and the Works	0	0	100%	100%	0	Mandato	15-Dec-17 A							
01-1015(3)(M12)	Original Substantial Completion of the Works	0	0	0%	0%	0	Mandato		27-Jul-24*		27-Jul-24		27-Jul-24	0	
01-1020	Extended Substantial Completion of The Works	0	0	0%	0%	0	Mandato		21-May-25*		21-May-25		21-May-25	0	
EP_SP_66_12-WP5A-M38.01.1.3 Extension of Time Granted		298	298	0%		298		27-Jul-24	21-May-25	27-Jul-24	21-May-25	27-Jul-24	21-May-25	0	
01-1015-1(3)(M12)	Extension of time granted (Claim No.1 to No.49) *Claim No.9 excluded	298	298	0%	0%	298		27-Jul-24	21-May-25	27-Jul-24	21-May-25	27-Jul-24	21-May-25	0	
01-1060	Issuance of FS Certificate	0	0	0%	0%	0	Mandato		29-Oct-24*		29-Oct-24		29-Oct-24	0	
EP_SP_66_12-WP5A-M38.01.1.2 Operation Phase		57	57	0%		57		21-May-25	16-Jul-25	21-May-25	16-Jul-25	21-May-25	16-Jul-25	0	
01-1030	Commencement of Operation	0	0	0%	0%	0	Mandato	21-May-25*		21-May-25		21-May-25		0	
01-1230	Issue Certificate of Completion of the Works (56 days after Substantial Completion)	0	0	0%	0%	0	Finish O		16-Jul-25*		16-Jul-25		16-Jul-25	0	
EP_SP_66_12-WP5A-M38.01.2 Planned Completion Dates		1655	1655	0%		1655		08-Nov-22	20-May-27	08-Nov-22	20-May-27	19-Mar-23	20-May-27	0	
01-1030(5a)	Grid Connection Agreement (GCA)	0	0	0%	0%	0	As Late /		30-Jan-24		30-Jan-24		19-Feb-24	20	
01-1040	Incoming Power Energization to IWMF Substation	0	0	0%	0%	0			28-Jul-24		28-Jul-24		17-Aug-24	20	
01-1050	Export Power to Grid	0	0	0%	0%	0			27-Aug-24		27-Aug-24		26-Dec-24	122	
01-1070	Completion of Civil Provision for Transmission	0	0	0%	0%	0			08-Nov-22		08-Nov-22		19-Mar-23	132	
01-1080	Commencement of C1.3.4.11 System Commissioning Test	0	0	0%	0%	0		12-Sep-24		12-Sep-24		31-Aug-24		-12	
01-1090	Completion of C1.3.4.11 System Commission Test	0	0	0%	0%	0			12-Dec-24		12-Dec-24		12-Dec-24	1	
01-1100	Completion of 90 Days Plant Commissioning Test	0	0	0%	0%	0			09-Apr-25		09-Apr-25		26-Mar-25	-13	
01-1110(3)(M15)	Issue of Certificate of Substantial Completion for the Works	0	0	0%	0%	0			03-Jun-25		03-Jun-25		20-May-25	-13	
01-1110-1(5a)	Completion of 180 Days for Installation, T&C of CCTV System and Onshore Power System at Portion 2	0	0	0%	0%	0	Finish O		16-Nov-25*		16-Nov-25		20-Dec-25	34	
01-1110-2(5a)	Replacement of Onshore Cranes within 2 yrs at Portion 2	0	0	0%	0%	0			20-May-27		20-May-27		20-May-27	0	
EP_SP_66_12-WP5A-M38.01.3 Dates of Site Pocessions		0	0	0%		0		31-Jan-21	31-Jan-21	31-Jan-21	31-Jan-21	28-Apr-22	28-Apr-22	453	
01-1160	Possession of Portion 3 (Not before 31 Dec 2019)	0	0	0%	0%	0	Finish O		31-Jan-21*		31-Jan-21		28-Apr-22	453	
01-1170	Possession of Portion 4 (Not before 31 Dec 2019)	0	0	0%	0%	0	Finish O		31-Jan-21*		31-Jan-21		28-Apr-22	453	
01-1180	Possession of Portion 5 (Not before 31 Dec 2019)	0	0	0%	0%	0	Finish O		31-Jan-21*		31-Jan-21		28-Apr-22	453	
EP_SP_66_12-WP5A-M38.03 Licence/Permit Applications		1036	1036	73.94%		270		27-Dec-18 A	27-Oct-21	31-Jan-21	27-Oct-21	23-Feb-21	21-May-25	1302	
EP_SP_66_12-WP5A-M38.03.1 License/Permit for Construction		966	818	72.05%		270		02-Aug-19 A	27-Oct-21	31-Jan-21	27-Oct-21	28-Jun-21	21-May-25	1302	
03-1090	EPD APCO(SP) License for Concrete Batching Plant	270	270	0%	0%	270		31-Jan-21	27-Oct-21	31-Jan-21	27-Oct-21	28-Jun-21	24-Mar-22	148	
03-1360(2)	CNP for 24Hrs	182	661	37.91%	37.91%	113		02-Aug-19 A	23-May-21	31-Jan-21	23-May-21	29-Jan-25	21-May-25	1459	
03-1370_1(M34)	Landscape and Visual Plan	180	180	0%	0%	180		31-Jan-21	29-Jul-21	31-Jan-21	29-Jul-21	10-Sep-21	08-Mar-22	222	
EP_SP_66_12-WP5A-M38.03.4 Fire Services Installations (FSI) Certificatie		550	853	65.27%		191		10-Apr-19 A	09-Aug-21	31-Jan-21	09-Aug-21	23-Feb-21	07-Sep-21	29	
EP_SP_66_12-WP5A-M38.03.4.3 Fire Engineering Report		550	763	81.64%		101		10-Apr-19 A	11-May-21	31-Jan-21	11-May-21	23-Feb-21	27-May-21	16	
05-3000	Perparation and Submission of Fire Engineering Report to FSD	550	742	85.45%	85.45%	80		10-Apr-19 A	20-Apr-21	31-Jan-21	20-Apr-21	23-Feb-21	13-May-21	23	
05-4450	Approval of Fire Engineering Report by FSD	14	14	0%	0%	14		28-Apr-21	11-May-21	28-Apr-21	11-May-21	14-May-21	27-May-21	16	Add FS to 03-
EP_SP_66_12-WP5A-M38.03.4.1 Fire Services Installations Certificate Inspection		90	90	0%		90		12-May-21	09-Aug-21	12-May-21	09-Aug-21	10-Jun-21	07-Sep-21	29	
03-1555(5a)	General Building Plans and FSI Provision Design Submission to FSD	90	90	0%	0%	90		12-May-21	09-Aug-21	12-May-21	09-Aug-21	10-Jun-21	07-Sep-21	29	
EP_SP_66_12-WP5A-M38.03.5 Air Pollution Control (Specified Processes) License		600	966	66.67%		200		27-Dec-18 A	18-Aug-21	31-Jan-21	18-Aug-21	12-Oct-21	29-Apr-22	254	
03-1730(3)	Early Engagement With EPD SP Licensing Department for Information exchange	600	966	66.67%	66.67%	200		27-Dec-18 A	18-Aug-21	31-Jan-21	18-Aug-21	12-Oct-21	29-Apr-22	254	
EP_SP_66_12-WP5A-M38.04 General Submissions		1320	1320	86.36%		180		18-Dec-17 A	29-Jul-21	31-Jan-21	29-Jul-21	03-Oct-21	25-May-26	1761	
EP_SP_66_12-WP5A-M38.04.1 Contractor's Plans Submission and Approval		1320	1320	86.36%		180		18-Dec-17 A	29-Jul-21	31-Jan-21	29-Jul-21	03-Oct-21	25-May-26	1761	
04-1100(1)	Technical Resources Plan (TRP)	240	1199	75%	30%	60	Finish O	19-Dec-17 A	31-Mar-21*	31-Jan-21	31-Mar-21	02-Nov-21	31-Dec-21	275	
04-1200(1)	Works Plan (WP)	90	1230	0%	30%	90	Finish O	18-Dec-17 A	30-Apr-21*	31-Jan-21	30-Apr-21	03-Oct-21	31-Dec-21	245	
04-1400(1)	Operation Plan (OP)	240	1200	75%	75%	60	Finish O	18-Dec-17 A	31-Mar-21*	31-Jan-21	31-Mar-21	02-Nov-21	31-Dec-21	275	
04-1450(1)	Asset Management Plan (AMP)	120	120	0%	0%	120	Start On	06-Mar-21*	03-Jul-21	06-Mar-21	03-Jul-21	21-Nov-21	20-Mar-22	260	
04-1500(1)	Handback Plan (HP)	120	120	0%	0%	120	Start On	06-Mar-21*	03-Jul-21	06-Mar-21	03-Jul-21	21-Nov-21	20-Mar-22	260	
EP_SP_66_12-WP5A-M38.04.1.1 Provisional Assessment (PA)		180	180	0%		180		31-Jan-21	29-Jul-21	31-Jan-21	29-Jul-21	27-Nov-25	25-May-26	1761	
04-1500(1)10	Preliminary Assessmant	180	180	0%	0%	180		31-Jan-21	29-Jul-21	31-Jan-21	29-Jul-21	27-Nov-25	25-May-26	1761	
EP_SP_66_12-WP5A-M38.05 Design Submissions		1233	1237	81.59%		227		27-Apr-18 A	14-Sep-21	31-Jan-21	14-Sep-21	19-Jan-21	09-May-24	968	
EP_SP_66_12-WP5A-M38.05.01 AIP Design Package Submissions		1216	1237	81.33%		227		27-Apr-18 A	14-Sep-21	31-Jan-21	14-Sep-21	19-Jan-21	09-May-24	968	
EP_SP_66_12-WP5A-M38.05.01.01 AIP Process and Layout Design (2.1)		1111	1115	90.55%		105		27-Apr-18 A	15-May-21	31-Jan-21	15-May-21	08-Feb-21	06-Jul-21	52	
EP_SP_66_12-WP5A-M38.05.01.01.2 MSW treatment process design for mechanical treatment (2.1.02)		105	192	0%		105		05-Nov-20 A	15-May-21	31-Jan-21	15-May-21	24-Mar-21	06-Jul-21	52	
05-1090	Mechanical Treatment Plant	105	192	0%	5%	105	Start On	05-Nov-20 A	15-May-21	31-Jan-21	15-May-21	24-Mar-21	06-Jul-21	52	
EP_SP_66_12-WP5A-M38.05.01.01.6 Site Master Layout Plan and Plant Layout (2.1.06)		60	1046	40%		36		27-Apr-18 A	07-Mar-21	31-Jan-21	07-Mar-21	08-Feb-21	15-Mar-21	8	
05-3020	Site Master Layout Plan and Plant Layout	60	1046	40%	65%	36		27-Apr-18 A	07-Mar-21	31-Jan-21	07-Mar-21	08-Feb-21	15-Mar-21	8	
EP_SP_66_12-WP5A-M38.05.01.01.7 Statutory Fire Compliance (2.1.25)		30	763	0%		94		10-Apr-19 A	11-May-21	07-Feb-21	11-May-21	23-Feb-21	27-May-21	16	
05-2990	Fire Safety Compliance	30	763	0%	0%	94		10-Apr-19 A	11-May-21	07-Feb-21	11-May-21	23-Feb-21	27-May-21	16	
EP_SP_66_12-WP5A-M38.05.01.02 AIP Ground Treatment, Reclamation, Seawall, Breakwater, Berth (2.2)		931	1139	85.5%		135		03-May-18	14-Jun-21	31-Jan-21	14-Jun-21	21-Mar-21	22-Oct-21	130	
05-1280	Draft plan of 2D/3D modelling works for seawall and breakwater design (2.2.05)	135	1019	88.89%	80%	15	Start On	03-May-18	14-Feb-21	31-Jan-21	14-Feb-21	21-Mar-21	04-Apr-21	49	
05-2960-1(M37)	Mooring Dolphins	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	10-Jun-21	22-Oct-21	130	
05-2970	Onshore crane Facility (2.2.11)	135	135	0%	0%	135	Start On	31-Jan-21*	14-Jun-21	31-Jan-21	14-Jun-21	08-May-21	19-Sep-21	97	
05-2980	Onshore vessel power supply system (2.2.12)	135	194	77.78%	77.78%	30		20-Aug-20 A	01-Mar-21	31-Jan-21	01-Mar-21	23-Apr-21	22-May-21	82	

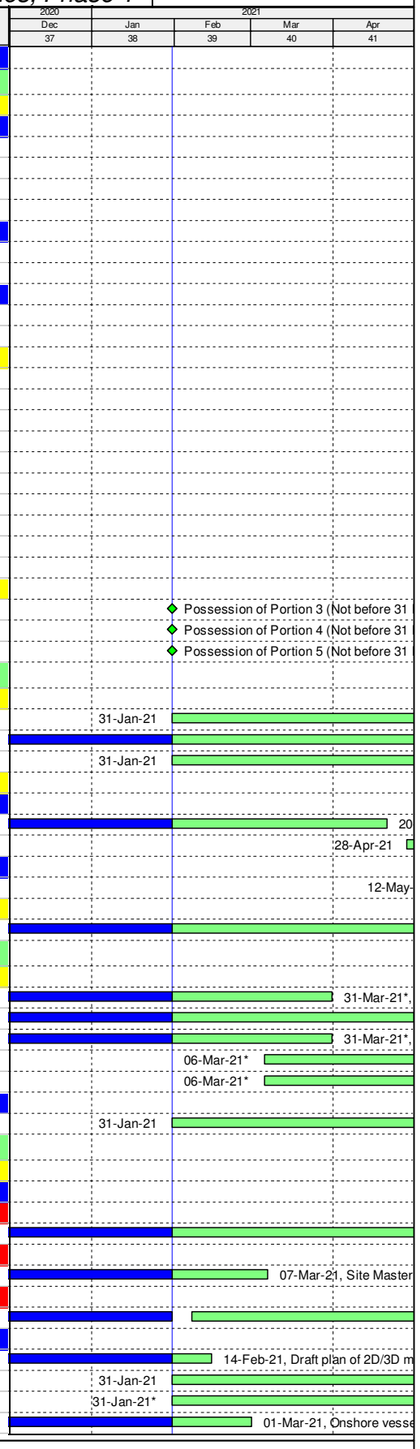


Remaining Work
Actual Work
Critical Remaining Work
Milestone
Actual Milestone
Critical Milestone

Activity ID	Activity Name	Original Duration	At Completion Duration	Duration % Complete	Activity % Complete	Remaining Duration	Primary Constraint	Acrtual Start	Actual Finish	Currect Start	Current Finish	Late Start	Late Finish	Total Float	M38 Remarks
EP_SP_66_12-WP5A-M38.05.01.03 AIP Incineration Plant Buildings (2.3)		931	1070	85.5%		135		11-Jul-18 A	14-Jun-21	31-Jan-21	14-Jun-21	05-Feb-21	24-Sep-22	466	
EP_SP_66_12-WP5A-M38.05.01.03.1 General Layout Drawings and Fire Saftey Strategy (2.3.00)		931	986	85.5%		135		03-Oct-18 A	14-Jun-21	31-Jan-21	14-Jun-21	30-Apr-21	11-Oct-21	119	
05-1210	Process Building	135	881	77.78%	5%	30	Start On	03-Oct-18 A	01-Mar-21	31-Jan-21	01-Mar-21	30-Apr-21	29-May-21	89	
05-1220	ACC Equipment Structure	135	148	79.26%	79.26%	28		03-Oct-20 A	27-Feb-21	31-Jan-21	27-Feb-21	06-May-21	02-Jun-21	95	
05-1250	Chimney and viewing platform	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	30-May-21	11-Oct-21	119	
EP_SP_66_12-WP5A-M38.05.01.03.2 Foundation design (2.3.01)		258	308	47.67%		135		11-Aug-20 A	14-Jun-21	31-Jan-21	14-Jun-21	27-Jul-21	18-Aug-22	429	
05-3030	Process Building Waste Bunker, Tipping Hall, Basin Area and Workshop	43	216	0%	5%	43	Start On	11-Aug-20 A	14-Mar-21	31-Jan-21	14-Mar-21	27-Jul-21	08-Sep-21	177	
05-3040	ACC Equipment Structure	43	216	0%	0%	43	Start On	11-Aug-20 A	14-Mar-21	31-Jan-21	14-Mar-21	19-Oct-21	30-Nov-21	261	
05-3070	Chimney and viewing platform	135	135	0%	0%	135	Start On	31-Jan-21*	14-Jun-21	31-Jan-21	14-Jun-21	22-Aug-21	04-Jan-22	203	
05-3090	Reception Pavilion	135	135	0%	0%	135	Start On	31-Jan-21*	14-Jun-21	31-Jan-21	14-Jun-21	05-Apr-22	18-Aug-22	429	
EP_SP_66_12-WP5A-M38.05.01.03.3 Structural design (2.3.02)		167	746	19.16%		135		31-May-19	14-Jun-21	31-Jan-21	14-Jun-21	12-May-22	24-Sep-22	466	
05-1330	Chimney and viewing platform	167	746	19.16%	5%	135	Start On	31-May-19	14-Jun-21	31-Jan-21	14-Jun-21	12-May-22	24-Sep-22	466	
EP_SP_66_12-WP5A-M38.05.01.03.6 Fire services installation design (2.3.05)		673	866	84.99%		101		28-Dec-18 A	11-May-21	31-Jan-21	11-May-21	27-Feb-21	27-May-21	16	
EP_SP_66_12-WP5A-M38.05.01.03.6.1 Process Building (2.3.05.01)		673	853	84.99%		101		10-Jan-19 A	11-May-21	31-Jan-21	11-May-21	14-Mar-21	27-May-21	16	
05-1510	Fire Systems	105	827	28.57%	5%	75		10-Jan-19 A	15-Apr-21	31-Jan-21	15-Apr-21	14-Mar-21	27-May-21	42	
05-1520	Fire engineering	30	30	0%	0%	30		12-Apr-21	11-May-21	12-Apr-21	11-May-21	28-Apr-21	27-May-21	16	
05-1530	FS schematics	105	759	93.33%	5%	7		10-Jan-19 A	06-Feb-21	31-Jan-21	06-Feb-21	06-May-21	12-May-21	95	
EP_SP_66_12-WP5A-M38.05.01.03.6.3 Turbin Hall Building (2.3.05.03)		590	866	82.88%		101		28-Dec-18 A	11-May-21	31-Jan-21	11-May-21	27-Feb-21	27-May-21	16	
05-5400	Fire Systems (2.3.05.03.01)	105	840	28.57%	5%	75		28-Dec-18 A	15-Apr-21	31-Jan-21	15-Apr-21	14-Mar-21	27-May-21	42	
05-5410 (M22)	Fire engineering	30	30	0%	0%	30		12-Apr-21	11-May-21	12-Apr-21	11-May-21	28-Apr-21	27-May-21	16	
05-5420 (M22)	FS schematics (2.3.05.03.03)	105	840	28.57%	5%	75		28-Dec-18 A	15-Apr-21	31-Jan-21	15-Apr-21	27-Feb-21	12-May-21	27	
EP_SP_66_12-WP5A-M38.05.01.03.6.5 Elevated Drive Way and Associated Structures (2.3.05.05)		180	487	58.33%		75		16-Dec-19 A	15-Apr-21	31-Jan-21	15-Apr-21	27-Feb-21	27-May-21	42	
05-5445 (M22)	Fire Systems	180	487	58.33%	5%	75		16-Dec-19 A	15-Apr-21	31-Jan-21	15-Apr-21	14-Mar-21	27-May-21	42	
05-5450 (M22)	FS schematics	180	487	58.33%	5%	75		16-Dec-19 A	15-Apr-21	31-Jan-21	15-Apr-21	27-Feb-21	12-May-21	27	
EP_SP_66_12-WP5A-M38.05.01.03.6.6 Reception Pavilion (2.3.05.06)		270	560	72.22%		75		04-Oct-19 A	15-Apr-21	31-Jan-21	15-Apr-21	27-Feb-21	27-May-21	42	
05-5460 (M22)	Fire Systems (2.3.05.06.01)	270	560	72.22%	5%	75		04-Oct-19 A	15-Apr-21	31-Jan-21	15-Apr-21	14-Mar-21	27-May-21	42	
05-5470 (M22)	FS schematics (2.3.05.06.03)	270	560	72.22%	5%	75		04-Oct-19 A	15-Apr-21	31-Jan-21	15-Apr-21	27-Feb-21	12-May-21	27	
EP_SP_66_12-WP5A-M38.05.01.03.6.7 Compressor & Closed Circuit (2.3.05.07)		140	583	46.43%		75		11-Sep-19 A	15-Apr-21	31-Jan-21	15-Apr-21	27-Feb-21	27-May-21	42	
05-5480 (M22)	Fire Systems (2.3.05.07.01)	140	583	46.43%	46.43%	75		11-Sep-19 A	15-Apr-21	31-Jan-21	15-Apr-21	14-Mar-21	27-May-21	42	
05-5490 (M22)	FS schematics (2.3.05.07.03)	140	583	46.43%	46.43%	75		11-Sep-19 A	15-Apr-21	31-Jan-21	15-Apr-21	27-Feb-21	12-May-21	27	
EP_SP_66_12-WP5A-M38.05.01.03.7 Building services design (excluding fire services installation design) (2.3.06)		924	1070	85.39%		135		11-Jul-18 A	14-Jun-21	31-Jan-21	14-Jun-21	05-Feb-21	15-Dec-21	184	
05-1550	Electrical Services and Lighting	150	797	70%	5%	45	Start On	10-Jan-19 A	16-Mar-21	31-Jan-21	16-Mar-21	27-Apr-21	10-Jun-21	86	
05-1560	MVAC	105	817	38.1%	38.1%	65	Start On	10-Jan-19 A	05-Apr-21	31-Jan-21	05-Apr-21	01-May-21	04-Jul-21	90	
05-1570	Odour Control	135	1005	48.15%	5%	70	Start On	11-Jul-18 A	10-Apr-21	31-Jan-21	10-Apr-21	10-Jun-21	18-Aug-21	130	
05-1580	Plumbing	210	770	89.05%	89.05%	23	Start On	15-Jan-19 A	22-Feb-21	31-Jan-21	22-Feb-21	17-Feb-21	11-Mar-21	17	
05-1590	Drainage (7 Packages)	210	782	83.33%	25%	35	Start On	15-Jan-19 A	06-Mar-21	31-Jan-21	06-Mar-21	05-Feb-21	11-Mar-21	5	
05-1600	ELV (7 Packages)	135	828	43.7%	65%	76	Start On	10-Jan-19 A	16-Apr-21	31-Jan-21	16-Apr-21	10-Jun-21	24-Aug-21	130	
05-1610	Lifts and Escalators (2 Packages)	135	488	33.33%	5%	90	Start On	30-Dec-19 A	30-Apr-21	31-Jan-21	30-Apr-21	12-Mar-21	10-Jun-21	40	
05-1630	Building Management System (BMS) (7 Packages)	135	162	54.07%	5%	62	Start On	23-Oct-20 A	02-Apr-21	31-Jan-21	02-Apr-21	15-Oct-21	15-Dec-21	257	
05-1770	Vehicle & Container Wash System	135	135	0%	0%	135	Start On	31-Jan-21*	14-Jun-21	31-Jan-21	14-Jun-21	02-Mar-21	14-Jul-21	30	
05-1770-1(M20)	Water Cannon System	135	627	80%	5%	27	Start On	11-Jun-19 A	26-Feb-21	31-Jan-21	26-Feb-21	16-Feb-21	14-Mar-21	16	
05-1770-2 (5a)	Process CCTV System	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	02-Mar-21	14-Jul-21	30	
EP_SP_66_12-WP5A-M38.05.01.04 AIP Mechanical Treatment Plant Building (2.4)		901	1012	85.02%		135		07-Sep-18 A	14-Jun-21	31-Jan-21	14-Jun-21	06-Feb-21	16-Feb-22	247	
05-1640	Architectural Design (2.4.00)	105	937	42.86%	65%	60		07-Sep-18 A	31-Mar-21	31-Jan-21	31-Mar-21	05-Sep-21	03-Nov-21	217	
05-1650	Foundation design (2.4.01)	105	617	0%	5%	105		07-Sep-19 A	15-May-21	31-Jan-21	15-May-21	26-Feb-21	10-Jun-21	26	
05-1660	Structural design (2.4.02)	105	726	0%	5%	105	Start On	21-May-19	15-May-21	31-Jan-21	15-May-21	04-Nov-21	16-Feb-22	277	
05-1670	Electrical and instrumentation works design (2.4.03)	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	04-May-21	16-Aug-21	93	
05-1680	Mechanical works design (2.4.04)	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	24-Mar-21	06-Jul-21	52	
05-1690	Fire services installation design (2.4.05) (3 Packages)	105	778	9.5%	0%	95	Start On	20-Mar-19 A	06-May-21	31-Jan-21	06-May-21	06-Feb-21	12-May-21	7	
EP_SP_66_12-WP5A-M38.05.01.04.7 Building services design (excluding fire services installation design) (2.4.06)		777	818	82.63%		135		20-Mar-19 A	14-Jun-21	31-Jan-21	14-Jun-21	10-Feb-21	01-Oct-21	109	
05-1700	LV and Emergency Power Distribution Design	17	700	0%	5%	17	Start On	20-Mar-19 A	16-Feb-21	31-Jan-21	16-Feb-21	25-May-21	10-Jun-21	114	
05-1710	MVAC	135	743	51.85%	5%	65	Start On	25-Mar-19 A	05-Apr-21	31-Jan-21	05-Apr-21	01-May-21	04-Jul-21	90	
05-1720	Odour Control	105	105	0%	0%	105	Start On	31-Jan-21*	15-May-21	31-Jan-21	15-May-21	06-May-21	18-Aug-21	95	
05-1730	Plumbing	135	788	22.22%	25%	105	Start On	20-Mar-19 A	15-May-21	31-Jan-21	15-May-21	10-Feb-21	25-May-21	10	
05-1740	Drainage	135	771	35%	5%	88	Start On	20-Mar-19 A	28-Apr-21	31-Jan-21	28-Apr-21	27-Feb-21	25-May-21	27	
05-1750	ELV	135	818	0%	0%	135	Start On	20-Mar-19 A	14-Jun-21	31-Jan-21	14-Jun-21	12-Apr-21	24-Aug-21	71	
05-1760	Lifts	135	533	0%	0%	135	Start On	30-Dec-19 A	14-Jun-21	31-Jan-21	14-Jun-21	22-Mar-21	03-Aug-21	50	
05-1760-1(M20)	Building Management System (BMS)	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	20-May-21	01-Oct-21	109	
EP_SP_66_12-WP5A-M38.05.01.05 AIP Wastewater Treatment Plant (2.5)		925	956	88.65%		105		03-Oct-18 A	15-May-21	31-Jan-21	15-May-21	10-Feb-21	24-Aug-21	101	
05-1780	Architectural Design (2.5.00)	135	911	55.56%	65%	60	Start On	03-Oct-18 A	31-Mar-21	31-Jan-21	31-Mar-21	12-Jun-21	10-Aug-21	132	
05-2790	Fire services installation design (2.5.05)	105	836	14.29%	5%	90		16-Jan-19 A	30-Apr-21	31-Jan-21	30-Apr-21	12-Feb-21	12-May-21	12	
EP_SP_66_12-WP5A-M38.05.01.05.7 Building services design (excluding fire services installation design) (2.5.06)		836	851	87.44%		105		16-Jan-19 A	15-May-21	31-Jan-21	15-May-21	10-Feb-21	24-Aug-21	101	
05-1830	LV and Emergency Power Distribution Design (2.5.06.01)	135	776	77.78%	25%	30	Start On	16-Jan-19 A	01-Mar-21	31-Jan-21	01-Mar-21	12-May-21	10-Jun-21	101	
05-1840	MVAC (2.5.06.02)	135	821	44.44%	25%	75	Start On	16-Jan-19 A	15-Apr-21	31-Jan-21	15-Apr-21	06-May-21	19-Jul-21	95	
05-1850	Odour Control (2.5.06.03)	105	105	0%	0%	105	Start On	31-Jan-21*	15-May-21	31-Jan-21	15-May-21	06-May-21	18-Aug-21	95	
05-1860	Plumbing (2.5.06.04)	135	836	33.33%	25%	90	Start On	16-Jan-19 A	30-Apr-21	31-Jan-21	30-Apr-21	25-Feb-21	25-May-21	25	

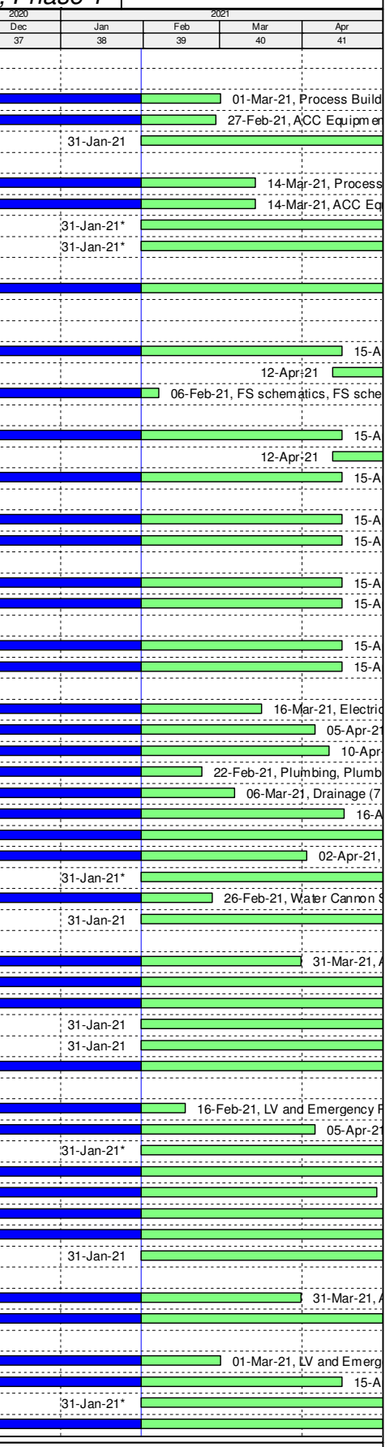


Remaining Work
Actual Work
Critical Remaining Work
Milestone
Actual Milestone
Critical Milestone

Activity ID	Activity Name	Original Duration	At Completion Duration	Duration % Complete	Activity % Complete	Remaining Duration	Primary Constraint	Acrtual Start	Actual Finish	Currect Start	Current Finish	Late Start	Late Finish	Total Float	M38 Remarks
05-1870	Drainage (2.5.06.05)	135	776	77.78%	25%	30	Start On	16-Jan-19 A	01-Mar-21	31-Jan-21	01-Mar-21	10-Feb-21	11-Mar-21	10	
05-1880	ELV (2.5.06.06)	135	822	43.7%	25%	76	Start On	16-Jan-19 A	16-Apr-21	31-Jan-21	16-Apr-21	10-Jun-21	24-Aug-21	130	
EP_SP_66_12-WP5A-M38.05.01.06 AIP Water Treatment Plant Building (2.6)		329	1012	58.97%		135		07-Sep-18 A	14-Jun-21	31-Jan-21	14-Jun-21	10-Feb-21	03-Mar-22	262	
05-1900	Architectural Design (2.6.00)	105	937	42.86%	65%	60	Start On	07-Sep-18 A	31-Mar-21	31-Jan-21	31-Mar-21	03-Jan-22	03-Mar-22	337	
05-1950	Fire services installation design (2.6.05) (3 Packages)	105	768	19%	19%	85		20-Mar-19 A	26-Apr-21	31-Jan-21	26-Apr-21	16-Feb-21	12-May-21	17	
EP_SP_66_12-WP5A-M38.05.01.06.7 Building services design (excluding fire services installation design) (2.6.06)		135	818	0%		135		20-Mar-19 A	14-Jun-21	31-Jan-21	14-Jun-21	10-Feb-21	24-Aug-21	71	
05-1960	Electrical Services and Lighting (2.6.06.01)	135	758	44.44%	5%	75	Start On	20-Mar-19 A	15-Apr-21	31-Jan-21	15-Apr-21	11-Jun-21	24-Aug-21	131	
05-1970	MVAC	135	753	44.44%	5%	75	Start On	25-Mar-19 A	15-Apr-21	31-Jan-21	15-Apr-21	21-Apr-21	04-Jul-21	80	
05-1990	Plumbing	135	788	22.22%	5%	105	Start On	20-Mar-19 A	15-May-21	31-Jan-21	15-May-21	10-Feb-21	25-May-21	10	
05-2000	Drainage	135	771	35%	5%	88	Start On	20-Mar-19 A	28-Apr-21	31-Jan-21	28-Apr-21	27-Feb-21	25-May-21	27	
05-2010	ELV	135	818	0%	5%	135	Start On	20-Mar-19 A	14-Jun-21	31-Jan-21	14-Jun-21	12-Apr-21	24-Aug-21	71	
EP_SP_66_12-WP5A-M38.05.01.07 AIP Administration Building (2.7)		932	1048	85.41%		136		03-Aug-18 A	15-Jun-21	31-Jan-21	15-Jun-21	07-Feb-21	15-Dec-21	183	
05-2020	Architectural Design (2.7.00)	135	972	55.56%	65%	60	Start On	03-Aug-18 A	31-Mar-21	31-Jan-21	31-Mar-21	02-Sep-21	01-Nov-21	214	
05-2030	Foundation design (2.7.01)	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	20-May-21	02-Oct-21	109	
05-2050	Electrical and instrumentation works design (2.7.03)	135	135	0%	0%	135	Start On	31-Jan-21*	14-Jun-21	31-Jan-21	14-Jun-21	05-Mar-21	17-Jul-21	33	
05-2060	Fire services installation design (3 Packages) (2.7.04)	135	611	29.63%	29.63%	95	Start On	03-Sep-19 A	05-May-21	31-Jan-21	05-May-21	07-Feb-21	12-May-21	7	
EP_SP_66_12-WP5A-M38.05.01.07.6 Building services design (excluding fire services installation design) (2.7.05)		594	652	77.1%		136		03-Sep-19 A	15-Jun-21	31-Jan-21	15-Jun-21	15-Feb-21	15-Dec-21	183	
05-2070	Electrical Services and Lighting (2.7.05.01)	135	591	44.44%	5%	75	Start On	03-Sep-19 A	15-Apr-21	31-Jan-21	15-Apr-21	11-Jun-21	24-Aug-21	131	
05-2080	MVAC	135	591	44.44%	5%	75	Start On	03-Sep-19 A	15-Apr-21	31-Jan-21	15-Apr-21	21-Apr-21	04-Jul-21	80	
05-2100	Plumbing	135	516	100%	5%	0	Start On	03-Sep-19 A	31-Jan-21	31-Jan-21	31-Jan-21	11-Mar-21	11-Mar-21	40	
05-2110	Drainage	135	604	35%	5%	88	Start On	03-Sep-19 A	28-Apr-21	31-Jan-21	28-Apr-21	27-Feb-21	25-May-21	27	
05-2120	ELV	135	592	43.7%	5%	76	Start On	03-Sep-19 A	16-Apr-21	31-Jan-21	16-Apr-21	10-Jun-21	24-Aug-21	130	
05-2130	Lifts and Escalators	135	533	0%	5%	135	Start On	30-Dec-19 A	14-Jun-21	31-Jan-21	14-Jun-21	15-Feb-21	30-Jun-21	15	
05-2130-1(M20)	Building Management System (BMS)	135	135	0%	0%	135	Start On	01-Feb-21*	15-Jun-21	01-Feb-21	15-Jun-21	03-Aug-21	15-Dec-21	183	
EP_SP_66_12-WP5A-M38.05.01.08 AIP IWMF Substation (2.8)		434	860	85.25%		64		27-Nov-18 A	04-Apr-21	31-Jan-21	04-Apr-21	08-Feb-21	01-Dec-21	241	
05-2170	Electrical and instrumentation works design (2.8.03) (14 Packages)	180	493	83.89%	25%	29	Start On	25-Oct-19 A	28-Feb-21	31-Jan-21	28-Feb-21	03-Nov-21	01-Dec-21	276	
05-2190	Fire services installation design (2.8.05) (2 Packages)	170	860	62.35%	25%	64	Start On	27-Nov-18 A	04-Apr-21	31-Jan-21	04-Apr-21	08-Feb-21	12-Apr-21	8	
EP_SP_66_12-WP5A-M38.05.01.1 AIP Chimney		258	539	47.67%		135		24-Dec-19 A	14-Jun-21	31-Jan-21	14-Jun-21	22-Mar-21	21-May-22	340	
EP_SP_66_12-WP5A-M38.05.01.1.1 Building services design (excluding fire services installation design)		258	539	47.67%		135		24-Dec-19 A	14-Jun-21	31-Jan-21	14-Jun-21	22-Mar-21	21-May-22	340	
05-5430(5a)	Electrical Services and Lighting	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	06-Jan-22	21-May-22	340	
05-5440(5a)	MVAC	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	22-Mar-21	04-Jul-21	50	
05-5450(5a)	Plumbing	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	05-Feb-22	21-May-22	370	
05-5460(5a)	Drainage	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	06-Jan-22	21-May-22	340	
05-5470(5a)	ELV	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	06-Jan-22	21-May-22	340	
05-5480(5a)	Lift	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	06-Jan-22	21-May-22	340	
05-5490(5a)	Building Management System (BMS)	135	493	34.07%	5%	89		24-Dec-19 A	29-Apr-21	31-Jan-21	29-Apr-21	21-Feb-22	21-May-22	386	
EP_SP_66_12-WP5A-M38.05.01.2 AIP Weighbridge		105	105	0%		105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	22-Mar-21	11-Jul-21	57	
EP_SP_66_12-WP5A-M38.05.01.2.1 Building services design (excluding fire services installation design)		105	105	0%		105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	22-Mar-21	11-Jul-21	57	
05-5510(5a)	MVAC	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	22-Mar-21	04-Jul-21	50	
05-5520(5a)	Plumbing	105	105	0%	25%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	29-Mar-21	11-Jul-21	57	
05-5530(5a)	Drainage	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	29-Mar-21	11-Jul-21	57	
05-5540(5a)	ELV	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	29-Mar-21	11-Jul-21	57	
05-5550(5a)	Lift	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	29-Mar-21	11-Jul-21	57	
EP_SP_66_12-WP5A-M38.05.01.09 AIP Air Quality Monitoring Stations (2.9)		120	120	0%		120		31-Jan-21	30-May-21	31-Jan-21	30-May-21	19-Jan-21	18-May-21	-12	
05-2250	Design of the Air Quality Monitoring Stations (2.9.01)	120	120	0%	0%	120	Start On	31-Jan-21*	30-May-21	31-Jan-21	30-May-21	19-Jan-21	18-May-21	-12	
EP_SP_66_12-WP5A-M38.05.01.10 AIP Roads and Utilities (2.10)		733	931	81.58%		135		27-Nov-18 A	14-Jun-21	31-Jan-21	14-Jun-21	02-Feb-21	12-Apr-22	302	
EP_SP_66_12-WP5A-M38.05.01.10.2 Sewerage design on the Artificial Island (2.10.02)		135	636	0%		135		18-Sep-19 A	14-Jun-21	31-Jan-21	14-Jun-21	30-Oct-21	13-Mar-22	272	
05-2290	Contaminated Sewerage concept / sizing	135	636	0%	5%	135	Start On	18-Sep-19 A	14-Jun-21	31-Jan-21	14-Jun-21	30-Oct-21	13-Mar-22	272	
EP_SP_66_12-WP5A-M38.05.01.10.3 Drainage system design on the Artificial Island (2.10.03)		135	725	22.22%		105		22-May-19	15-May-21	31-Jan-21	15-May-21	02-Feb-21	17-May-21	2	
05-2310	First Flush Drainage System concept / sizing	135	725	22.22%	5%	105	Start On	22-May-19	15-May-21	31-Jan-21	15-May-21	02-Feb-21	17-May-21	2	
EP_SP_66_12-WP5A-M38.05.01.10.4 Water supply system design on the Artificial Island (2.10.04)		563	655	76.02%		135		30-Aug-19 A	14-Jun-21	31-Jan-21	14-Jun-21	10-Feb-21	12-Apr-22	302	
05-2350	Rainwater harvesting System (2.10.04.04)	135	184	22.22%	5%	105	Start On	13-Nov-20 A	15-May-21	31-Jan-21	15-May-21	10-Feb-21	25-May-21	10	
05-2360	Water Tanks (2.10.04.05)	135	135	0%	0%	135	Start On	31-Jan-21*	14-Jun-21	31-Jan-21	14-Jun-21	29-Nov-21	12-Apr-22	302	
05-2370	External FS Systems (2.10.04.06)	135	589	0%	65%	135		04-Nov-19 A	14-Jun-21	31-Jan-21	14-Jun-21	29-Nov-21	12-Apr-22	302	
05-2370-1(M24)	E&M system for seawater intake and brine discharge (2.10.04.07)	90	610	0%	5%	90		30-Aug-19 A	30-Apr-21	31-Jan-21	30-Apr-21	02-Aug-21	30-Oct-21	183	
05-2370-2(M24)	Building Services system for seawater intake and brine discharge (2.10.04.09)	90	416	0%	5%	90		11-Mar-20 A	30-Apr-21	31-Jan-21	30-Apr-21	11-Apr-21	09-Jul-21	70	
05-2370-3(5a)	Chemical scrubber system for odour control (2.10.04.10)	90	90	0%	0%	90	Start On	31-Jan-21*	30-Apr-21	31-Jan-21	30-Apr-21	21-May-21	18-Aug-21	110	
EP_SP_66_12-WP5A-M38.05.01.10.6 Design of telecommunication and other utilities (2.10.06)		718	931	81.2%		135		27-Nov-18 A	14-Jun-21	31-Jan-21	14-Jun-21	22-Mar-21	07-Apr-22	297	
05-2380	Power Distribution System concept / schematics (2.10.06.01)	135	169	0%	5%	135	Start On	28-Dec-20 A	14-Jun-21	31-Jan-21	14-Jun-21	22-Mar-21	03-Aug-21	50	
05-2410	Site ELV Network System - Communications System concept / schematics (2.10.06.04)	135	463	0%	5%	135	Start On	09-Mar-20 A	14-Jun-21	31-Jan-21	14-Jun-21	22-Mar-21	03-Aug-21	50	
05-2420	Site ELV Network System - Security Systems concept / schematics (2.10.06.05)	135	463	0%	5%	135	Start On	09-Mar-20 A	14-Jun-21	31-Jan-21	14-Jun-21	22-Mar-21	03-Aug-21	50	
05-2430	Site ELV Network System - Navigation aids concept / schematics (2.10.06.06)	135	135	0%	0%	135	Start On	31-Jan-21*	14-Jun-21	31-Jan-21	14-Jun-21	22-Mar-21	03-Aug-21	50	
05-2440	Microwave transmission of FS direct link (2.10.06.07)	135	886	33.33%	33.33%	90		27-Nov-18 A	30-Apr-21	31-Jan-21	30-Apr-21	06-May-21	03-Aug-21	95	
05-2450	Fuel Handling System concept / schematics (2.10.06.08)	135	508	0%	5%	135	Start On	24-Jan-20 A	14-Jun-21	31-Jan-21	14-Jun-21	24-Nov-21	07-Apr-22	297	
05-3190	Computerised Maintenance Management System (CMMS)	105	676	28.57%	65%	75	Start On	10-Jun-19 A	15-Apr-21	31-Jan-21	15-Apr-21	20-Apr-21	03-Jul-21	79	
05-3200	Information and Document Management System (IDMS)	105	641	28.57%	65%	75	Start On	15-Jul-19 A	15-Apr-21	31-Jan-21	15-Apr-21	20-Apr-21	03-Jul-21	79	

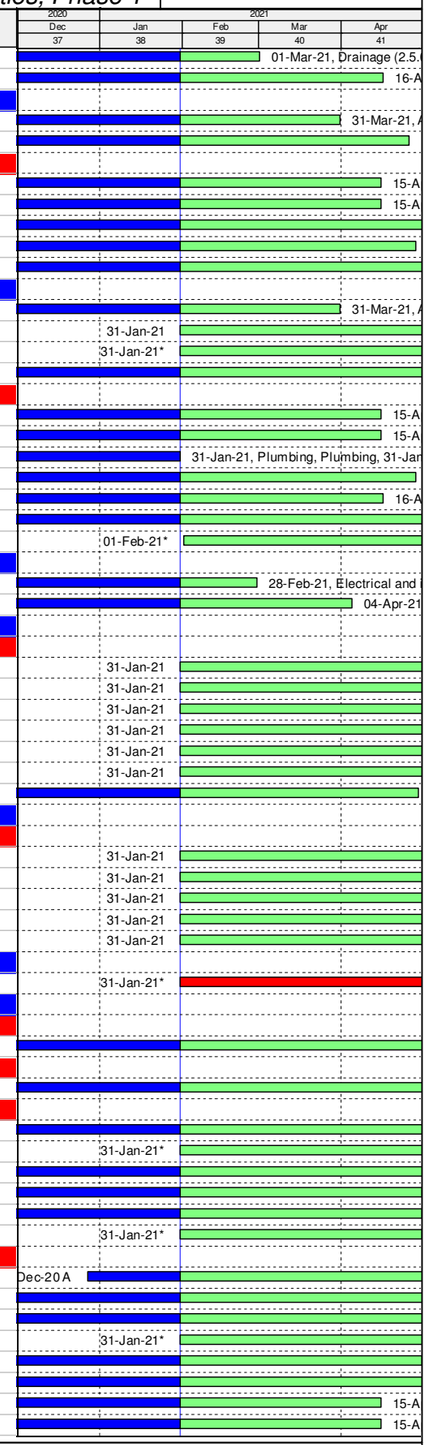


Remaining Work
Actual Work
Critical Remaining Work
Milestone
Actual Milestone
Critical Milestone

Activity ID	Activity Name	Original Duration	At Completion Duration	Duration % Complete	Activity % Complete	Remaining Duration	Primary Constraint	Actual Start	Actual Finish	Current Start	Current Finish	Late Start	Late Finish	Total Float	M38 Remarks
05-3200-1(M34)	Design of Pipe / Utilities Trenches concept (2.10.06.09.01)	105	105	0%	0%	105	Start On	31-Jan-21*	15-May-21	31-Jan-21	15-May-21	16-Nov-21	28-Feb-22	289	
05-3200-2(M34)	Sitewide Utilities Trenches Design (2.10.06.09.02)	105	206	0%	5%	105	Start On	22-Oct-20 A	15-May-21	31-Jan-21	15-May-21	16-Nov-21	28-Feb-22	289	
05-3840 (M22)	Automatic Traffic Control System (ATCS) (2.10.06.12)	90	90	0%	0%	90		31-Jan-21	30-Apr-21	31-Jan-21	30-Apr-21	24-Jun-21	21-Sep-21	144	
EP_SP_66_12-WP5A-M38.05.01.10.7	Utility ducts/Pipebridges design (2.10.25)	303	311	70.3%		90		24-Jun-20 A	30-Apr-21	31-Jan-21	30-Apr-21	16-Feb-21	03-Sep-21	126	
05-2460	Design of Pipe / Utilities Trenches concept	90	246	0%	5%	90		28-Aug-20 A	30-Apr-21	31-Jan-21	30-Apr-21	06-Jun-21	03-Sep-21	126	
05-2470	Utility ducts network	90	246	0%	5%	90		28-Aug-20 A	30-Apr-21	31-Jan-21	30-Apr-21	06-Jun-21	03-Sep-21	126	
05-2480	Pipebridge network - Layout	120	216	50%	5%	60		28-Aug-20 A	31-Mar-21	31-Jan-21	31-Mar-21	16-Feb-21	16-Apr-21	16	
05-2490	Pipebridge network - Foundation Plan	135	281	55.56%	5%	60		24-Jun-20 A	31-Mar-21	31-Jan-21	31-Mar-21	16-Feb-21	16-Apr-21	16	
05-2500	Pipebridge network - Structure Plan	135	281	55.56%	5%	60		24-Jun-20 A	31-Mar-21	31-Jan-21	31-Mar-21	16-Feb-21	16-Apr-21	16	
EP_SP_66_12-WP5A-M38.05.01.11	AIP Architectural, Finishes and Landscaping Works (2.11)	303	487	40.59%		180		30-Mar-20 A	29-Jul-21	31-Jan-21	29-Jul-21	04-Feb-21	22-May-22	297	
EP_SP_66_12-WP5A-M38.05.01.11.1	External and internal finishes design for Incineration Plant Buildings (2.11.01)	229	444	40.17%		137		30-Mar-20 A	16-Jun-21	31-Jan-21	16-Jun-21	01-Jul-21	11-Apr-22	298	
05-2510	External and internal finishes design for Incineration Plant Building (6 Packages)	137	409	0%	5%	137	Start On	04-May-20	16-Jun-21	31-Jan-21	16-Jun-21	27-Aug-21	11-Jan-22	208	
05-2520	External and internal finishes design for ACC Equipment Structure	137	137	0%	0%	137	Start On	31-Jan-21*	16-Jun-21	31-Jan-21	16-Jun-21	01-Jul-21	15-Nov-21	151	
05-2530	External and internal finishes design for Turbine Hall Building (3 Packages)	137	409	0%	5%	137	Start On	04-May-20	16-Jun-21	31-Jan-21	16-Jun-21	25-Nov-21	11-Apr-22	298	
05-2540	External and internal finishes design for Air Compressor Building (3 Packages)	137	409	0%	5%	137	Start On	04-May-20	16-Jun-21	31-Jan-21	16-Jun-21	09-Nov-21	25-Mar-22	282	
05-2550	External and internal finishes design for Chimney (6 Packages)	137	137	0%	0%	137	Start On	31-Jan-21*	16-Jun-21	31-Jan-21	16-Jun-21	26-Oct-21	12-Mar-22	268	
05-2560	External and internal finishes design for Reception Pavilion (5 Packages)	137	444	0%	5%	137	Start On	30-Mar-20 A	16-Jun-21	31-Jan-21	16-Jun-21	26-Oct-21	12-Mar-22	268	
EP_SP_66_12-WP5A-M38.05.01.11.2	External and internal finishes design for MT Plant Building (2.11.02)	136	415	0%		136		27-Apr-20 A	15-Jun-21	31-Jan-21	15-Jun-21	03-Oct-21	15-Feb-22	245	
05-2570	External and internal finishes design for MT Plant Building (7 Packages)	136	415	0%	5%	136	Start On	27-Apr-20 A	15-Jun-21	31-Jan-21	15-Jun-21	03-Oct-21	15-Feb-22	245	
EP_SP_66_12-WP5A-M38.05.01.11.3	External and internal finishes design for the Wastewater Treatment Plant (2.11.03)	135	135	0%		135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	04-Oct-21	15-Feb-22	246	
05-2580	External and internal finishes design for the Wastewater Treatment Plant (3 Packages)	135	135	0%	0%	135	Start On	31-Jan-21*	14-Jun-21	31-Jan-21	14-Jun-21	04-Oct-21	15-Feb-22	246	
EP_SP_66_12-WP5A-M38.05.01.11.4	External and internal finishes design for the Water Treatment Plant Building (2.11.04)	135	135	0%		135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	04-Oct-21	15-Feb-22	246	
05-2590	External and internal finishes design for the Water Treatment Plant Building (3 Packages)	135	135	0%	0%	135	Start On	31-Jan-21*	14-Jun-21	31-Jan-21	14-Jun-21	04-Oct-21	15-Feb-22	246	
EP_SP_66_12-WP5A-M38.05.01.11.5	External and internal finishes design for the Administration Building (2.11.05)	135	414	0%		135		27-Apr-20 A	14-Jun-21	31-Jan-21	14-Jun-21	03-Jan-22	18-May-22	337	
05-2600	External and internal finishes design for the Administration Building (6 Packages)	135	414	0%	5%	135	Start On	27-Apr-20 A	14-Jun-21	31-Jan-21	14-Jun-21	03-Jan-22	18-May-22	337	
EP_SP_66_12-WP5A-M38.05.01.11.6	External and internal finishes design for the IWMF Substation (2.11.06)	135	382	44.44%		75		30-Mar-20 A	15-Apr-21	31-Jan-21	15-Apr-21	04-Feb-21	19-Apr-21	4	
05-2610	External and internal finishes design for the IWMF Substation (4 Packages)	135	382	44.44%	5%	75	Start On	30-Mar-20 A	15-Apr-21	31-Jan-21	15-Apr-21	04-Feb-21	19-Apr-21	4	
EP_SP_66_12-WP5A-M38.05.01.11.7	Landscape masterplan (2.11.07)	303	448	40.59%		180		08-May-20	29-Jul-21	31-Jan-21	29-Jul-21	24-Nov-21	22-May-22	297	
05-2620	Water Feature (2.11.07.01)	105	406	0%	5%	105	Start On	19-Jun-20 A	29-Jul-21	16-Apr-21	29-Jul-21	24-Nov-21	08-Mar-22	222	
05-2630	Planting details	105	105	0%	0%	105	Start On	16-Apr-21*	29-Jul-21	16-Apr-21	29-Jul-21	24-Nov-21	08-Mar-22	222	
05-2920_1(M34)	Turbine Hall Building (2.11.07.04)	105	448	0%	5%	105		08-May-20	29-Jul-21	16-Apr-21	29-Jul-21	07-Feb-22	22-May-22	297	
05-2920_2(M34)	Reception Pavilion (2.11.07.06)	105	373	0%	5%	105		08-May-20	15-May-21	31-Jan-21	15-May-21	07-Feb-22	22-May-22	372	
05-2920_3(M34)	MT Plant Building and Water Treatment Plant Building (2.11.07.07)	105	448	0%	5%	105		08-May-20	29-Jul-21	16-Apr-21	29-Jul-21	07-Feb-22	22-May-22	297	
05-2920_4(M34)	Administration Building (2.11.07.08)	105	448	0%	5%	105		08-May-20	29-Jul-21	16-Apr-21	29-Jul-21	07-Feb-22	22-May-22	297	
05-2920_5(M34)	IWMF Substation (2.11.07.09)	105	448	0%	5%	105		08-May-20	29-Jul-21	16-Apr-21	29-Jul-21	07-Feb-22	22-May-22	297	
05-2920_6(M34)	Process Building (2.11.07.10)	105	448	0%	5%	105		08-May-20	29-Jul-21	16-Apr-21	29-Jul-21	07-Feb-22	22-May-22	297	
EP_SP_66_12-WP5A-M38.05.01.11.8	Architectural Detailing - Site Wide (2.11.29)	107	107	0%		107		31-Jan-21	17-May-21	31-Jan-21	17-May-21	31-May-21	14-Sep-21	120	
05-2640	Architectural Detailing - Site Wide Concept	107	107	0%	0%	107	Start On	31-Jan-21*	17-May-21	31-Jan-21	17-May-21	31-May-21	14-Sep-21	120	
EP_SP_66_12-WP5A-M38.05.01.11.9	External and internal finishes design for Elavated Driveway	137	137	0%		137		31-Jan-21	16-Jun-21	31-Jan-21	16-Jun-21	01-Oct-21	14-Feb-22	243	
05-5410	External and internal finishes design for Elavated Driveway	137	137	0%	0%	137	Start On	31-Jan-21*	16-Jun-21	31-Jan-21	16-Jun-21	01-Oct-21	14-Feb-22	243	
EP_SP_66_12-WP5A-M38.05.01.12	AIP Testing and Commissioning (2.12)	686	876	66.91%		227		23-Apr-19 A	14-Sep-21	31-Jan-21	14-Sep-21	28-Feb-21	30-Aug-23	715	
05-2650-1(5)	Factory Acceptance Testing plan (2.12.01.02-06) (7 Packages)	60	876	0%	0%	227		23-Apr-19 A	14-Sep-21	31-Jan-21	14-Sep-21	27-Apr-21	09-Dec-21	86	
05-2660	Site Acceptance Testing plan (2.12.02)	75	75	0%	0%	75	Start On	31-Jan-21*	15-Apr-21	31-Jan-21	15-Apr-21	28-Feb-21	13-May-21	28	
05-2670	System commissioning plan (2.12.03)	105	105	0%	0%	105	Start On	31-Jan-21*	15-May-21	31-Jan-21	15-May-21	29-May-21	10-Sep-21	118	
05-2680	Plant commissioning plan (2.12.04)	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	18-May-23	30-Aug-23	837	
EP_SP_66_12-WP5A-M38.05.01.13	AIP Transportation Facilities for the Operation (2.13)	136	321	22.79%		105		29-Jun-20 A	15-May-21	31-Jan-21	15-May-21	18-May-21	10-Sep-21	118	
05-2690	Design of vehicles for MSW and Ash and Residues delivery (2.13.01)	105	321	0%	5%	105		29-Jun-20 A	15-May-21	31-Jan-21	15-May-21	29-May-21	10-Sep-21	118	
05-2700	Design of marine vessels for the use of the Employer and visitors (2.13.02)	105	250	0%	5%	105		08-Sep-20 A	15-May-21	31-Jan-21	15-May-21	18-May-21	30-Aug-21	107	
EP_SP_66_12-WP5A-M38.05.01.14	AIP Miscellaneous Works (2.14)	258	375	35.66%		166		06-Jul-20 A	15-Jul-21	31-Jan-21	15-Jul-21	20-Jul-21	09-May-24	1029	
05-2710	Design of process related CCTV and existing onshore crane replacement works at Portion 2 (2.14.01)	105	105	0%	0%	105	Start On	02-Apr-21*	15-Jul-21	02-Apr-21	15-Jul-21	26-Jan-24	09-May-24	1029	
05-2720	Design of visitors and environmental education facilities (2.14.02)	105	314	0%	5%	105		06-Jul-20 A	15-May-21	31-Jan-21	15-May-21	20-Jul-21	01-Nov-21	170	
EP_SP_66_12-WP5A-M38.05.01.15	AIP Miscellaneous Detailing (2.15)	105	105	0%		105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	27-Feb-21	09-Sep-21	117	
05-2730	Covered walkway at passenger berth (2.15.02)	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	27-Feb-21	11-Jun-21	27	
05-2750	Weighbridge office (2.15.04)	105	105	0%	0%	105	Start On	31-Jan-21*	15-May-21	31-Jan-21	15-May-21	28-May-21	09-Sep-21	117	
EP_SP_66_12-WP5A-M38.05.01.16	AIP Auxiliary Plant Systems (2.16)	227	398	40.53%		135		13-May-20	14-Jun-21	31-Jan-21	14-Jun-21	01-May-21	26-Jul-22	407	
05-2770	Vehicle Fuel Filling Station (2.16.02)	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	27-Jan-22	10-Jun-22	361	
05-2780	Stores systems (2.16.03)	135	135	0%	0%	135	Start On	31-Jan-21*	14-Jun-21	31-Jan-21	14-Jun-21	14-Mar-22	26-Jul-22	407	
05-2780-1(5a)	IWMF Laboratory (2.16.04)	135	398	0%	5%	135		13-May-20	14-Jun-21	31-Jan-21	14-Jun-21	09-Sep-21	21-Jan-22	221	
05-2780-2(5a)	hoisting systems (2.16.09)	135	272	0%	5%	135		16-Sep-20 A	14-Jun-21	31-Jan-21	14-Jun-21	01-May-21	12-Sep-21	90	
EP_SP_66_12-WP5A-M38.05.02	DDA Design Package Submissions	969	1066	76.57%		227		15-Oct-18 A	14-Sep-21	31-Jan-21	14-Sep-21	29-Jan-21	16-Jun-23	640	
EP_SP_66_12-WP5A-M38.05.02.01	DDA Process and Layout Design (2.1)	324	833	47.22%		171		10-Apr-19 A	20-Jul-21	31-Jan-21	20-Jul-21	23-Feb-21	25-Aug-22	401	
EP_SP_66_12-WP5A-M38.05.02.01.1	MSW treatment process design for incineration (2.1.13)	228	388	53.95%		105		23-Apr-20 A	15-May-21	31-Jan-21	15-May-21	23-Feb-21	14-Dec-21	213	
05-5090	Incineration System (2.1.13.01) (2 Packages)	105	199	86.67%	5%	14		30-Jul-20 A	13-Feb-21	31-Jan-21	13-Feb-21	28-Sep-21	11-Oct-21	240	
05-5100	Heat Recovery Boiler (2.1.13.02) (2 Packages)	105	297	86.67%	5%	14	Start On	23-Apr-20 A	13-Feb-21	31-Jan-21	13-Feb-21	28-Sep-21	11-Oct-21	240	
05-5110	Ash Cranes (2.1.13.04) (2 Packages)	105	69	86.67%	0%	14		07-Dec-20 A	13-Feb-21	31-Jan-21	13-Feb-21	25-Mar-21	07-Apr-21	53	
05-5120	Leachate Collection and Treatment (2.1.13.05) (2 Packages)	105	105	0%	0%	105	Start On	31-Jan-21*	15-May-21	31-Jan-21	15-May-21	01-Sep-21	14-Dec-21	213	

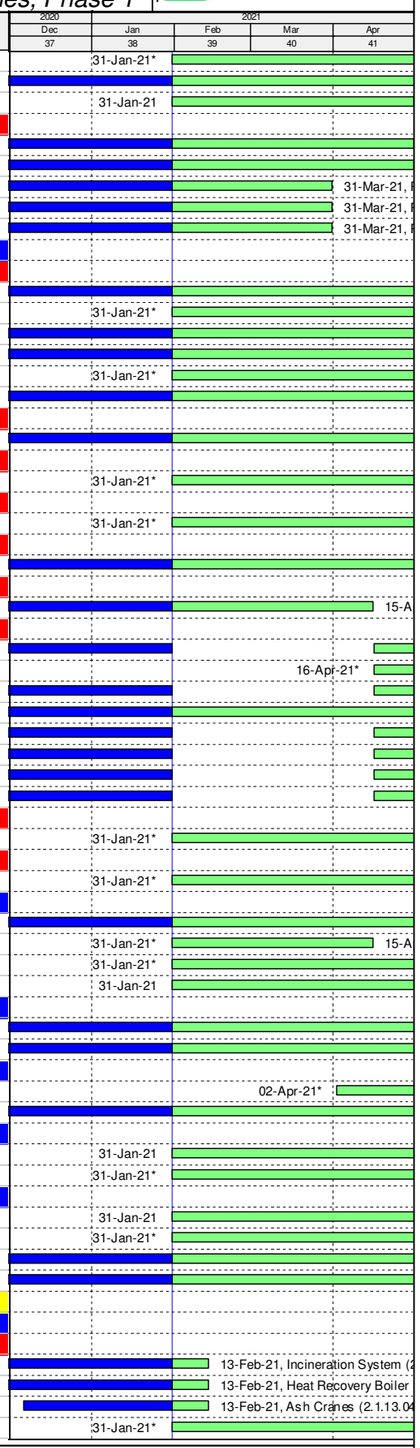


Remaining Work
Actual Work
Critical Remaining Work
Milestone
Actual Milestone
Critical Milestone

Activity ID	Activity Name	Original Duration	At Completion Duration	Duration % Complete	Activity % Complete	Remaining Duration	Primary Constraint	Actual Start	Actual Finish	Current Start	Current Finish	Late Start	Late Finish	Total Float	M38 Remarks
05-5130	Waste Water Treatment System (2.1.13.06) (2 Packages)	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	27-Aug-21	09-Dec-21	208	
05-5140	Overall Plan Water Scheme (2.1.13.07)	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	23-Feb-21	07-Jun-21	23	
05-5150	Boiler Feed Water System (2.1.13.03) (2 Packages)	105	216	66.67%	45%	35	Start On	03-Aug-20 A	06-Mar-21	31-Jan-21	06-Mar-21	10-Nov-21	14-Dec-21	283	
EP_SP_66_12-WP5A-M38.05.02.01.2 MSW treatment process design for mechanical treatment (2.1.14)		105	148	0%		105		19-Dec-20 A	15-May-21	31-Jan-21	15-May-21	08-Dec-21	22-Mar-22	311	
05-3510	Water Treatment Plant and Boiler Water Treatment (Demin Unit) Plant	105	148	0%	5%	105		19-Dec-20 A	15-May-21	31-Jan-21	15-May-21	08-Dec-21	22-Mar-22	311	
EP_SP_66_12-WP5A-M38.05.02.01.3 Waste heat recovery and Power generation system (2.1.15)		258	391	59.3%		105		20-Apr-20 A	15-May-21	31-Jan-21	15-May-21	26-Feb-21	08-Feb-22	269	
05-5220	Power Island (Steam Turbine Generator, Pressure Reducing and Desuperheating Station, Air Cooled Co	105	356	0%	5%	105		25-May-20	15-May-21	31-Jan-21	15-May-21	26-Feb-21	10-Jun-21	26	
05-5230	Closed Circuit Cooling Water System	105	391	0%	5%	105		20-Apr-20 A	15-May-21	31-Jan-21	15-May-21	27-Oct-21	08-Feb-22	269	
05-5240	Compressed Air Plants	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	27-Oct-21	08-Feb-22	269	
EP_SP_66_12-WP5A-M38.05.02.01.4 Flue gas treatment process design for incineration (2.1.16)		105	298	85.71%		15		23-Apr-20 A	14-Feb-21	31-Jan-21	14-Feb-21	12-Jun-21	11-Oct-21	239	
05-4660	Flue Gas Treatment System (2 Packages)	105	298	85.71%	5%	15	Start On	23-Apr-20 A	14-Feb-21	31-Jan-21	14-Feb-21	27-Sep-21	11-Oct-21	239	
05-4980	Boiler ash and APC residue handling and solidification (2 Packages)	105	298	85.71%	5%	15	Start On	23-Apr-20 A	14-Feb-21	31-Jan-21	14-Feb-21	12-Jun-21	26-Jun-21	132	
EP_SP_66_12-WP5A-M38.05.02.01.5 Logistic arrangement design for MSW and Ash and Residues (2.1.17)		258	314	59.3%		105		06-Jul-20 A	15-May-21	31-Jan-21	15-May-21	09-Mar-21	25-Aug-22	467	
05-4390	Weighbridge Systems	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	22-Jun-21	04-Oct-21	142	
05-4400	Waste Crane and Grapple System	105	239	71.43%	5%	30		06-Jul-20 A	01-Mar-21	31-Jan-21	01-Mar-21	09-Mar-21	07-Apr-21	37	
05-4410	Mechanical Shredder	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	13-May-22	25-Aug-22	467	
EP_SP_66_12-WP5A-M38.05.02.01.6 Site Master Layout Plan and Plant Layout (2.1.18)		105	105	0%		105		07-Apr-21	20-Jul-21	07-Apr-21	20-Jul-21	15-Apr-21	28-Jul-21	8	
05-3520	Site Master Layout Plan and Plant Layout	105	105	0%	0%	105		07-Apr-21	20-Jul-21	07-Apr-21	20-Jul-21	15-Apr-21	28-Jul-21	8	
EP_SP_66_12-WP5A-M38.05.02.01.7 Statutory Fire Compliance (2.1.26)		60	763	0%		92		10-Apr-19 A	11-May-21	09-Feb-21	11-May-21	25-Feb-21	27-May-21	16	
05-4420	Fire Safety Compliance	60	763	0%	0%	92		10-Apr-19 A	11-May-21	09-Feb-21	11-May-21	25-Feb-21	27-May-21	16	
EP_SP_66_12-WP5A-M38.05.02.02 DDA Ground Treatment, Reclamation, Seawall, Breakwater, Berth (2.2)		907	1004	81.81%		165		15-Oct-18 A	14-Jul-21	31-Jan-21	14-Jul-21	12-Feb-21	30-Sep-22	443	
05-3430-2(M37)	Geotechnical Interpretative Report (2.2.02.02)	105	974	0%	65%	135		15-Oct-18 A	14-Jun-21	31-Jan-21	14-Jun-21	12-Feb-21	26-Jun-21	12	
05-3450	Seawall design (2.2.20)	60	841	50%	65%	30		12-Nov-18 A	01-Mar-21	31-Jan-21	01-Mar-21	06-Mar-21	04-Apr-21	34	
05-3460	Breakwater design (2.2.21)	105	765	0%	65%	105		12-Apr-19 A	15-May-21	31-Jan-21	15-May-21	18-Jun-22	30-Sep-22	503	
05-3470	Berth design (2.2.22)	60	852	50%	65%	30		01-Nov-18 A	01-Mar-21	31-Jan-21	01-Mar-21	06-Mar-21	04-Apr-21	34	
05-3490	Onshore vessel power supply system (2.2.24)	135	135	0%	0%	135		02-Mar-21	14-Jul-21	02-Mar-21	14-Jul-21	23-May-21	04-Oct-21	82	
EP_SP_66_12-WP5A-M38.05.02.03 DDA Incineration Plant Buildings (2.3)		926	933	76.78%		215		13-Feb-19 A	02-Sep-21	31-Jan-21	02-Sep-21	29-Jan-21	24-Nov-22	448	
EP_SP_66_12-WP5A-M38.05.02.03.1 General Layout Drawings and Fire Saftey Strategy (2.3.25)		137	137	0%		137		28-Feb-21	14-Jul-21	28-Feb-21	14-Jul-21	30-May-21	15-Oct-21	93	
05-3290	Process Building	135	135	0%	0%	135		02-Mar-21	14-Jul-21	02-Mar-21	14-Jul-21	30-May-21	11-Oct-21	89	
05-3300	ACC Equipment Structure	135	135	0%	0%	135		28-Feb-21	12-Jul-21	28-Feb-21	12-Jul-21	03-Jun-21	15-Oct-21	95	
EP_SP_66_12-WP5A-M38.05.02.03.2 Foundation design (2.3.13)		137	137	0%		137		19-Apr-21	02-Sep-21	19-Apr-21	02-Sep-21	13-Oct-21	21-May-22	261	
05-3220	Process Building Waste Bunker, Tipping Hall, Basin Area and Workshop	137	137	0%	0%	137		19-Apr-21	02-Sep-21	19-Apr-21	02-Sep-21	13-Oct-21	27-Feb-22	177	
05-3230	ACC Equipment Structure	137	137	0%	0%	137		19-Apr-21	02-Sep-21	19-Apr-21	02-Sep-21	05-Jan-22	21-May-22	261	
EP_SP_66_12-WP5A-M38.05.02.03.3 Structural design (2.3.14)		281	437	32.74%		189		28-May-20	07-Aug-21	31-Jan-21	07-Aug-21	29-Jan-21	24-Nov-22	474	
05-5340	ACC Equipment Structure	180	180	0%	0%	180		31-Jan-21	29-Jul-21	31-Jan-21	29-Jul-21	29-Jan-21	27-Jul-21	-2	
05-5350	Turbin Hall Building (2.3.14.03)	189	189	0%	0%	189	Start On	31-Jan-21*	07-Aug-21	31-Jan-21	07-Aug-21	22-Apr-22	27-Oct-22	446	
05-5360	Compressor and CCCW Building	189	189	0%	0%	189	Start On	31-Jan-21*	07-Aug-21	31-Jan-21	07-Aug-21	12-Sep-21	19-Mar-22	224	
05-5380	Chimney, Elevated Drive Way and associated structures and Reception Pavilion	189	189	0%	0%	189	Start On	31-Jan-21*	07-Aug-21	31-Jan-21	07-Aug-21	20-May-22	24-Nov-22	474	
05-5390	Reception Pavilion Structural Design	189	437	0%	5%	189	Start On	28-May-20	07-Aug-21	31-Jan-21	07-Aug-21	01-Aug-21	06-Feb-22	182	
EP_SP_66_12-WP5A-M38.05.02.03.4 Electrical and instrumentation works design (2.3.15)		196	251	38.78%		120		22-Sep-20 A	30-May-21	31-Jan-21	30-May-21	04-Feb-21	07-Sep-21	100	
05-3360	11kV/380V Power Transformers and 11kV Earthing Transformer	105	206	28.57%	5%	75		22-Sep-20 A	15-Apr-21	31-Jan-21	15-Apr-21	04-Feb-21	19-Apr-21	4	
05-3370	E&IC Package 1 (Process Island)	120	120	0%	0%	120		31-Jan-21	30-May-21	31-Jan-21	30-May-21	09-Mar-21	06-Jul-21	37	
05-3380	E&IC Package 2 (Power Island)	165	159	27.27%	5%	120		23-Dec-20 A	30-May-21	31-Jan-21	30-May-21	11-May-21	07-Sep-21	100	
EP_SP_66_12-WP5A-M38.05.02.03.8 Operation Management System (2.3.15.04)		258	342	59.3%		105		08-Jun-20 A	15-May-21	31-Jan-21	15-May-21	15-Jan-22	29-Apr-22	349	
05-3390	Supervisory Control/Data Acquisition/ Distributed Control (SCADA/DCS) System (12 Packages)	105	342	0%	5%	105		08-Jun-20 A	15-May-21	31-Jan-21	15-May-21	15-Jan-22	29-Apr-22	349	
05-3420	Automatic License Plate and Container Recoginition System (ALPCRS)	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	15-Jan-22	29-Apr-22	349	
EP_SP_66_12-WP5A-M38.05.02.03.5 Mechanical works design (2.3.16)		926	823	88.66%		105		13-Feb-19 A	15-May-21	31-Jan-21	15-May-21	26-Feb-21	01-Jan-22	231	
EP_SP_66_12-WP5A-M38.05.02.03.5.1 Plant and Equipment		808	823	87%		105		13-Feb-19 A	15-May-21	31-Jan-21	15-May-21	26-Feb-21	11-Oct-21	149	
05-3580	Weighbridge Systems	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	22-Jun-21	04-Oct-21	142	
05-3590	Waste Crane and Grapple System	105	198	28.57%	5%	75		30-Sep-20 A	15-Apr-21	31-Jan-21	15-Apr-21	08-Apr-21	21-Jun-21	67	
05-3600	Mechanical Shredder	105	219	0%	0%	105		09-Oct-20 A	15-May-21	31-Jan-21	15-May-21	27-Mar-21	09-Jul-21	55	
05-3610	Incineration System (9 Packages)	105	753	66.67%	5%	35		13-Feb-19 A	06-Mar-21	31-Jan-21	06-Mar-21	07-Sep-21	11-Oct-21	219	
05-3620	Heat Recovery Boiler (8 Packages)	105	728	2%	5%	103		17-May-19	13-May-21	31-Jan-21	13-May-21	29-Mar-21	09-Jul-21	57	
05-3630	Boiler Feed Water Systems (4 Packages)	105	600	66.67%	5%	35		16-Jul-19 A	06-Mar-21	31-Jan-21	06-Mar-21	05-Jun-21	09-Jul-21	125	
05-3640	Ash cranes	105	266	71.43%	0%	30		09-Jun-20 A	01-Mar-21	31-Jan-21	01-Mar-21	09-Mar-21	07-Apr-21	37	
05-3650	Leachate collection and treatment	105	105	0%	0%	105	Start On	31-Jan-21*	15-May-21	31-Jan-21	15-May-21	27-Mar-21	09-Jul-21	55	
05-3790	Flue Gas Treatment System (12 Packages)	105	509	66.67%	5%	35		15-Oct-19 A	06-Mar-21	31-Jan-21	06-Mar-21	07-Sep-21	11-Oct-21	219	
05-3800	Boiler ash and APC residue handling and solidification	105	271	66.67%	5%	35	Start On	09-Jun-20 A	06-Mar-21	31-Jan-21	06-Mar-21	05-Jun-21	09-Jul-21	125	
05-3810	Steam Turbine Generator (STG) and Pressure Reducing and Desuperheating Station (PRDS)	105	290	0%	5%	105		30-Jul-20 A	15-May-21	31-Jan-21	15-May-21	26-Feb-21	10-Jun-21	26	
05-3820	Air cooled condenser	105	290	0%	5%	105		30-Jul-20 A	15-May-21	31-Jan-21	15-May-21	26-Feb-21	10-Jun-21	26	
05-3825(3)	Closed Circuit Cooling Water System	105	290	0%	5%	105		30-Jul-20 A	15-May-21	31-Jan-21	15-May-21	20-May-21	01-Sep-21	109	
EP_SP_66_12-WP5A-M38.05.02.03.5.2 Process Pipeworks (Incl. Ductworks) and Valves		442	731	76.24%		105		16-May-19	15-May-21	31-Jan-21	15-May-21	17-May-21	01-Jan-22	231	
05-3840	Process island (furnace-boiler-FGC)	105	708	21.9%	0%	82		16-May-19	22-Apr-21	31-Jan-21	22-Apr-21	12-Oct-21	01-Jan-22	254	
05-4350	Pipebridge A (Between Process island & Turbine Hall)	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	17-May-21	29-Aug-21	106	
05-4360	Compressed Air Plant area	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	03-Jul-21	15-Oct-21	153	
05-4370	Pipebridge B (Between CCCW Area & Turbine Hall)	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	17-May-21	29-Aug-21	106	

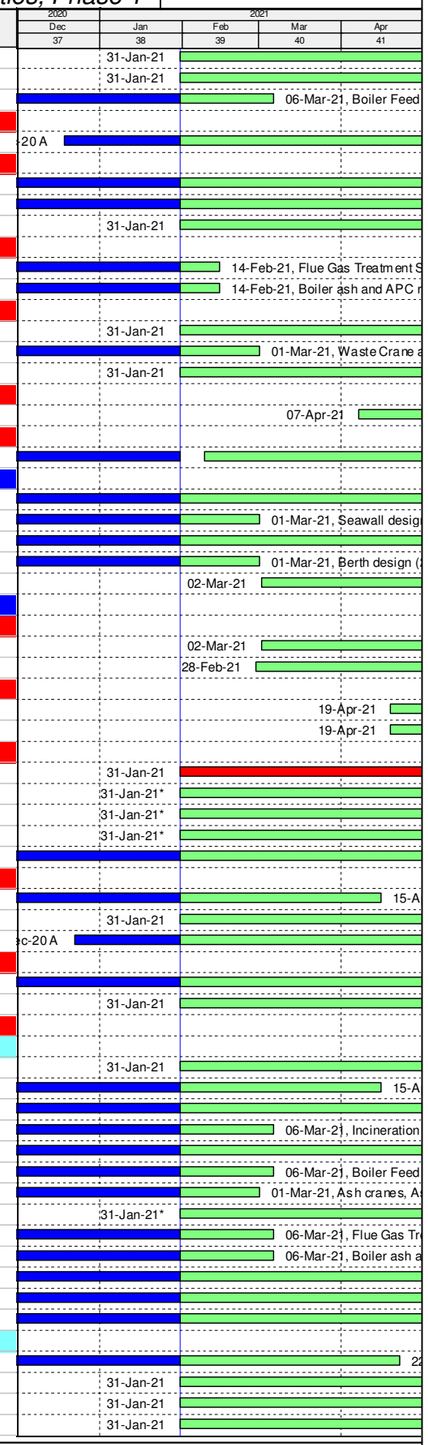


Remaining Work
Actual Work
Critical Remaining Work
Milestone
Actual Milestone
Critical Milestone

Activity ID	Activity Name	Original Duration	At Completion Duration	Duration % Complete	Activity % Complete	Remaining Duration	Primary Constraint	Actual Start	Actual Finish	Current Start	Current Finish	Late Start	Late Finish	Total Float	M38 Remarks
05-4380	Pipebridge C (Between Turbine Hall & ACC Yard)	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	17-May-21	29-Aug-21	106	
05-4950	Turbine Hall	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	27-May-21	08-Sep-21	116	
05-4970	CCCW Area	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	03-Jul-21	15-Oct-21	153	
EP_SP_66_12-WP5A-M38.05.02.03.5.3	**Process steel structure support (For eqipment, piping & duct, cable tray etc)**	712	653	85.25%		105		02-Aug-19 A	15-May-21	31-Jan-21	15-May-21	27-Mar-21	27-Oct-21	165	
05-3530	Process island (furnace-boiler-FGC) (3 Packages)	105	653	0%	25%	105		02-Aug-19 A	15-May-21	31-Jan-21	15-May-21	27-Mar-21	09-Jul-21	55	
05-3540	Pipebridge (Between Process island & Turbine Hall)	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	17-May-21	29-Aug-21	106	
05-3550	Turbine Hall	105	219	67.62%	0%	34		30-Jul-20 A	05-Mar-21	31-Jan-21	05-Mar-21	24-Sep-21	27-Oct-21	236	
05-3560	Pipebridge (Between CCCW Area & Turbine Hall)	105	261	0%	5%	105		28-Aug-20 A	15-May-21	31-Jan-21	15-May-21	17-May-21	29-Aug-21	106	
05-3570	Pipebridge (Between Turbine Hall & ACC Yard)	105	261	0%	5%	105		28-Aug-20 A	15-May-21	31-Jan-21	15-May-21	17-May-21	29-Aug-21	106	
EP_SP_66_12-WP5A-M38.05.02.03.5.4	**Equipment and piping insulation**	105	105	0%		105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	20-May-21	15-Oct-21	153	
05-4500	Incineration System	105	105	0%	0%	105	Start On	31-Jan-21*	15-May-21	31-Jan-21	15-May-21	29-Jun-21	11-Oct-21	149	
05-4510	Heat Recovery Boiler	105	105	0%	0%	105	Start On	31-Jan-21*	15-May-21	31-Jan-21	15-May-21	29-Jun-21	11-Oct-21	149	
05-4520	Boiler Feed Water Systems	105	105	0%	0%	105	Start On	31-Jan-21*	15-May-21	31-Jan-21	15-May-21	03-Jul-21	15-Oct-21	153	
05-4530	Flue Gas Treatment System	105	105	0%	0%	105	Start On	31-Jan-21*	15-May-21	31-Jan-21	15-May-21	29-Jun-21	11-Oct-21	149	
05-4540	Boiler ash and APC residue handling and solidification	105	105	0%	0%	105	Start On	31-Jan-21*	15-May-21	31-Jan-21	15-May-21	03-Jul-21	15-Oct-21	153	
05-4550	Steam Turbine Generator (STG) and Pressure Reducing and Desuperheating Station (PRDS)	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	29-Jun-21	11-Oct-21	149	
05-4560	Air cooled condenser	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	03-Jul-21	15-Oct-21	153	
05-4570	Closed Circuit Cooling Water System	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	20-May-21	01-Sep-21	109	
EP_SP_66_12-WP5A-M38.05.02.03.6	**Fire services installation design (2.3.17)**	105	105	0%		105		16-Apr-21	29-Jul-21	16-Apr-21	29-Jul-21	13-May-21	25-Aug-21	27	
05-3680	FS schematics	105	105	0%	0%	105		16-Apr-21	29-Jul-21	16-Apr-21	29-Jul-21	13-May-21	25-Aug-21	27	
EP_SP_66_12-WP5A-M38.05.02.03.7	**Building services design (excluding fire services installation design) (2.3.18)**	173	173	0%		173		27-Feb-21	18-Aug-21	27-Feb-21	18-Aug-21	15-Mar-21	29-Apr-22	254	
05-3700	MVAC (6 Packages)	135	135	0%	0%	135		06-Apr-21	18-Aug-21	06-Apr-21	18-Aug-21	05-Jul-21	16-Nov-21	90	
05-3770	Building Management System (BMS) ELV (7 Packages)	135	135	0%	0%	135		03-Apr-21	15-Aug-21	03-Apr-21	15-Aug-21	16-Dec-21	29-Apr-22	257	
05-3780-1(M20)	Water Cannon System	60	60	0%	0%	60		27-Feb-21	27-Apr-21	27-Feb-21	27-Apr-21	15-Mar-21	13-May-21	16	
EP_SP_66_12-WP5A-M38.05.02.04	**DDA Mechanical Treatment Plant Building (2.4)**	163	163	0%		163		01-Apr-21	10-Sep-21	01-Apr-21	10-Sep-21	26-May-21	16-Feb-22	159	
05-5160	Architectural Design (2.4.25)	105	105	0%	0%	105	Start On	01-Apr-21*	14-Jul-21	01-Apr-21	14-Jul-21	04-Nov-21	16-Feb-22	217	
EP_SP_66_12-WP5A-M38.05.02.04.7	**Building services design (excluding fire services installation design) (2.4.18)**	158	158	0%		158		06-Apr-21	10-Sep-21	06-Apr-21	10-Sep-21	26-May-21	16-Nov-21	67	
05-3860	MVAC	135	135	0%	0%	135		06-Apr-21	18-Aug-21	06-Apr-21	18-Aug-21	05-Jul-21	16-Nov-21	90	
05-3890	Drainage	135	135	0%	0%	135		28-Apr-21	10-Sep-21	28-Apr-21	10-Sep-21	26-May-21	07-Oct-21	27	
EP_SP_66_12-WP5A-M38.05.02.05	**DDA Wastewater Treatment Plant (2.5)**	211	211	0%		211		31-Jan-21	29-Aug-21	31-Jan-21	29-Aug-21	09-May-21	27-Feb-22	181	
05-3920	Architectural Design (2.5.25)	75	75	0%	0%	75	Start On	01-Apr-21*	14-Jun-21	01-Apr-21	14-Jun-21	11-Aug-21	24-Oct-21	132	
05-3930	Foundation design (2.5.13)	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	15-Oct-21	27-Feb-22	257	
05-3950	Electrical and instrumentation works design (2.5.15)	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	09-May-21	20-Sep-21	98	
EP_SP_66_12-WP5A-M38.05.02.05.7	**Building services design (excluding fire services installation design) (2.5.18)**	136	136	0%		136		16-Apr-21	29-Aug-21	16-Apr-21	29-Aug-21	20-Jul-21	06-Jan-22	130	
05-3990	MVAC	120	120	0%	0%	120		16-Apr-21	13-Aug-21	16-Apr-21	13-Aug-21	20-Jul-21	16-Nov-21	95	
05-4030	ELV	135	135	0%	0%	135		17-Apr-21	29-Aug-21	17-Apr-21	29-Aug-21	25-Aug-21	06-Jan-22	130	
EP_SP_66_12-WP5A-M38.05.02.06	**DDA Water Treatment Plant Building (2.6)**	223	223	0%		223		31-Jan-21	10-Sep-21	31-Jan-21	10-Sep-21	28-Mar-21	16-Jun-22	279	
05-4050	Architectural Design (2.6.25)	105	105	0%	0%	105		01-Apr-21	14-Jul-21	01-Apr-21	14-Jul-21	04-Mar-22	16-Jun-22	337	
05-4060	Foundation design (2.6.13)	180	180	0%	0%	180		31-Jan-21	29-Jul-21	31-Jan-21	29-Jul-21	28-Mar-21	23-Sep-21	56	
05-4080	Electrical and instrumentation works design (2.6.15)	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	08-Jun-21	20-Sep-21	128	
05-4090	Mechanical works design (2.6.16)	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	08-Jun-21	20-Sep-21	128	
05-4100	Fire services installation design (2.6.17)	105	105	0%	0%	105		26-Apr-21	09-Aug-21	26-Apr-21	09-Aug-21	13-May-21	25-Aug-21	17	
EP_SP_66_12-WP5A-M38.05.02.06.7	**Building services design (excluding fire services installation design) (2.6.18)**	148	148	0%		148		16-Apr-21	10-Sep-21	16-Apr-21	10-Sep-21	26-May-21	06-Jan-22	118	
05-4110	Electrical Services and Lighting	135	135	0%	0%	135		16-Apr-21	28-Aug-21	16-Apr-21	28-Aug-21	25-Aug-21	06-Jan-22	131	
05-4120	MVAC	135	135	0%	0%	135		16-Apr-21	28-Aug-21	16-Apr-21	28-Aug-21	05-Jul-21	16-Nov-21	80	
05-4150	Drainage	135	135	0%	0%	135		28-Apr-21	10-Sep-21	28-Apr-21	10-Sep-21	26-May-21	07-Oct-21	27	
EP_SP_66_12-WP5A-M38.05.02.07	**DDA Administration Building (2.7)**	163	163	0%		163		01-Apr-21	10-Sep-21	01-Apr-21	10-Sep-21	26-May-21	14-Feb-22	157	
05-4170	Architectural Design (2.7.21)	105	105	0%	0%	105	Start On	01-Apr-21*	14-Jul-21	01-Apr-21	14-Jul-21	01-Nov-21	14-Feb-22	214	
EP_SP_66_12-WP5A-M38.05.02.07.6	**Building services design (excluding fire services installation design) (2.7.15)**	148	148	0%		148		16-Apr-21	10-Sep-21	16-Apr-21	10-Sep-21	26-May-21	06-Jan-22	118	
05-4220	Electrical Services and Lighting	135	135	0%	0%	135		16-Apr-21	28-Aug-21	16-Apr-21	28-Aug-21	25-Aug-21	06-Jan-22	131	
05-4230	MVAC	135	135	0%	0%	135		16-Apr-21	28-Aug-21	16-Apr-21	28-Aug-21	05-Jul-21	16-Nov-21	80	
05-4250	Plumbing	135	135	0%	0%	135		16-Apr-21	28-Aug-21	16-Apr-21	28-Aug-21	26-May-21	07-Oct-21	40	
05-4260	Drainage	135	135	0%	0%	135		28-Apr-21	10-Sep-21	28-Apr-21	10-Sep-21	26-May-21	07-Oct-21	27	
05-4270	ELV	135	135	0%	0%	135		17-Apr-21	29-Aug-21	17-Apr-21	29-Aug-21	25-Aug-21	06-Jan-22	130	
EP_SP_66_12-WP5A-M38.05.02.08	**DDA IWMF Substation (2.8)**	208	539	3.85%		200		27-Feb-20 A	18-Aug-21	31-Jan-21	18-Aug-21	13-Apr-21	05-May-22	260	
05-4290	Architectural Design (2.8.25)	105	105	0%	0%	105	Start On	31-Jan-21*	15-May-21	31-Jan-21	15-May-21	22-Apr-21	04-Aug-21	81	
05-4300	Foundation design (2.8.13)	200	200	0%	0%	200		31-Jan-21	18-Aug-21	31-Jan-21	18-Aug-21	16-Jul-21	31-Jan-22	166	
05-4310	Structural design (2.8.14)	195	534	0%	5%	195		27-Feb-20 A	13-Aug-21	31-Jan-21	13-Aug-21	23-Oct-21	05-May-22	265	
05-4320	Electrical and instrumentation works design (2.8.15)	135	135	0%	0%	135		01-Mar-21	13-Jul-21	01-Mar-21	13-Jul-21	02-Dec-21	15-Apr-22	276	
05-4340	Fire services installation design (2.8.17)	135	135	0%	0%	135		05-Apr-21	17-Aug-21	05-Apr-21	17-Aug-21	13-Apr-21	25-Aug-21	8	
EP_SP_66_12-WP5A-M38.05.02.08.7	**Building services design (excluding fire services installation design) (2.8.18)**	135	135	0%		135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	26-May-21	29-Apr-22	319	
05-4990	Electrical Services and Lighting	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	25-Aug-21	06-Jan-22	206	
05-5000	MVAC	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	05-Jul-21	16-Nov-21	155	
05-5010	Plumbing	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	26-May-21	07-Oct-21	115	
05-5020	Drainage	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	26-May-21	07-Oct-21	115	
05-5030	ELV	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	25-Aug-21	06-Jan-22	206	

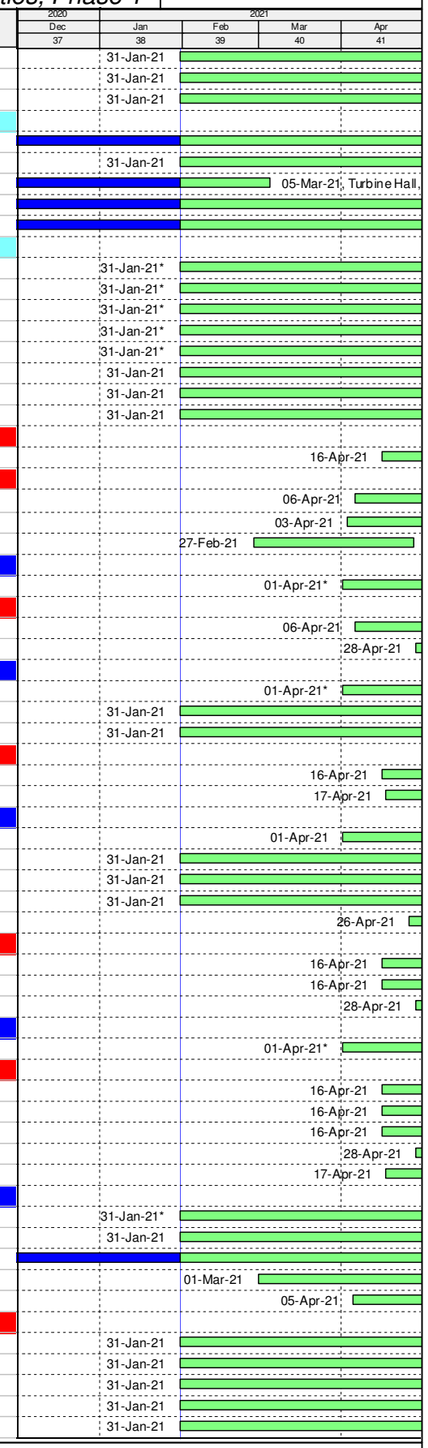


Remaining Work
Actual Work
Critical Remaining Work
Milestone
Actual Milestone
Critical Milestone

Activity ID	Activity Name	Original Duration	At Completion Duration	Duration % Complete	Activity % Complete	Remaining Duration	Primary Constraint	Acrtual Start	Actual Finish	Currect Start	Current Finish	Late Start	Late Finish	Total Float	M38 Remarks
05-5030-1(M20)	Building Management System (BMS)	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	16-Dec-21	29-Apr-22	319	
EP_SP_66_12-WP5A-M38.05.02.10 DDA Roads and Utilities (2.10)		195	195	0%		195		31-Jan-21	13-Aug-21	31-Jan-21	13-Aug-21	17-Apr-21	16-Jun-23	672	
EP_SP_66_12-WP5A-M38.05.02.10.1 Permanent road works layout on the Artificial Island (2.10.13)		135	135	0%		135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	20-Sep-22	16-Jun-23	732	
05-4470	Roads and hardstandings layout	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	20-Sep-22	01-Feb-23	597	
05-4480	Road signage and markings	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	02-Feb-23	16-Jun-23	732	
EP_SP_66_12-WP5A-M38.05.02.10.2 Sewerage design on the Artificial Island (2.10.14)		135	135	0%		135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	26-May-21	07-Oct-21	115	
05-4430	Foul Sewerage	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	26-May-21	07-Oct-21	115	
EP_SP_66_12-WP5A-M38.05.02.10.3 Drainage system design on the Artificial Island (2.10.15)		135	135	0%		135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	26-May-21	07-Oct-21	115	
05-5310	Surface water Drainage System	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	26-May-21	07-Oct-21	115	
EP_SP_66_12-WP5A-M38.05.02.10.4 Water supply system design on the Artificial Island (2.10.16)		135	135	0%		135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	26-May-21	20-Aug-22	432	
05-5250	Potable Water Distribution System	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	08-Apr-22	20-Aug-22	432	
05-5260	Recycled Water System	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	08-Apr-22	20-Aug-22	432	
05-5270	Irrigation System	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	26-May-21	07-Oct-21	115	
05-5300-1(M24)	E&M system for seawater intake and brine discharge (2.10.04.07)	90	90	0%	0%	90		02-Mar-21	30-May-21	02-Mar-21	30-May-21	01-Sep-21	29-Nov-21	183	
EP_SP_66_12-WP5A-M38.05.02.10.6 Design of telecommunication and other utilities (2.10.18)		135	135	0%		135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	23-Apr-21	05-Aug-22	417	
05-4590	Site Lighting Concept / Schematics	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	24-Mar-22	05-Aug-22	417	
05-4600	Lightning Protection System concept / schematics	135	135	0%	0%	135		31-Jan-21	14-Jun-21	31-Jan-21	14-Jun-21	23-Apr-21	04-Sep-21	82	
EP_SP_66_12-WP5A-M38.05.02.10.7 Utility ducts/Pipebridges design (2.10.26)		135	135	0%		135		01-Apr-21	13-Aug-21	01-Apr-21	13-Aug-21	17-Apr-21	29-Aug-21	16	
05-5060	Pipebridge network - Layout	135	135	0%	0%	135		01-Apr-21	13-Aug-21	01-Apr-21	13-Aug-21	17-Apr-21	29-Aug-21	16	
05-5070	Pipebridge network - Foundation Plan	135	135	0%	0%	135		01-Apr-21	13-Aug-21	01-Apr-21	13-Aug-21	17-Apr-21	29-Aug-21	16	
05-5080	Pipebridge network - Structure Plan	135	135	0%	0%	135		01-Apr-21	13-Aug-21	01-Apr-21	13-Aug-21	17-Apr-21	29-Aug-21	16	
EP_SP_66_12-WP5A-M38.05.02.11 DDA Architectural, Finishes and Landscaping Works (2.11)		167	167	0%		167		02-Mar-21	15-Aug-21	02-Mar-21	15-Aug-21	05-Apr-21	11-May-22	268	
EP_SP_66_12-WP5A-M38.05.02.11.1 External and internal finishes design for Incineration Plant Buildings (2.11.15)		137	137	0%		137		02-Mar-21	16-Jul-21	02-Mar-21	16-Jul-21	26-Sep-21	11-May-22	298	
05-4670	External and internal finishes design for Incineration Plant Building (13 Packages)	137	137	0%	0%	137	Start On	02-Mar-21*	16-Jul-21	02-Mar-21	16-Jul-21	26-Sep-21	10-Feb-22	208	
05-4690	External and internal finishes design for Turbine Hall Building (7 Packages)	137	137	0%	0%	137	Start On	02-Mar-21*	16-Jul-21	02-Mar-21	16-Jul-21	25-Dec-21	11-May-22	298	
05-4700	External and internal finishes design for Air Compressor Building (7 Packages)	137	137	0%	0%	137	Start On	02-Mar-21*	16-Jul-21	02-Mar-21	16-Jul-21	09-Dec-21	24-Apr-22	282	
05-4710	External and internal finishes design for Chimney (10 Packages)	137	137	0%	0%	137	Start On	02-Mar-21*	16-Jul-21	02-Mar-21	16-Jul-21	25-Nov-21	11-Apr-22	268	
05-4720	External and internal finishes design for Reception Pavilion (10 Packages)	137	137	0%	0%	137	Start On	02-Mar-21*	16-Jul-21	02-Mar-21	16-Jul-21	25-Nov-21	11-Apr-22	268	
EP_SP_66_12-WP5A-M38.05.02.11.6 External and internal finishes design for the IWMF Substation (2.11.20)		137	137	0%		137		01-Apr-21	15-Aug-21	01-Apr-21	15-Aug-21	05-Apr-21	19-Aug-21	4	
05-4770	External and internal finishes design for the IWMF Substation	137	137	0%	0%	137		01-Apr-21	15-Aug-21	01-Apr-21	15-Aug-21	05-Apr-21	19-Aug-21	4	
EP_SP_66_12-WP5A-M38.05.02.12 DDA Testing and Commissioning (2.12)		227	372	0%		227		08-Sep-20 A	14-Sep-21	31-Jan-21	14-Sep-21	14-May-21	18-Dec-21	95	
05-4810	Factory Acceptance Testing plan (2.12.09.01) (1 Packages)	60	60	0%	0%	60		31-Jan-21	31-Mar-21	31-Jan-21	31-Mar-21	20-Oct-21	18-Dec-21	262	
05-4810-1(5a)	Factory Acceptance Testing plan (2.12.09.02-07) (8 Packages)	60	372	0%	5%	60		08-Sep-20 A	14-Sep-21	17-Jul-21	14-Sep-21	11-Oct-21	09-Dec-21	86	
05-4820	Site Acceptance Testing plan (2.12.10)	105	105	0%	0%	105		16-Apr-21	29-Jul-21	16-Apr-21	29-Jul-21	14-May-21	26-Aug-21	28	
05-5430(M38)	Construction Plan for Prefabs 1-2-3 (2.12.09.07)	105	105	0%	0%	105		31-Jan-21	15-May-21	31-Jan-21	15-May-21	22-Jun-21	04-Oct-21	142	New Activity
EP_SP_66_12-WP5A-M38.06 Procurement of Major Equipment		1407	1662	49.96%		704		18-Jun-18 A	04-Jan-23	31-Jan-21	04-Jan-23	20-Jan-21	24-Dec-22	-11	
EP_SP_66_12-WP5A-M38.06.1 Off-site Fabrication of Incineration Modules		1407	1651	49.96%		704		29-Jun-18 A	04-Jan-23	31-Jan-21	04-Jan-23	20-Jan-21	24-Dec-22	-11	
EP_SP_66_12-WP5A-M38.06.1.25 Material Procurement		1003	1247	70.09%		300		29-Jun-18 A	26-Nov-21	31-Jan-21	26-Nov-21	09-Mar-21	02-Jan-22	37	
06-1000-1(1)	Mechanical Equipment Material Submission and Approval	180	942	97.22%	97.22%	5		09-Jul-18 A	04-Feb-21	31-Jan-21	04-Feb-21	05-Apr-21	09-Apr-21	64	
06-1000-2(1)	Pipe Material Submission and Approval	90	465	94.44%	92%	5		29-Oct-19 A	04-Feb-21	31-Jan-21	04-Feb-21	05-Apr-21	09-Apr-21	64	
06-1000-3(1)	Electircal and Instrumentation Material Submission and Approval	90	90	0%	0%	90		31-Jan-21	30-Apr-21	31-Jan-21	30-Apr-21	09-Mar-21	06-Jun-21	37	
06-1010-1(1)	Mechanical Equipment Procurement (incl. FAT)	360	1041	74%	74%	94		29-Jun-18 A	04-May-21	31-Jan-21	04-May-21	05-Jul-21	06-Oct-21	155	
06-1010-2(1)	Pipe Material Procurement (incl. FAT)	180	180	0%	0%	180		05-Feb-21	03-Aug-21	05-Feb-21	03-Aug-21	10-Apr-21	06-Oct-21	64	
06-1010-3(1)	Electircal and Instrumentation Material Procurement (Incl. FAT)	300	300	0%	0%	300		31-Jan-21	26-Nov-21	31-Jan-21	26-Nov-21	09-Mar-21	02-Jan-22	37	
EP_SP_66_12-WP5A-M38.06.1.26 Fabrication of Module		1041	1046	32.37%		704		24-Feb-20 A	04-Jan-23	31-Jan-21	04-Jan-23	20-Jan-21	24-Dec-22	-11	
06-1010-4(5a)	Perparation Works for Steel Support Frame	180	347	97.22%	97.22%	5		24-Feb-20 A	04-Feb-21	31-Jan-21	04-Feb-21	20-Jan-21	24-Jan-21	-11	
06-1020-1(1)	Erection of Steel Support Frame	669	671	20.33%	20.33%	533		15-Sep-20 A	17-Jul-22	31-Jan-21	17-Jul-22	20-Jan-21	06-Jul-22	-11	
06-1020-2(1)	Mechancial Installation Works	584	584	0%	0%	584		31-Jan-21	06-Sep-22	31-Jan-21	06-Sep-22	20-Jan-21	26-Aug-22	-11	
06-1020-3(1)	Piping and Instrumentation Installation Works	650	650	0%	0%	650		31-Jan-21	11-Nov-22	31-Jan-21	11-Nov-22	20-Jan-21	31-Oct-22	-11	
06-1020-4(1)	Electrcal Installation Works	704	704	0%	0%	704		31-Jan-21	04-Jan-23	31-Jan-21	04-Jan-23	20-Jan-21	24-Dec-22	-11	
EP_SP_66_12-WP5A-M38.06.2 Off-site Fabrication of Turbine Modules		484	1289	31.61%		331		18-Jun-18 A	27-Dec-21	31-Jan-21	27-Dec-21	11-Feb-21	06-Apr-22	100	
EP_SP_66_12-WP5A-M38.06.2.1 Material Procurement		484	1289	31.61%		331		18-Jun-18 A	27-Dec-21	31-Jan-21	27-Dec-21	03-Jun-21	06-Apr-22	100	
06-1050-2(1)	Pipe Material Submission and Approval	90	90	0%	0%	90		15-Feb-21	15-May-21	15-Feb-21	15-May-21	11-Jun-21	08-Sep-21	116	
06-1050-3(1)	Electircal and Instrumentation Material Submission and Approval	90	90	0%	0%	90		02-Apr-21	30-Jun-21	02-Apr-21	30-Jun-21	11-Jul-21	08-Oct-21	100	
06-1060-1(1)	Mechanical Equipment Procurement (Incl. FAT)	350	1086	63.43%	63.43%	128		18-Jun-18 A	07-Jun-21	31-Jan-21	07-Jun-21	03-Jun-21	08-Oct-21	123	
06-1060-2(1)	Pipe Material Procurement (Incl. FAT)	180	180	0%	0%	180		15-Feb-21	13-Aug-21	15-Feb-21	13-Aug-21	11-Jun-21	07-Dec-21	116	
06-1060-3(1)	Electircal and Instrumentation Material Procurement (Incl. FAT)	300	300	0%	0%	300		03-Mar-21	27-Dec-21	03-Mar-21	27-Dec-21	11-Jun-21	06-Apr-22	100	
EP_SP_66_12-WP5A-M38.06.2.2 Fabrication of Module		120	120	0%		120		31-Jan-21	30-May-21	31-Jan-21	30-May-21	11-Feb-21	10-Jun-21	11	
06-1070-1(1)	Erection of Steel Support Frame	120	120	0%	0%	120		31-Jan-21	30-May-21	31-Jan-21	30-May-21	11-Feb-21	10-Jun-21	11	
EP_SP_66_12-WP5A-M38.06.3 Procurement for ACC Units		200	200	0%		200		31-Jan-21	18-Aug-21	31-Jan-21	18-Aug-21	08-Feb-21	26-Aug-21	8	
06-1110	Material & Equipment Procurement	200	200	0%	0%	200		31-Jan-21	18-Aug-21	31-Jan-21	18-Aug-21	08-Feb-21	26-Aug-21	8	
EP_SP_66_12-WP5A-M38.06.4 Procurement for MT Plant Equipment		180	180	0%		180		31-Jan-21	29-Jun-21	31-Jan-21	29-Jul-21	23-Apr-21	19-Oct-21	82	
06-1150-1(1)	Mechanical Equipment Material Submission and Approval	180	180	0%	0%	180		31-Jan-21	29-Jul-21	31-Jan-21	29-Jul-21	23-Apr-21	19-Oct-21	82	
EP_SP_66_12-WP5A-M38.06.7 Procurement for HV Transformers and Associated Equipment		573	1027	18.85%		465		19-Jul-19 A	10-May-22	31-Jan-21	10-May-22	11-Jun-21	12-Aug-22	94	
EP_SP_66_12-WP5A-M38.06.7.1 Procurement of Transformers & EDG		550	1027	38.55%		338		19-Jul-19 A	10-May-22	07-Jun-21	10-May-22	11-Jun-21	14-May-22	4	

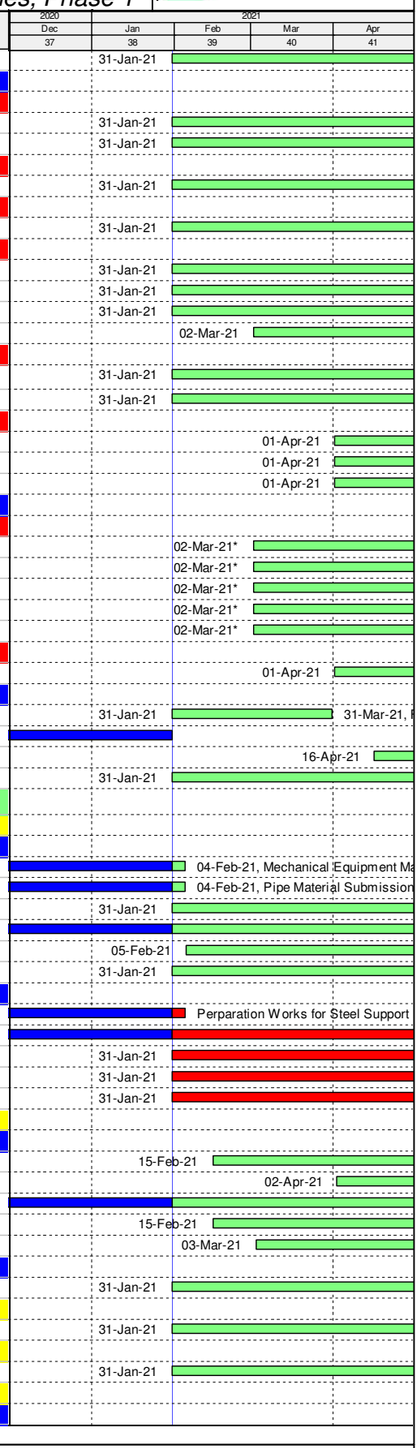

Remaining Work
Actual Work
Critical Remaining Work
Milestone
Actual Milestone
Critical Milestone

Activity ID	Activity Name	Original Duration	At Completion Duration	Duration % Complete	Activity % Complete	Remaining Duration	Primary Constraint	Acrtual Start	Actual Finish	Currect Start	Current Finish	Late Start	Late Finish	Total Float	M38 Remarks
06-1280(1)	Procurement of Transfromers	550	1027	38.55%	38.55%	338		19-Jul-19 A	10-May-22	07-Jun-21	10-May-22	11-Jun-21	14-May-22	4	
EP_SP_66_12-WP5A-M38.06.7.2 Procurement of Switchboard/Pannels and Cables		395	395	0%		395		31-Jan-21	01-Mar-22	31-Jan-21	01-Mar-22	14-Jul-21	12-Aug-22	164	
06-2090(1)	Material Submission and Approval	90	90	0%	0%	90		31-Jan-21	30-Apr-21	31-Jan-21	30-Apr-21	14-Jul-21	11-Oct-21	164	
06-2100(1)	Material & Equipment Procurement	335	335	0%	0%	335		01-Apr-21	01-Mar-22	01-Apr-21	01-Mar-22	12-Sep-21	12-Aug-22	164	
EP_SP_66_12-WP5A-M38.06.10 Procruement and Off-site Fabrication of Pipe Bridges (Incl. Pipings)		450	850	0%		450		09-Aug-20 A	06-Dec-22	13-Sep-21	06-Dec-22	29-Sep-21	22-Dec-22	16	
06-1400	Material & Equipment Procurement	450	850	0%	0%	450		09-Aug-20 A	06-Dec-22	13-Sep-21	06-Dec-22	29-Sep-21	22-Dec-22	16	
EP_SP_66_12-WP5A-M38.06.18 Procurement for Cranage Equipment		120	120	0%		120		02-Mar-21	29-Jun-21	02-Mar-21	29-Jun-21	08-Apr-21	05-Aug-21	37	
06-1710	Material Submission and Approval	120	120	0%	0%	120		02-Mar-21	29-Jun-21	02-Mar-21	29-Jun-21	08-Apr-21	05-Aug-21	37	
EP_SP_66_12-WP5A-M38.08 Maritime Works		762	928	74.14%		197		31-Jan-19 A	16-Aug-21	31-Jan-21	16-Aug-21	17-Jan-21	19-Nov-22	461	
EP_SP_66_12-WP5A-M38.08.1 Marine Construction		762	928	74.14%		197		31-Jan-19 A	16-Aug-21	31-Jan-21	16-Aug-21	17-Jan-21	19-Nov-22	461	
EP_SP_66_12-WP5A-M38.08.1.1 Phase I - Construction of Perimeter Seawalls		762	608	80.58%		148		29-Oct-19 A	27-Jun-21	31-Jan-21	27-Jun-21	06-Feb-21	03-Jul-21	6	
EP_SP_66_12-WP5A-M38.08.1.1.1 Seawall and Berth at DCM Area		762	608	80.58%		148		29-Oct-19 A	27-Jun-21	31-Jan-21	27-Jun-21	06-Feb-21	03-Jul-21	6	
EP_SP_66_12-WP5A-M38.08.1.1.1.5 Seawall Structural Works		762	608	80.58%		148		29-Oct-19 A	27-Jun-21	31-Jan-21	27-Jun-21	06-Feb-21	03-Jul-21	6	
08-1100	Rubble Mound Laying (100,000m3 approx, @550m3/d)	182	230	93.41%	93.41%	12		27-Jun-20 A	11-Feb-21	31-Jan-21	11-Feb-21	24-Mar-21	04-Apr-21	52	
08-1105(6) (M22)	Prefabrication for Caisson (No.35 to No.43) Including Marine Access	337	399	91.1%	91.1%	30		28-Jan-20 A	01-Mar-21	31-Jan-21	01-Mar-21	06-Mar-21	04-Apr-21	34	
08-1115(3)	Caisson infill, Solid ballast, toe protection, precast concrete blocks ..etc Laying	250	608	40.8%	40.8%	148		29-Oct-19 A	27-Jun-21	31-Jan-21	27-Jun-21	06-Feb-21	03-Jul-21	6	
EP_SP_66_12-WP5A-M38.08.1.2 Phase II - Reclamation, Breakwater and Berth Construction		618	928	68.13%		197		31-Jan-19 A	16-Aug-21	31-Jan-21	16-Aug-21	17-Jan-21	19-Nov-22	461	
EP_SP_66_12-WP5A-M38.08.1.2.1 Reclamation		197	258	0%		197		01-Dec-20 A	16-Aug-21	31-Jan-21	16-Aug-21	17-Jan-21	18-Aug-21	3	
08-1200-2 (M35)	Reclamation fill for Eastern Side (from E6) from -7.5mPD to +2.5mPD (480,011m3 @ 4000m3/d)	120	138	35.8%	35.8%	77		01-Dec-20 A	18-Apr-21	31-Jan-21	18-Apr-21	17-Jan-21	04-Apr-21	-13	
08-1210	Reclamation fill from +2.5 to Formation Level (510,000m3 @4250m3/d)	120	120	0%	0%	120		18-Apr-21	16-Aug-21	18-Apr-21	16-Aug-21	05-Apr-21	02-Aug-21	-13	
EP_SP_66_12-WP5A-M38.08.1.2.1.1 Instrumentation		120	120	0%		120		17-Feb-21	17-Jun-21	17-Feb-21	17-Jun-21	04-Feb-21	27-Jul-21	41	
08-1340 (M23)	Placing Settlement Plates for Settlement Markers & Instrumentation on +2.5mPD (~42nrs)	120	120	0%	0%	120		17-Feb-21	17-Jun-21	17-Feb-21	17-Jun-21	04-Feb-21	03-Jun-21	-13	
08-1350 (M23)	Extension of instruments above +2.5mPD	65	65	0%	0%	65		13-Apr-21	17-Jun-21	13-Apr-21	17-Jun-21	24-May-21	27-Jul-21	41	
EP_SP_66_12-WP5A-M38.08.1.2.1.2 PVD Remedial Works		58	58	0%		58		19-Mar-21	16-May-21	19-Mar-21	16-May-21	06-Mar-21	18-Aug-21	95	
08-1390 (M34)	GI for ground condition varification at Zone D for PVD (2 nr approx @0.5 nr/day) Inc Report	14	14	0%	0%	14		19-Mar-21	02-Apr-21	19-Mar-21	02-Apr-21	06-Mar-21	19-Mar-21	-13	
08-1390 (M34)15	Install Sand Drains at Zone D (approx. 62 nr @ 4nr/day/2 set of equipment)	16	16	0%	0%	16		02-Apr-21	18-Apr-21	02-Apr-21	18-Apr-21	20-Mar-21	04-Apr-21	-13	
08-1390 (M34)20	GI for ground condition varification at other Zone for PVD (10 nr approx @0.5 nr/day) Inc Report	28	28	0%	0%	28		18-Apr-21	16-May-21	18-Apr-21	16-May-21	22-Jul-21	18-Aug-21	95	
EP_SP_66_12-WP5A-M38.08.1.2.2 Breakwater		618	910	71.11%		179		31-Jan-19 A	28-Jul-21	31-Jan-21	28-Jul-21	25-May-22	19-Nov-22	479	
08-1250	Geotextile and Sand Blanket Laying	45	747	64%	64%	16		31-Jan-19 A	16-Feb-21	31-Jan-21	16-Feb-21	19-Sep-22	05-Oct-22	597	
08-1280	Rubble Mound Laying (100,000m3 approx, @550m3/d)	188	326	5%	5%	179		06-Sep-20 A	28-Jul-21	31-Jan-21	28-Jul-21	25-May-22	19-Nov-22	479	
08-1285(1)	Prefabrication for Caission	180	384	12%	12%	158		19-Jun-20 A	08-Jul-21	31-Jan-21	08-Jul-21	25-May-22	30-Oct-22	480	
EP_SP_66_12-WP5A-M38.08.1.2.3 Seawall and Berth at Marine Access		37	37	0%		37		18-Apr-21	25-May-21	18-Apr-21	25-May-21	05-Apr-21	27-Jun-21	34	
08-1320(2)	Caisson Laying for Marine Access (8nrs)	30	30	0%	0%	30		18-Apr-21	18-May-21	18-Apr-21	18-May-21	05-Apr-21	04-May-21	-13	
08-1320(5A)	Caisson Infill, Solid ballast, toe protection, precast concrete blocks ..etc Laying	30	30	0%	0%	30		25-Apr-21	25-May-21	25-Apr-21	25-May-21	29-May-21	27-Jun-21	34	
EP_SP_66_12-WP5A-M38.15 Works By CLP		601	601	0%		601		04-Jan-23	27-Aug-24	04-Jan-23	27-Aug-24	20-Mar-23	14-Aug-24	-12	
EP_SP_66_12-WP5A-M38.15.1 Installation of Transmission System		120	120	0%		120		04-Jan-23	03-May-23	04-Jan-23	03-May-23	20-Mar-23	17-Jan-24	259	
15-0800	450 days Prior to Commencement of System Commissioning Test	0	0	0%	0%	0	As Late /	01-Apr-23		01-Apr-23		20-Mar-23		-12	
15-0900	Completion of Civil Provision for Transmission	0	0	0%	0%	0	Start On	04-Jan-23*		04-Jan-23		20-Mar-23		75	
15-1000	Construction of Transmission System	90	90	0%	0%	90		04-Jan-23	03-Apr-23	04-Jan-23	03-Apr-23	20-Sep-23	18-Dec-23	259	
15-1002	Cable Testing	30	30	0%	0%	30		04-Apr-23	03-May-23	04-Apr-23	03-May-23	19-Dec-23	17-Jan-24	259	
EP_SP_66_12-WP5A-M38.15.2 Remaining Installation Works by CLP		178	178	0%		178		30-Nov-23	26-May-24	30-Nov-23	26-May-24	18-Jan-24	15-Jun-24	21	
15-1005	Plant Installation inside CLP Equipment Room	60	60	0%	0%	60	Start On	30-Nov-23*	28-Jan-24	30-Nov-23	28-Jan-24	18-Jan-24	17-Mar-24	49	
15-1010	Cable Termination Works	30	30	0%	0%	30		26-Feb-24	27-Mar-24	26-Feb-24	27-Mar-24	18-Mar-24	16-Apr-24	21	
15-1015	Testing and Commissioning	60	60	0%	0%	60		27-Mar-24	26-May-24	27-Mar-24	26-May-24	17-Apr-24	15-Jun-24	21	
EP_SP_66_12-WP5A-M38.15.3 Metering & Energization		60	60	0%		60		28-Jun-24	27-Aug-24	28-Jun-24	27-Aug-24	16-Jun-24	14-Aug-24	-12	
15-1020	Incoming Power System Final Inspection and Metering works	30	30	0%	0%	30		28-Jun-24	28-Jul-24	28-Jun-24	28-Jul-24	16-Jun-24	15-Jul-24	-12	
15-1030	Energization of Incoming Power Supply Main System	0	0	0%	0%	0			28-Jul-24		28-Jul-24		15-Jul-24	-12	
15-1040	Energization of Incoming Power Supply Sub System	0	0	0%	0%	0			28-Jul-24		28-Jul-24		15-Jul-24	-12	
15-1050	Export Power System Final Inspection and Metering works	30	30	0%	0%	30		28-Jul-24	27-Aug-24	28-Jul-24	27-Aug-24	16-Jul-24	14-Aug-24	-12	
15-1060	Connection to Grid	0	0	0%	0%	0			27-Aug-24		27-Aug-24		14-Aug-24	-12	

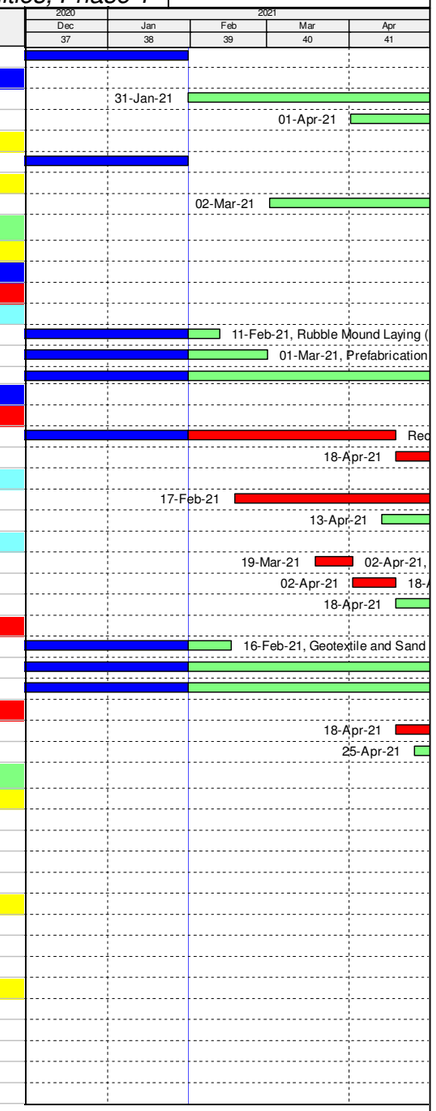

Remaining Work
Actual Work
Critical Remaining Work
Milestone
Actual Milestone
Critical Milestone

Appendix B Summary of Implementation Status of Environmental Mitigation

Appendix B

Table B.1 Implementation Schedule for Air Quality Measures for the IWMF at the artificial island near SKC

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
S3b.8.1	Air Pollution Control (Construction Dust) Regulation & Good Site Practices • Use of regular watering, with complete coverage, to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather. • Use of frequent watering for particularly dusty construction areas and areas close to ASRs. • Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines. • Open stockpiles shall be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs. • Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations. • Establishment and use of vehicle wheel and body washing facilities at the exit points of the site. • Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading	Work site / During the construction period	Contractor		✓			Air Pollution Control (Construction Dust) Regulation	Implemented, N/A for dust control measures for transportation outside site boundary.

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	points, and use of water sprinklers at the loading area where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods. • Imposition of speed controls for vehicles on unpaved site roads. Ten kilometers per hour is the recommended limit. • Where possible, routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs • Instigation of an environmental monitoring and auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise.								
S3b.6.3	<u>Odour Removal by Deodorizers</u> • Deodorizers with 95% odour removal efficiency would be installed for the air ventilated from the mechanical treatment plant before discharge to the atmosphere	Waste reception halls, the waste storage area, the mechanical treatment plant / During design & operation phase	IWMF Operator	✓		✓		EIAO-TM	N/A
S3b.8.2	<u>Air Pollution Control and Stack Monitoring</u>	IWMF stack emissions / During	IWMF Operator	✓		✓		EIAO-TM, Supporting Document for	N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	• Air pollution control and stack monitoring system will be installed for the IWMF to ensure that the emissions from the IWMF stack will meet the proposed target emission limits. • Voluntary Enhancement Measures in Flue Gas Cleaning and Emission Monitoring: 1. Two-stage bag filter system with reagent recirculation; 2. In addition to SCR, provide SNCR for removal of NO_x; tighten emission limit for half-hourly and daily NO_x to 160 mg/m^3 and 80 mg/m_3 respectively; 3. Well-mixed feed waste: to minimize the fluctuation of pollutant loading on the flue gas treatment system; 4. Two more AQMSs would be set up at South Lantau and Shek Kwu Chau respectively; 5. Limit levels will be set under the IWMF DBO contract to require that waste feed shall cease if any of the air pollutant has exceeded 95% of the emission concentration limit as stipulated in the Special Process license; and 6. Each incineration chamber shall be fitted with auxiliary burners to ensure complete burn out of the combustion gases.	design & operation phase						Application for Variation of Environmental Permit (EP-429/2012)	

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
-	Treated Fly Ash and Air Pollution Control Residues: • During testing and commissioning, the Contractor shall sample and test every container of treated fly ash and air pollution control residues for conformance to the Incineration Residue Pollution Control Limits and leachability criteria shown in Table 2 of the Environmental Permit. If a test result confirms that any one of the samples does not conform to the limits and the criteria, the Contractor shall be required to sample and test every container of treated fly ash and air pollution control residues for conformance to the Incineration Residue Pollution Control Limits and leachability criteria for the next six months. • During the first six months of operation, if the requirements in (a) could be fully conformed with, the Contractor shall sample and test every shipload of treated fly ash and air pollution control residues for conformance to the Incineration Residue Pollution Control Limits and leachability criteria shown in Table 2 of the Environmental Permit. The Contractor shall take two samples from each shipload for testing and the Contractor shall not dispose of any of that shipload of treated fly ash and air	IWMF stack emissions / During design & operation phase	IWMF Operator	✓		✓		Supporting Document for Application for Variation of Environmental Permit (EP-429/2012)	N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	pollution control residues until the test results confirm that the two samples conform to the limits and the criteria. If a test result confirms that any one of the two samples does not conform to the limits and the criteria, the Contractor shall be required to sample and test every shipload of treated fly ash and air pollution control residues for conformance to the Incineration Residue Pollution Control Limits and leachability criteria for the next six months. The Contractor shall make due allowance in the Design and the Operation for the time to sample and test treated fly ash and air pollution control residues before disposal. • Provided that there is no non-conformance to the Incineration Residue Pollution Control Limits and leachability criteria shown in Table 2 of the Environmental Permit throughout a continuous sixmonth period in the Operation Period, the testing frequency shall be reduced to monthly interval.Two samples from one shipload of treated fly ash and air pollution control residues shall be collected and tested for conformance to the Incineration Residue Pollution Control Limits and leachability criteria. The Contractor shall not dispose of any of the treated fly ash and air pollution								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	control residues in the shipload which the samples are taken until the test results confirm that the samples conform to the limits and the criteria. If the test result confirm that any one of the samples does not conform to the limits and the criteria, the Contractor shall be required to sample and test every shipload of treated fly ash and air pollution control residues for conformance to the Incineration Residue Pollution Control Limits and leachability criteria shown in Table 2 of the Environmental Permit for the next six months.								
-	<u>Bottom Ash:</u> • During testing and commissioning, the Contractor shall sample and test every container of bottom ash for conformance to the leachability criteria shown in Table 2 of the Environmental Permit. If a test result confirms that any one of the samples does not conform to the criteria, the Contractor shall be required to sample and test every container of bottom ash for conformance to the leachability criteria for the next six months. • During the first six months of operation, if the requirements in (d) could be fully conformed with, the Contractor shall sample and test one shipload of bottom ash each month for	IWMF stack emissions / During design & operation phase	IWMF Operator	✓		✓		Supporting Document for Application for Variation of Environmental Permit (EP-429/2012)	N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	conformance to the leachability criteria shown in Table 2 of the Environmental Permit. The Contractor shall take two samples from the shipload for testing and the Contractor shall not dispose of any of that shipload of bottom ash until the test results confirm that the two samples conform to the criteria. If a test result confirms that any one of the two samples does not conform to the criteria, the Contractor shall be required to sample and test each shipload of bottom ash for conformance to the leachability criteria for the next six months. The Contractor shall make due allowance in the Design and the Operation for the time to sample and test bottom ash before disposal. • Provided that there is no non-conformance to the leachability criteria shown in Table 2 of the Environmental Permit throughout a continuous six month period in the Operation Period, the Contractor shall be allowed to take two samples from any one shipload of bottom ash once every six months for conformance to the leachability criteria. The Contractor shall not dispose of any of the bottom ash in the shipload which the samples are taken until the test								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	results confirm that the samples conform to the criteria. If the test result confirm that any one of the samples does not conform to the criteria, the Contractor shall be required to sample and test one shipload of bottom ash each month for conformance to the leachability criteria shown in Table 2 of the Environmental Permit for the next six months as stipulated above.								

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Table B.2 Implementation Schedule for Noise Impact Measures for the IWMF at the artificial island near SKC

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
S4b.8	Good site practices to limit noise emissions at source and use of quiet plant and working methods, whenever practicable.	Work Sites / Construction Period	EPD and its contractors		✓			EIAO-TM	Implemented
S4b.6 & S4b.8	All the ventilation fans installed in the below will be provided with silencers or acoustics treatment. (i) Stack of the incinerator (ii) Ventilation systems within the IWMF Enclosure and discharge silencer or other acoustic treatment equipment should be installed in the air-cooled chillers Other than provision of silencer or other acoustic treatment equipment for the stack of the incinerator and ventilation system, the detailed design should incorporate the following good practice in order to minimize the nuisance on the neighboring NSRs. (i) The exhaust of the ventilation system and any opening of the building should be located facing away from any NSRs; and (ii) Louver or other acoustic treatment equipment could also be applied to the exhaust of the ventilation system.	Within IWMF area / Construction Period	EPD and its contractors	✓		✓		EIAO-TM	N/A

-	<u>Voluntary Enhancement Measure</u> • Provision of air-conditioner and double glazed windows to nearby NSR at Shek Kwu Chau (i.e. SARDA) as precautionary measures.	IWMF site	Design team, contractor, IWMF operator	✓	✓			Supporting Document for Application for Variation of Environmental Permit (EP-429/2012)	Implemented

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Table B.3 Implementation Schedule for Water Quality Measures for the Artificial Island near SKC

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
S5b.8.1.1	<u>Drainage and Construction Site Runoff</u> The site practices outlined in ProPECC PN 1/94 "Construction Site Drainage" should be followed as far as practicable in order to minimise surface runoff and the chance of erosion. These practices include the following items: • At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct storm water to silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the contractor prior to the commencement of construction. • Boundaries of earthworks should be surrounded by dykes or embankments for flood protection, as necessary. • Sand/silt removal facilities such as sand/silt traps and sediment basins should be provided to remove sand/silt particles from runoff to meet the requirements of the TM-DSS. The design of efficient silt removal facilities	Work site / During the construction period	Contractor		✓			EIAO-TM; ProPECC PN 1/94; WPCO	N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	should be based on the guidelines in Appendix A1 of ProPECC PN 1/94, which states that the retention time for silt/sand traps should be 5 minutes under maximum flow conditions. The detailed design of the sand/silt traps shall be undertaken by the contractor prior to the commencement of construction. • Water pumped out from foundation piles must be discharged into silt removal facilities. • Measures should be taken to minimize the ingress of site runoff and drainage into excavations. Drainage water pumped out from excavations should be discharged into storm drains via silt removal facilities. • During rainstorms, exposed slope/soil surfaces should be covered by a tarpaulin or other means, as far as practicable. Other measures that need to be implemented before, during and after rainstorms are summarized in ProPECC PN 1/94. • Exposed soil areas should be minimized to reduce potential for increased siltation and contamination of runoff. • Earthwork final surfaces should be well compacted and subsequent permanent work or surface protection should be immediately performed.								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	• Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric during rainstorms.								
S5b.8.1.2	<u>General Construction Activities</u> Construction solid waste should be collected, handled and disposed of properly to avoid entering to the nearby watercourses and public drainage system. Rubbish and litter from construction sites should also be collected to prevent spreading of rubbish and litter from the site area. It is recommended to clean the construction sites on a regular basis.	Work site / During the construction period	Contractor		✓			EIAO-TM; ProPECC PN 1/94; WPCO	Implemented

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
S5b.8.1.3	There is a need to apply to EPD for a discharge license for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge license. All the run-off and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TM-DSS. The beneficial uses of the treated effluent for other on-site activities such as dust suppression and general cleaning etc., can minimize water consumption and reduce the effluent discharge volume. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the relevant WPCO license which is under the ambit of regional office of EPD.	Work site / During the construction period	Contractor		✓			EIAO-TM; ProPECC PN 1/94; WPCO	Discharge License was issued on 22/08/2019.
S5b.8.1.4	Accidental Spillage Contractor must register as a chemical waste producer if chemical wastes would be produced from construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.	Work site / During the construction period	Contractor		✓			EIAO-TM; ProPECC PN 1/94; WPCO; WDO	Deficiency of Mitigation Measures but rectified by the Contractor.
S5b.8.1.5	Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas which	Work site / During the construction period	Contractor		✓			EIAO-TM; ProPECC PN 1/94; WPCO; WDO	Implemented.

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	appropriately equipped to control these discharges.								
S5b.8.1.6	Oils and fuels should only be used and stored in designated areas which have pollution prevention facilities. All fuel tanks and storage areas should be sited on sealed areas in order to prevent spillage of fuels and solvents to the nearby watercourses. All waste oils and fuels should be collected in designated tanks prior to disposal.	Work site / During the construction period	Contractor		✓			EIAO-TM; ProPECC PN 1/94; WPCO; WDO	Deficiency of Mitigation Measures but rectified by the Contractor.
S5b.8.1.7	Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows: • Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport. • Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents. • Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.	Work site / During the construction period	Contractor		✓			EIAO-TM; ProPECC PN 1/94; WPCO; WDO	Implemented.
S5b.8.1.8	<u>Sewage Effluent</u> Temporary sanitary facilities, such as portable chemical toilets, should be employed on-site where necessary to	Work site / During the construction period	Contractor		✓			EIAO-TM; ProPECC PN 1/94; WPCO	N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	handle sewage from the workforce. A licensed contractor would be responsible. for appropriate disposal and maintenance of these facilities.								
S5b.8.1.9	<u>Reclamation and Construction of Breakwaters</u> • The proposed dredging and reclamation should be commenced in phases. The breakwaters and seawalls should be constructed and the reclamation should be started within the enclosed breakwaters after the completion of the breakwater. Silt curtain should be applied around caissons / blockwork during the filling of the cell to prevent the loss of fine in the filling material. • The maximum production rate for dredging for the anti-scouring protection layer shall not exceed the permitted maximum daily dredging rate and carried out within its respective distance from the nearest non-translocatable coral community by the dredging contractor as specified in S.2.18 of the Further Environmental Permit (no.:FEP-01/429/2012/A). It is recommended to employ closed grab with small capacity of 2 m^3 to control the dredging rate. • Any gap that may need to be provided for marine access will be located at the middle of the North Western seawall, away from the identified coral communities and will be shielded by silt curtains systems to control sediment plume dispersion. • The silt curtain system at marine access opening should be closed as soon as the	Work site / During the marine construction period	Contractor		✓			EIAO-TM; WPCO, Supporting Document for Application for Variation of Environmental Permit (EP-429/2012) Further Environmental Permit No. FEP-01/429/2012/A	Implemented.

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	barges passes through the marine access opening in order to minimize the period of curtain opening. Filling should only be carried out behind the silt curtain when the silt curtain is completely closed. • To enhance the effectiveness of the silt curtain at the marine access, the northern breakwater would be built before the commencement of the reclamation to reduce the current velocity towards the marine access opening. • The silt curtain system at marine access opening should be regularly checked and maintained to ensure proper functioning. • Where public fill is proposed for filling below +2.5mPD, the fine content in the public fill will be controlled to 25% which is in line with the CEDD's General Specification; • The filling for reclamation should be carried out behind the seawall. The filling material should only consist of public fill, rock and sand. The filling composition and filling rates at each filling area should follow those delineated in Table 1 of the FEP-01/429/2012/. The filling above high watermark is not restricted; • No dredging should be carried out within 16m to the nearest non-translocatable coral community; • Daily site audit including full-time on-site monitoring by the ET is recommended during the dredging for anti-scouring protection layer								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	for checking the compliance with the permitted no. of grab; • Closed grab dredger should be used to minimize the loss of sediment during the raising of the loaded grabs through the water column; • Frame-type silt curtains should be deployed around the dredging operations; • Floating-type silt curtains should be used to surround the circular cell during the sheetpiling work; • The descent speed of grabs should be controlled to minimize the seabed impact speed; • Barges should be loaded carefully to avoid splashing of material; • All barges used for the transport of dredged materials should be fitted with tight bottom seals in order to prevent leakage of material during loading and transport; • No concurrence works between laying of submarine cables and dredging/reclamation works within the same location is allowed. For works close to each other, the construction program should be arranged so that the dredging/reclamation works within area bounded by the breakwaters and the laying of cables would not operate within a distance of 80m from each other to avoid any accumulative impact on the environment (in case if such tight schedule is necessary).								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	• All barges should be filled to a level which ensures that material does not spill over during loading and transport to the disposal site and that adequate freeboard is maintained to ensure that the decks are not washed by wave action. • No DCM works should be carried out within 100m to the nearest non-translocatable coral colony / colonies. • Silt curtains should be employed to enclose DCM field trial and any full scale DCM work to minimize the potential impacts on water aspect. • A sand blanket is to be placed on top of the marine deposit using tremie pipes prior to the DCM ground treatment to avoid seabed sediment disturbance.								
S5b.8.2.3	Operational Phase Discharges A pipeline drainage system will serve the development area collecting surface runoff from paved areas, roof, etc. Sustainable drainage principle would be adopted in the drainage system design to minimize peak surface runoff, maximize permeable surface and maximize beneficial use of rainwater.	Within IWMF site / During the operational phase	IWMF Operator	✓		✓		WPCO	N/A
S5b.8.2.4	Oil interceptors should be provided in the drainage system of any potentially contaminated areas (such as truck parking area and maintenance workshop) and regularly cleaned to prevent the release of oil products into the storm water drainage system in case of accidental spillages.	Within IWMF site / During the operational phase	IWMF Operator	✓		✓		WPCO; WDO	N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	Accidental spillage should be cleaned up as soon as practicable and all waste oils and fuels should be collected and handled in compliance with the Waste Disposal Ordinance.								
S5b.8.2.5	Refuse Entrapment Collection and removal of floating refuse should be performed at regular intervals for keeping the water within the Project site boundary and the neighboring water free from rubbish.	Within the Project site / During the operational phase	IWMF Operator			✓		WPCO	N/A
S5b.8.2.6	Transportation of bottom ash, fly ash and APC residues to WENT Landfill for disposal Covered container should be used in the shipping of the incineration waste to limit the contact between the incineration waste and the marine water. A comprehensive emergency response plan for any accidental spillage should be submitted by the operation contractor to the EPD for agreement before the operation of the facilities. Salvage and cleanup action to recover the spilled incineration waste containers following the spillage should be carried out according to the emergency response plan to mitigate the environmental impact in case of spillage.	Transportation of Incineration Ash / During the operational phase	IWMF Operator			✓			N/A

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Table B.4 Implementation Schedule for Waste Management Measures for the IWMF at the artificial island near SKC

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
6b.5.1.2	Good Site Practices Adverse environmental impacts in relation to waste management are not expected, provided that good site practices are strictly followed. Recommendations for good site practices during the construction activities would include: • Obtain relevant waste disposal permits from appropriate authorities, in accordance with the Waste Disposal Ordinance (Cap. 354) and subsidiary Regulations and the Land (Miscellaneous Provisions) Ordinance (Cap. 28); • Provide staff training for proper waste management and chemical handling procedures; • Provide sufficient waste disposal points and regular waste collection; • Provide appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; and • Carry out regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; • Separate chemical wastes for special handling and disposed of to licensed facility for treatment; and • Employ licensed waste collector to collect waste.	Work Site/ During Construction Period	Contractor		✓			WDO; LDO; ETWB TCW No. 19/2005; EIAO-TM	Implemented
6b.5.1.3	Waste Reduction Measures	Work Site/ During Design	Contractor	✓	✓				Implemented

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	Good management and control can prevent the generation of a significant amount of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include: • Design foundation works that could minimize the amount of excavated material to be generated. • Provide training to workers on the importance of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycling; • Sort out demolition debris and excavated materials from demolition works to recover reusable/recyclable portions (i.e. soil, broken concrete, metal etc.); • Segregate and store different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; • Encourage the collection of aluminum cans by providing separate labelled bins to enable this waste to be segregated from other general refuse generated by the work force; • Proper storage and site practices to minimize the potential for damage or contamination of construction materials; and • Plan and stock construction materials carefully to minimize amount of waste to be	& Construction Period							N/A for foundation and demolition items

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	generated and to avoid unnecessary generation of waste.								
6b.5.1.7	<u>Dredged Sediment – Application of Dumping Permit</u> The project proponent should agree in advance with MFC of CEDD on the site allocation. The project proponent or contractor for the dredging works shall then apply for the site allocations of marine sediment disposal based on the prior agreement with MFC/CEDD. The project proponent or contractor should also be responsible for the application of all necessary permits from relevant authorities, including the dumping permit as required under DASO from EPD, for the disposal of dredged sediment prior to the commencement of the dredging works.	Seawall and Reclamation site / Construction Period	EPD and its contractor	✓	✓			DASO ETWB TCW 34/2002	Implemented
6b.5.1.8	<u>Dredged Sediment – Sediment Quality Report</u> The project proponent or contractor will need to satisfy the appropriate authorities that the quality of the marine sediment to be dredged has been identified according to the requirements of ETWB TCW 34/2002. This should be completed well before the dredging works and would include at least the submission of a formal Sediment Quality Report under Tier I of ETWB TCW No. 34/2002 to DEP for approval. Subject to advice from DEP, it is possible that further marine SI in accordance with ETWB TCW 34/2002 might be necessary for the application of dumping permit under DASO. In such case, a sediment sampling and testing	Seawall and Reclamation site / Construction Period	EPD and its contractor	✓				DASO ETWB TCW 34/2002	Implemented

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	proposal shall be submitted to and approved by DEP before the additional marine SI works.								
6b.5.1.9	Dredged Sediment – Sediment Transportation The barge transporting the sediments to the designated disposal sites should be equipped with tight fitting seals to prevent leakage and should not be filled to a level that would cause overflow of materials or laden water during loading or transportation. In addition, monitoring of the barge loading shall be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels shall be equipped with automatic self-monitoring devices as specified by the DEP.	Seawall and Reclamation site / Construction Period	EPD and its contractor		✓			DASO ETWB TCW 34/2002	Implemented
6b.5.1.10	Construction and Demolition Materials In order to minimize the impact resulting from collection and transportation of C&D materials for off-site disposal, the excavated material arising from site formation and foundation works should be reused on-site as backfilling material and for landscaping works as far as practicable. Other mitigation requirements are listed below: • A Waste Management Plan (WMP), which becomes part of the Environmental Management Plan (EMP), should be prepared in accordance with ETWB TCW No.19/2005; • A recording system for the amount of wastes generated, recycled and disposed	Work Site/ During Design & Construction Period	Contractor	✓	✓			ETWB TCW No. 19/2005	Implemented

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	(including the disposal sites) should be adopted for easy tracking; and • In order to monitor the disposal of C&D materials at public filling facilities and landfills and to control fly-tipping, a trip-ticket system should be adopted (refer to *ETWB TCW No. 31/2004*).								
6b.5.1.11 – 6b.5.1.12	The Contactor should prepare and implement an EMP in accordance with ETWB TCW No.19/2005, which describes the arrangements for avoidance, reuse, recovery, recycling, storage, collection, treatment and disposal of different categories of waste to be generated from construction activities. Such a management plan should incorporate site specific factors, such as the designation of areas for segregation and temporary storage of reusable and recyclable materials. The EMP should be submitted to the Engineer for approval. The Contractor should implement waste management practices in the EMP throughout the construction stage of the Project. The EMP should be reviewed regularly and updated by the Contractor, preferably on a monthly basis. All surplus C&D materials arising from or in connection with construction works should become the property of the Contractor when it is removed unless otherwise stated. The Contractor would be responsible for devising a system to work for on-site sorting of C&D materials and promptly removing all sorted and process materials arising from the	Work Site/ During Design & Construction Period	Contractor	✓	✓			ETWB TCW No. 19/2005	Implemented

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	construction activities to minimize temporary stockpiling on-site. The system should be included in the EMP identifying the source of generation, estimated quantity, arrangement for on-site sorting, collection, temporary storage areas and frequency of collection by recycling Contractors or frequency of removal off-site.								
6b.5.1.13	<u>Chemical Wastes</u> Should chemical wastes be produced at the construction site, the Contractor would be required to register with EPD as a Chemical Waste Producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste (such as explosive, flammable, oxidizing, irritant, toxic, harmful, or corrosive). The Contractor should employ a licensed collector to transport and dispose of the chemical wastes, to either the Chemical Waste Treatment Centre at Tsing Yi, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Work Site/ During Construction Period	Contractor		✓			Waste Disposal (Chemical Waste) (General) Regulation	Implemented.

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
6b.5.1.14	General Refuse General refuse should be stored in enclosed bins or compaction units separate from C&D materials. A licensed waste collector should be employed by the Contractor to remove general refuse from the site, separately from C&D materials. Preferably an enclosed and covered area should be provided to reduce the occurrence of 'wind blown' light material.	Work Site/ During Construction Period	Contractor		✓			Public Health and Municipal Services Ordinance	Implemented
6b.5.1.16 – 6b.5.1.33	Biogas Generation The Contractor shall review the data and analysis results, and the data from further Site Investigation, if any. Subject to the review findings, the following gas protection measures may be considered if necessary: - gas monitoring after reclamation; - passive ventilation; - gas impermeable membrane; - ventilation with "at risk" rooms; - protection of utilities or below ground services; - precautions during construction works; - precautions prior to entry of belowground services	Reclamation site (if dredging at the reclamation site is not required) / Design & Construction Period	Designer and/or contractor	✓	✓			EPD/TR8/97	N/A
6b.5.2.1	Good Site Practices	IWMF Site/During	IWMF Operator			✓		Waste Disposal Ordinance (Cap.354);	N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	It is recommended that the following good operational practices should be adopted to minimise waste management impacts: • Obtain the necessary waste disposal permits from the appropriate authorities, in accordance with the Waste Disposal Ordinance (Cap. 354) and Waste Disposal (Chemical Waste) (General) Regulation; • Nomination of an approved person to be responsible for good site practice, arrangements for collection and effective disposal to an appropriate facility of all wastes generated at the site; • Use of a waste haulier licensed to collect specific category of waste; • A trip-ticket system should be included as one of the contractual requirements and implemented by the Environmental Team to monitor the disposal of solid wastes at landfills, and to control fly tipping. Reference should be made to ETWB TCW No. 31/2004. • Training of site personnel in proper waste management and chemical waste handling procedures; • Separation of chemical wastes for special handling and appropriate treatment at a licensed facility; • Routine cleaning and maintenance programme for drainage systems, sumps and oil interceptors;	Operation Period						Waste Disposal (Chemical Waste) (General) Regulation; ETWB TCW No. 1/2004	

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	• Provision of sufficient waste disposal points and regular collection for disposal; • Adoption of appropriate measures to minimize windblown litter and dust during transportation of waste, such as covering trucks or transporting wastes in enclosed containers; and • Implementation of a recording system for the amount of wastes generated, and disposed of (including recycled the disposal sites).								
6b.5.2.2	<u>Waste Reduction Measures</u> Good management and control can prevent the generation of significant amounts of waste. It is recommended that the following good operational practices should be adopted to ensure waste reduction: • Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; • Encourage collection of aluminum cans, plastic bottles and packaging material (e.g. carton boxes) and office paper by individual collectors. Separate labelled bins should be provided to help segregate this waste from other general refuse generated by the work force; and • Any unused chemicals or those with remaining functional capacity should be reused as far as practicable.	IWMF Site/ During Operation Period	IWMF Operator			✓			Implemented

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
6b.5.2.3	<u>Storage, Handling, Treatment, Collection and Disposal of</u> <u>Incineration By-Products</u> The following measures are recommended for the storage, handling and collection of the incineration by-products: • Ash should be stored in storage silos; • Ash should be handled and conveyed in closed systems fully segregated from the ambient environment; • Ash should be wetted with water to control fugitive dust, where necessary; • All fly ash and APC residues should be treated, e.g. by cement solidification or chemical stabilization, for compliance with the proposed Incineration Residue Pollution Control Limits and leachability criteria prior to disposal; • The ash should be transported in covered trucks or containers to the designated landfill site. The Contractor should provide EPD with chemical analysis results of the bottom ash, and treated fly ash and APC residues to confirm that the ash/residue can comply with the proposed Incineration Residue Pollution Control Limits before disposal.	IWMF Site/ During Operation Period	IWMF Operator			✓		Incineration Residue Pollution Control Limits	N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
6b.6.3.1	<u>Fuel Oil Tank Construction and Test</u> • The fuel tank to be installed should be of specified durability. • Double skin tanks are preferred. • Underground fuel storage tank should be placed within a concrete pit. • The concrete pit shall be accessible to allow regular tank integrity tests to be carried out at regular intervals. • Tank integrity tests should be conducted by an independent qualified surveyor or structural engineer. • Any potential problems identified in the test should be rectified as soon as possible.	Fuel Oil Storage Tank/ During Design, Construction and Operation Periods	IWMF Contractor	✓	✓	✓			N/A
6b.6.3.1	<u>Fuel Oil Pipeline Construction and Test</u> • Installation of aboveground fuel oil pipelines is preferable; if underground pipelines are unavoidable, concrete lined trenches should be constructed to contain the pipelines. • Double skin pipelines are preferred. • Distance between the fuel oil refuelling points and the fuel oil storage tank shall be minimized.	Fuel Oil Pipelines/ During Design, Construction and Operation Periods	IWMF Contractor	✓	✓	✓			N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	• Integrity tests for the pipelines should be conducted by an independent qualified surveyor or structural engineer at regular intervals. • Any potential problems identified in the test should be rectified as soon as possible.								
6b.6.3.1	<u>Fuel Oil Leakage Detection</u> • Installation of leak detection device at storage tank and pipelines. • Installation and use of pressure gauges (e.g. at the two ends of a filling line) in fuel filling, which allows unexpected pressure drop or difference and sign of leakage to be detected.	Fuel Oil Storage Tank and Pipelines/ During Design, Construction and Operation Periods	IWMF Contractor	✓	✓	✓			N/A
6b.6.3.1	<u>Fuel Oil Storage Tank Refuelling</u> • Storage tank refuelling (from road tanker) should only be conducted by authorized staff of the oil company using the company's standard procedures.	Fuel Oil Refuelling Point/ During Operation Period	IWMF Operator			✓			N/A
6b.6.3.1	<u>Fuel Oil Spillage Response</u> An Oil Spill Response Plan should be prepared by the operator to document the appropriate response procedures for oil spillage incidents in detail. General procedures to be taken in case of fuel oil spillage are presented below. • Training	IWMF Site/ During Operation Period	IWMF Operator			✓			N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	- Training on oil spill response actions should be given to relevant staff. The training shall cover the followings: ➢Tools & resources to combat oil spillage and fire, e.g. locations of oil spill handling equipment and fire fighting equipment; ➢General methods to deal with oil spillage and fire incidents; ➢Procedures for emergency drills in the event of oil spills and fire; and ➢Regular drills shall be carried out. • Communication -Establish communication channel with the Fire Services Department (FSD) and EPD to report any oil spillage incident so that necessary assistance from relevant department can be quickly sought. • Response Procedures -Any fuel oil spillage within the IWMF site should be immediately reported to the Plant Manager with necessary details including location, source, possible cause and extent of the spillage. -Plant Manager should immediately attend to the spillage and initiate any appropriate action to confine and clean up the spillage. The response								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	procedures shall include the following: ➢Identify and isolate the source of spillage as soon as possible. ➢Contain the oil spillage and avoid infiltration into soil/ groundwater and discharge to storm water channels. ➢Remove the oil spillage. ➢Clean up the contaminated area. ➢If the oil spillage occurs during storage tank refuelling, the refueling operation should immediately be stopped. ➢Recovered contaminated fuel oil and the associated material to remove the spilled oil should be considered as chemical waste. The handling and disposal procedures for chemical wastes are discussed in the following paragraphs.								
6b.6.3.2	<u>Chemicals and Chemical Wastes Handling & Storage</u> • Chemicals and chemical wastes should only be stored in suitable containers in purpose-built areas. • The storage of chemical wastes should comply with the requirements of the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. • The storage areas for chemicals and chemical wastes shall have an	Chemicals and Chemical Wastes Storage Area / During Operation Period	IWMF Operator			✓			N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	impermeable floor or surface. The impermeable floor/ surface shall possess the following properties: - Not liable to chemically react with the materials and their containers to be stored. - Able to withstand normal loading and physical damage caused by container handling - The integrity and condition of the impermeable floor or surface should be inspected at regular intervals to ensure that it is satisfactorily maintained ➢ For liquid chemicals and chemical wastes storage, the storage area should be bunded to contain at least 110% of the storage capacity of the largest containers or 20% of the total quantity of the chemicals/chemical wastes stored, whichever is the greater. ➢ Storage containers shall be checked at regular intervals for their structural integrity and to ensure that the caps or fill points are tightly closed. ➢ Chemical handling shall be conducted by trained workers under supervision.								
6b.6.3.2	<u>Chemicals and Chemical Wastes Spillage Response</u>	IWMF Site/ During	IWMF Operator			✓			N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	A Chemicals and/ or Chemical Wastes Spillage Response Plan shall be prepared by the operator to document in detail the appropriate response procedures for chemicals or chemical wastes spillage incidents. General procedures to be undertaken in case of chemicals/ chemical waste spillages are presented below. • Training - Training on spill response actions should be given to relevant staff. The training shall cover the followings: ➢ Tools & resources to handle spillage, e.g. locations of spill handling equipment; ➢ General methods to deal with spillage; and ➢ Procedures for emergency drills in the event of spills. • Communication - Establish communication channel with FSD and EPD to report the spillage incident so that necessary assistance from relevant department can be quickly sought. • Response Procedures	Operation Period							

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	- Any spillage within the IWMF site should be reported to the Plant Manager. - Plant Manager shall attend to the spillage and initiate any appropriate actions needed to confine and clean up the spillage. The response procedures shall include the followings: ➢ Identify and isolate the source of spillage as soon as possible; ➢ Contain the spillage and avoid infiltration into soil/ groundwater and discharge to storm water channels (in case the spillage occurs at locations out of the designated storage areas); ➢ Remove the spillage; the removal method/ procedures documented in the Material Safety Data Sheet (MSDS) of the chemicals spilled should be observed; ➢ Clean up the contaminated area (in case the spillage occurs at locations out of the designated storage areas); and								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	➢ The waste arising from the cleanup operation should be considered as chemical wastes.								
6b.6.3.3	<u>Preventive Measures for Incineration By-products Handling</u> The recommended measures listed below can minimize the potential contamination to the surrounding environment due to the incineration by-products: • Ash should be stored in storage silos; • Ash should be handled and conveyed in closed systems fully segregated from the ambient environment; • Ash should be wetted with water to control fugitive dust, where necessary; • All fly ash and APC residues should be treated, e.g. by cement solidification or chemical stabilization, for compliance with the proposed Incineration Residue Pollution Control Limits and leachability criteria prior to disposal; • The ash should be transported in covered trucks or containers to the designated landfill site.	Storage, Handling & Collection of Incineration Ash at IWMF/ During Operation Period	IWMF Operator			✓			N/A
6b.6.3.4 - 6b.6.3.6	<u>Incident Record</u>	IWMF Site/ During	IWMF Operator			✓		Guidance Manual for Use of Risk-based Remediation	N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	After any spillage, an incident report should be prepared by the Plant Manager. The incident report should contain details of the incident including the cause of the incident, the material spilled and estimated spillage amount, and also the response actions undertaken. The incident record should be kept carefully and able to be retrieved when necessary. The incident report should provide sufficient details for the evaluation of any environmental impacts due to the spillage and assessment of the effectiveness of measures taken. In case any spillage or accidents results in significant land contamination, EPD should be informed immediately and the IWMF operator should be responsible for the cleanup of the affected area. The responses procedures described in **Section 6b.6.3.1** and **Section 6b.6.3.2** of EIA report should be followed accordingly together with the land contamination assessment and remediation guidelines stipulated in the *Guidance Manual for Use of Risk-based Remediation Goals for Contaminated Land Management and the Guidance Note for Contaminated Land and Remediation.*	Operation Period						Goals for Contaminated Land Management and the Guidance Note for Contaminated Land and Remediation.	

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Table B.5 Implementation Schedule for Ecological Quality Measures for the IWMF at the artificial island near SKC

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
7b.8.2.1	<u>Measures to avoid direct loss of intertidal habitat</u> • The site boundary has been proposed to avoid direct contact with the intertidal natural rocky shore of Shek Kwu Chau. It avoids direct loss of intertidal communities and the existing natural rocky shore habitat, where Reef Egret and White-bellied Sea Eagle have been recorded within and in the vicinity of this habitat.	IWMF site	Design team	✓				EIAO-TM	N/A
7b.8.2.2	<u>Measures to minimise loss of coastal subtidal habitat</u> • Extensive coral colonies were recorded at the coastal hard bottom habitat at Shek Kwu Chau. To avoid and minimise the extensive direct impact on the coral colonies, the proposed reclamation area has been moved further offshore to minimise loss of subtial habitat near shore.	IWMF site	Design team	✓				EIAO-TM	N/A
7b.8.2.3	<u>Zero Discharge Scheme</u> • The design scheme of the Project has avoided discharge of wastewater into the marine environment. A zero discharge scheme would be adopted during the operation of the Project. An on-site wastewater treatment plant would be provided to treat the wastewater generated from the IWMF (mainly human sewage). The treated effluent would be re-used in the incineration	IWMF site	Design team, IWMF operator	✓		✓		WPCO	N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	plant and mechanical treatment plant, or for onsite washdown and landscape.								
7b.8.2.4	<u>Measures to avoid loss of plant species of conservation importance</u> • Landing portal construction works would not cause direct lost to the recorded individual of protected plant species, • *Aquilaria sinensis*, at the coastal shrubland habitat at Cheung Sha. As a precautionary measure, the plant should be tagged with eye-catching tape and fenced off prior to works, in order to avoid any damage by workers.	Cheung Sha landing portal	Design team, Contractor	✓	✓		✓	EIAO-TM	N/A
7b.8.3.1-7b.8.3.15	<u>Measures to minimise water quality impact</u> • Measures for water quality as recommended in **Section 5b** of the EIA Report should be implemented.	Work site	Design team, contractor, IWMF operator	✓	✓	✓	✓	EIAO-TM; ProPECC PN 1/94; WPCO	Implemented
7b.8.3.16 - 7b.8.3.30	<u>Measures to minimise disturbance on Finless Porpoise</u> *Minimisation of Habitat Loss for Finless Porpoise* • Substantial revision has been made on the layout plan and form of the breakwater, in order to minimise the potential loss of important habitat for Finless Porpoise. The revision has greatly reduced the size of the embayment area, as well as the Project footprint. As a result, the size of habitat loss for Finless Porpoise has	IWMF site, work site, marine traffic route	Design team, contractor, IWMF operator	✓	✓	✓	✓	EIAO-TM, Supporting Document for Application for Variation of the Environmental Permit (EP-429/2012)	Implemented for avoidance of construction works that may produce underwater acoustic disturbance, Vessel Travel Route implementation, training of staff, MMEZ and marine mammal watching works during deployment of silt curtain; N/A for others

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	reduced from the original ~50 ha, down to ~31 ha. *Avoidance of peak season for finless porpoise occurrence* • To minimise potential acoustic disturbance from construction activities on Finless Porpoise, construction works that may produce underwater acoustic disturbance should be scheduled outside the months with peak Finless Porpoise occurrence (December to May), including: - sheet piling works for construction of cofferdam surrounding the reclamation area (Phase 1); - sheet piling works for construction of the shorter section of breakwater (Phase 1); - sheet piling works for construction of the remaining section of breakwater (Phase 3); - bored piling works for berth area (Phase 3); and - submarine cable installation works between Shek Kwu Chau and Cheung Sha. Such works should be restricted within June to November. This approach would not only avoid the peak season for Finless Porpoise occurrence, the magnitude of impacts arise								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	from acoustic disturbance would also be minimised. • Submarine cable installation works are also recommended to be scheduled within June to November, when sightings of Finless Porpoise is scarce in the area of the proposed alignment of the submarine cable. • Since the DCM ground treatment and the installation of precast seawalls and breakwaters should generate no underwater acoustic disturbance to Finless Porpoise, no specific mitigation measures are required. *Opt for quieter construction methods and plants* • Considering the sensitivity of marine mammals to underwater acoustic disturbance, instead of the previously proposed conventional breakwater and reclamation peripheral structure, which requires noisy piling works, the current circular cells structure for breakwater and reclamation peripheral structure is proposed. A quieter sheet piling method using vibratory hammer or hydraulic impact hammer, should be adopted for the installation of circular cells for cellular cofferdam and northern breakwater during								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	Phase 1, and southern breakwater Phase 3; • Non-percussive bore piling method would be adopted for the installation of tubular piles for the berth construction during Phase 3. *Monitored exclusion zones* • During the installation/re-installation/relocation process of floating type silt curtains, in order to avoid the accidental entrance and entrapment of marine mammals within the silt curtains, a monitored exclusion zone of 250 m radius from silt curtain should be implemented. The exclusion zone should be closely monitored by an experienced marine mammal observer at least 30 minutes before the start of installation/re-installation/relocation process. If a marine mammal is noted within the exclusion zone, all marine works should stop immediately and remain idle for 30 minutes, or until the exclusion zone is free from marine mammals. • The experienced marine mammal observer should be well trained to detect marine mammals. Binoculars should be used to search the exclusion zone from an elevated platform with unobstructed visibility. The observer should also be independent								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	from the project proponent and has the power to call-off construction activities. • In addition, as marine mammals cannot be effectively monitored within the proposed monitored exclusion zone at night, or during adverse weather conditions (i.e. Beaufort 5 or above, visibility of 300 meters or below), marine works should be avoided under weather conditions with low visibility. *Marine mammal watching plan* • Upon the completion of the installation/re-installation/relocation of floating type silt curtain, all marine works would be conducted within a fully enclosed environment within the silt curtain, hence exclusion zone monitoring would no longer be required. Subsequently, a marine mammal watching plan should be implemented. The plan should include regular inspection of silt curtains, and visual inspection of the waters surrounded by the curtains. Special attention should be paid to Phase 2 (reclamation) where the floating type still curtain would be opened occasionally for vessel access, leaving a temporary 50 m opening. An action plan should be devised to cope with any unpredicted incidents such as the case when								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	marine mammals are found within the waters surrounded by the silt curtains. *Small openings at silt curtains* • The openings for vessel access at the silt curtains should be as small as possible to minimise the risk of accidental entrance. *Adoption of regular travel route* • During construction and operation, captains of all vessels should adopt regular travel route, in order to minimize the chance of vessel collision with marine mammals, which may otherwise result in damage to health or mortality. The regular travel route should avoid areas with high sighting density of Finless Porpoise as much as possible. *Vessel speed limit* • The frequent vessel traffic in the vicinity of works area may increase the chance of mammal mammals being killed or seriously injured by vessel collision. A speed limit of ten knots should be strictly enforced within areas with high density of Finless Porpoise. • Passive acoustic monitoring and land-based theodolite monitoring surveys should be								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	adopted to verify the predicted impacts and effectiveness of the proposed mitigation measures. *Training of Staff* • Staff, including captains of vessels, should be aware of the guidelines for safe vessel operations in the presence of cetaceans during construction and operation phases. Adequate trainings should be provided								
7b.8.3.31 - 7b.8.3.34	<u>Measures to minimise impact on corals</u> *Coral translocation* • Coral communities within and in proximity to the proposed dredging sites would be disturbed by the Project due to the dredging operations. In order to minimise direct loss of coral communities, translocation of corals that are attached to movable rocks with diameter less than 50 cm are recommended. In order to avoid disturbance to corals during the spawning period, the spawning season of corals (June to August) should be avoided; and that translocation should be carried out during the winter season (November-March).	IWMF site	Design team, contractor, IWMF operator	✓	✓	✓	✓	EIAO-TM	Implemented, tagged coral found missing after hitting by typhoons Re-tagging of 10 coral colonies at indirect impact site and control site were conducted in November and December 2018 respectively.

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	• The REA survey results suggest that the 198 directly affected coral colonies were attached to movable rocks (less than 50 cm in diameter). It is technically feasible to translocate them to avoid direct loss. • Prior to coral translocation, a more detailed baseline survey, including a coral mapping survey, is recommended to further confirm the exact number and location of coral colonies within the potentially affected area. A more detailed coral translocation plan, including selection of suitable recipient site, plan for coral translocation, and event / action plan for coral monitoring should be submitted upon approval of this Project, prior to commencement of construction works. Advice from relevant governmental departments (i.e. AFCD) and professionals would be sought after, in order to identify a desirable location for the relocation of coral communities. Post-translocation monitoring on the translocated corals should also be considered. *Coral monitoring programme* • A coral monitoring programme is recommended to assess any adverse and unacceptable impacts to the coral								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	communities at the coasts of Shek Kwu Chau during construction of the Project. *Phasing of Works* • To minimize environmental impacts, the proposed phasing of construction works has been carefully designed to reduce the amount of concurrent works, hence minimize SS elevation and the associated impacts on corals.								
7b.8.3.35 - 7b.8.3.41	<u>Specific measures to minimize disturbance on breeding White-bellied Sea Eagle</u> *Avoidance of noisy works during the breeding season of White-bellied Sea Eagle* • To minimize potential noise disturbance from construction activities on WBSE, noisy construction works should be scheduled outside their breeding season (December to May) to minimise potential degradation in breeding ground quality and breeding activities, including: - sheet piling works for construction of cofferdam surrounding the reclamation area (Phase 1); - sheet piling works for construction of the shorter section of breakwater (Phase 1);	IWMF site, marine traffic route	Design Team, Contractor, IWMF operator	✓	✓	✓	✓	EIAO-TM	Implemented

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	- sheet piling works for construction of the remaining section of breakwater (Phase 3); and - bored piling works for berth area (Phase 3). *Opt for quieter construction methods and plants* • To minimise potential construction noise disturbance on WBSE, quieter construction methods and plants should be adopted. The recommended noise mitigation measures in the **Noise** chapter (**Section 4b.8** of the EIA Report) should be implemented to minimise potential noise disturbance to acceptable levels. *Restriction on vessel access near the nest of White-bellied Sea Eagle* • During construction and operation, in order to minimize disturbance on the existing WBSE nest, a pre-defined practical route to restrict vessel access near the nest should be adopted to keep vessels and boats as far away from the nest as possible. *White-bellied Sea Eagle monitoring programme* • A WBSE monitoring programme is recommended to assess any adverse and unacceptable impacts to the breeding								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	activities of WBSE during construction and operation of the Project. Monitoring surveys for WBSE would include pre-construction phase (twice per month for duration of three months during their breeding season -between December and May, immediately before the commencement of works), construction phase, and operation phase (two years after the completion of construction works). • Surveys should be conducted twice per month during their breeding season (from December to May); and once per month outside breeding season (June to November). More details on monitoring for WBSE are presented in the EM&A Manual. *Education of staff* • Staff, including captains of all vessels during construction and operation phases, should be aware of the ecological importance of WBSE. Awareness should be raised among staff to minimise any intentional or unintentional disturbance to the nest. *Minimisation of Glare Disturbance* • To minimise glare disturbance on WBSE, which may cause disorientation of birds								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	by interfering with their magnetic compass, and disruption in behavioural patterns such as reproduction, fat storage and foraging pattern, any un-necessary outdoor lighting should be avoided, and in-ward and down-ward pointing of lights should be adopted.								
-	Construction of Seawall/Breakwaters • To widen the open channel between the Artificial Island and Shek Kwu Chau. • To design the precast concrete seawall with environmental friendly features.	IWMF site	Design team, contractor, IWMF operator	✓	✓			Supporting Document for Application for Variation of Environmental Permit (EP-429/2012)	N/A
7b.8.3.42	Opt for Quieter Construction Methods and Plants • Quieter construction methods and plants should be used to minimise disturbance to the nearby terrestrial habitat and the associated wildlife.	Work site	Design team, contractor, IWMF operator	✓	✓	✓	✓	EIAO-TM	Implemented
7b.8.3.43	Measures to minimize impacts from artificial lighting • Unnecessary lighting should be avoided, and shielding of lights should be provided to minimize disturbance from light pollution on fauna groups.	IWMF site	Design team, contractor, IWMF operator	✓	✓	✓		EIAO-TM	Implemented
7b.8.3.44 - 7b.8.3.45	Measures to minimize accidental spillage • Regular maintenance of vessels, vehicles and equipment that may cause leakage and spillage should only be undertaken within	Work site	Contractor, IWMF operator		✓	✓	✓	EIAO-TM	Deficiency of Mitigation Measures but rectified by the Contractor.

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	pre-designated areas, which are appropriately equipped to control the associated discharges. • Oils, fuels and chemicals should be contained in suitable containers, and only be used and stored in designated areas which have pollution prevention facilities. All fuel tanks and storage areas should be sited on sealed areas in order to prevent spillage of fuels and solvents to the nearby watercourses. All waste oils and fuels should be collected in designated tanks prior to disposal.								
7b.8.3.46	<u>Measures to minimise sewage effluent</u> • Temporary sanitary facilities, such as portable chemical toilets, should be employed on-site where necessary to handle sewage from the workforce.	Work site	Contractor		✓			EIAO-TM	N/A
7b.8.3.47	<u>Measures to minimise drainage and construction runoff</u> • Potential ecological impacts resulted from potential degradation of water quality due to unmitigated surface runoff could be minimised via the detailed mitigation measures in **Section 5b.8** of the EIA Report. The following presents some of the mitigation measures:	Work site	Contractor		✓		✓	EIAO-TM	N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	- On-site drainage system with implemented sedimentation control facilities. - Channels, earth bunds or sand bag barriers should be provided on site to direct storm water to silt removal facilities. - Provision of embankment at boundaries of earthworks for flood protection. - Water pumped out from foundation piles must be discharged into silt removal facilities. - During rainstorms, exposed slope/soil surfaces should be covered by tarpaulin or other means, as far as practicable. - Exposed soil surface should be minimized to reduce siltation and runoff. - Earthwork final surfaces should be well compacted. Subsequent permanent surface protection should be immediately performed. - Open stockpiles of construction materials, and construction wastes on-site should be covered with tarpaulin or similar fabric during rainstorms.								
7b.8.3.48	<u>Measures to minimise impacts from general construction activities</u> • To avoid the entering of construction solid waste into the nearby habitats, construction solid waste should be collected, handled	Work site	Contractor		✓			EIAO-TM	Implemented

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	and disposed of properly to avoid entering to the nearby habitats. It is recommended to clean the construction sites on a regular basis.								
7b.8.3.49	<u>Pest Control</u> Good waste management practices should be adopted at the IWMF in order to minimise the risk of introduction of pest to the island: - Transportation of wastes in enclosed containers - Waste storage area should be well maintained and cleaned - Waste should only be disposed of at designated areas - Timely removal of the newly arrived waste - Removal of items that are capable of retaining water - Rapid clean up of any waste spillages - Maintenance of a tidy and clean site environment - Regular application of pest control - Education of staff the importance of site cleanliness	IWMF site	IWMF operator			✓			N/A
7b.8.3.50	<u>Control of Marine Habitat Quality during Operation Phase</u> • Depending on the seabed condition of the approach channel for marine vessels during operation phase of the IWMF, maintenance dredging may be required to	IWMF site	IWMF operator			✓		EIAO-TM; WPCO	N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	ensure safe access. In order to avoid degradation in water quality due to elevation in SS and dispersion of sediment plume due to dredging works, it is recommended that any future maintenance dredging works should not be carried out within 100 m from the shore, similar to that of the dredging for anti-scouring protection layer during construction phase. All maintenance dredging works should be carried out with the implementation of silt curtain to control the dispersion of SS. The production rate should comply with the permit dredging rate and number of grab per hour.								
7b.8.4.1 – 7b.8.4.8	<u>Compensation of loss of important habitat of Finless Porpoise</u> *Designation of Marine Park* • The Project Proponent has made a firm commitment to seek to designate a marine park of approximately 700 ha in the waters between Soko Islands and Shek Kwu Chau, in accordance with the statutory process stipulated in the Marine Parks Ordinance, as a compensation measure for the habitat loss arising from the construction of the IWMF at the artificial island near SKC. • The Project Proponent shall seek to complete the designation by 2018 to tie in	Waters between Shek Kwu Chau and Soko Islands	Project Proponent	✓		✓		EIAO-TM	N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	with the operation of the IWMF at the artificial island near SKC. • A further study should be carried out to review relevant previous studies and collate available information on the ecological characters of the proposed area for marine park designation; and review available survey data for Finless Porpoise, water quality, fisheries, marine traffic and planned development projects in the vicinity. Based on the findings, ecological profiles of the proposed area for marine park designation should be established, and the extent and location of the proposed marine park be determined. The adequacy of enhancement measures should also be reviewed. • In addition, a management plan for the proposed marine park should be proposed, covering information on the responsible departments for operation and management (O&M) of the marine park, as well as the O&M duties of each of the departments involved. Consultation with relevant government departments and stakeholders should be conducted under the study. The study should be submitted to Director of Environmental Protection (DEP) for approval before the commencement of construction works.								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	• The Project Proponent should provide assistance to AFCD during the process of the marine park designation. .								
7b.8.5.1 – 7b.8.5.4	Additional Enhancement or Precautionary Measures *Deployment of Artificial Reefs* • Deployment of artificial reefs (ARs) is an enhancement measure for the marine habitats. ARs are proposed to be deployed within the proposed marine park under this Project. The exact location, dimension and type of ARs to be deployed are to be further investigated along with the further study of the proposed marine park under this Project. The proposed ARs would be deployed at the same time as the complete designation of marine park. *Release of Fish Fry at Artificial Reefs and Marine Park* • Release of fish fry at the proposed ARs, as well as the proposed marine park under this study, should enhance the fish resources in the nearby waters, and subsequently food sources for Finless Porpoise. The proposed ARs with various micro-habitats would have the potential to provide shelter and nursery ground for the released fish fry.	Within the proposed marine park under this study	Project Proponent	✓		✓		EIAO-TM	N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
	The frequency and quantity of fry to be released should be agreed by AFCD.								

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Table B.6 Implementation Schedule for Fisheries Measures for the IWMF at the artificial island near SKC

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
8b.8.1.2	Measure to minimize loss of and disturbance on fisheries resources • Alteration to the phasing of works, construction method, and layout plan of the IWMF at the artificial island near SKC has been made. The total fishing ground to be permanently lost due to the project has been significantly reduced from ~50 ha to ~31 ha. By adopting the current circular cells instead of the conventional seawall construction method, SS elevation would be greatly reduced, minimizing adverse impact on the health of fisheries resources.	IWMF site	Design team, contractor	✓	✓		✓	EIAO-TM	N/A
8b.8.1.3	Measure to minimize impingement and entrainment • Provision of a screen at the water intake point for desalination plant would be essential to minimize the risk of impingement and entrainment of fisheries resources (including fish, larvae and egg) through the intake point.	IWMF site	Design team, contractor, IWMF operator	✓	✓	✓		EIAO-TM	N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
8b.8.1.4-8b.8.1.6	<u>Measures to control water quality</u> • No wastewater effluent, anti-fouling agent, heavy metals and other contaminants would be released during operation phase of the Project. • Mitigation measures recommended in the water quality impact assessment during construction and operation would serve to protect fisheries resources from indirect impacts resulted from the Project	Work site, IWMF site	Design team, contractor, IWMF operator	✓	✓	✓	✓	EIAO-TM	Implemented
8b.8.1.7 – 8b.8.1.8	<u>Additional Enhancement / Precautionary Measures</u> • Artificial Reefs (ARs) are proposed to be deployed within the proposed marine park under this Project as an enhancement measure for the marine habitats. This enhancement feature would bring positive impacts to the previously identified important spawning and nursery ground for fisheries resources. *Release of Fish Fry at Artificial Reefs* • Release of fish fry has been proposed under this Project. The proposed deployment of ARs within the proposed marine park would provide shelter and nursery ground for the released fish fry. The frequency and quantity of fry to be released should be agreed by AFCD.	Within the proposed marine park in the waters between Soko Islands and Shek Kwu Chau	Project Proponent	✓		✓		EIAO-TM	N/A

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Table B.7 Implementation Schedule for Landscape and Visual Measures for the IWMF at the artificial island near SKC

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
S10b.10 MLVC- 01	Grass-hydroseeded bare soil surface and stock pile area	Work site / During construction phase	Contractor		✓				N/A
S10b.10 MLVC-02	<u>Landscape Design</u> 1) Early planting using fast grow trees and tall shrubs at strategic locations within site as buffer to block view corridors to the site from the VSRs, and to locally screen haul roads, excavation works and site preparation works. 2) Use of tree species of dense tree crown to serve as visual barrier. 3) Hard and soft landscape treatment (e.g. trees and shrubs) of open areas within development to provide a background for the outdoor containers from open view, shade and shelter, and a green appearance from surrounding viewpoints. 4) Planting strip along the periphery of the project site. 5) Selected tree species suitable for the coastal condition.	Work site / During design & construction phases	Contractor	✓	✓				N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
S10b.10 MLVC-03	<u>Adoption of Natural Features of the Existing Shoreline</u> 1) Use of boulders in different sizes and with the similar textures of the existing rocky shores for the construction of breakwater and artificial shoreline in order to blend into the existing natural shoreline. 2) Use of cellular cofferdam together with the natural boulders to form a curvature shoreline for the reclamation area to echo with the natural shoreline of SKC.	Work site / During construction phase	Contractor		✓				N/A
S10b.10 MLVC-04	<u>Greening Design (Rooftop & Vertical Greening)</u> 1) Implementation of rooftop and vertical greening (vertical building envelope) along the periphery of each building block to increase the amenity value of the work, moderate temperature extremes and enhance building energy performance. The greening appearance of the building shall enhance its visual harmony with the natural surroundings as well as reduce the apparent visual mass of the structure. 2) Sufficient space between concrete enclosure and stack to minimize heat transfer. 3) Introduction of landscape decks at the stack to further enhance the overall natural and green concept unique for this site.	Work site / During design & construction phases	Contractor	✓	✓				N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
S10b.10 MVC-01	<u>Visual Mitigation and Aesthetic Design</u> 1) Use of natural materials with recessive color to minimize the bulkiness of the building. 2) Adoption of innovative aesthetic design to the chimney to minimize or visually mitigate the massing of the chimney so as to reduce its visual impact to the surroundings. 3) Color of the chimney in a gradual changing manner to match with the color of the sky. 4) Provision of observation deck for public enjoyment at the top of the chimney to diminish the feeling of chimney. 5) Provision of sky gardens between the two stacks to allow additional greening for enhancing the aesthetic quality. Maintenance access (elevator and staircase) from the ground floor to the sky gardens will be provided to allow maintenance of the sky gardens. 6) Integration of the visitor's walkway with different material façade design of incinerator plant to enhance the aesthetic quality.	Structures in IWMF / During design & constructio n phases	Contractor	✓	✓				N/A
S10b.10 MVC-02	Control of the security floodlight for construction areas at night to avoid excessive glare to the surrounding receiver.	Work site / During construction phase	Contractor		✓				Implemented

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
S10b.10 MVC-03	Optimization of the construction sequence and construction programme to minimize the duration of impact.	Work site / During design & construction phases	Contractor	✓	✓				Implemented
S10b.10 MVC-04	Storage of the backfilling materials for site formation & construction materials / wastes on site at a maximum height of 2m, covered with an impermeable material of visually un-obtrusive material (in earth tone).	Work site / During construction phase	Contractor		✓				N/A
S10b.10 MVC-05	Reduction of the number of construction traffic at the site to practical minimum.	Work site / During construction phase	Contractor		✓				Implemented
S10b.10 MLVO-01	<u>Planting Maintenance</u> Provision of proper planting maintenance and replacement of defective plant species on the new planting areas to enhance aesthetic and landscape quality.	Project site / During Operation phase	Contractor			✓			N/A
S10b.10 MVO-01	<u>Environmental Education Centre</u> Development of an Environmental Education Center, in which regular exhibitions and lectures to promote environmental awareness and waste reduction concept would be provided, as a part of the IWMF for the general public to alleviate negative public perceptions of the development.	Project site / During Operation phase	Contractor			✓			N/A
S10b.10 MVO-02	<u>Control of Light</u> Control the numbers of lights and their intensity to a level that is good enough to meet the safety requirements at night but not excessive.	Project site / During Operation phase	Contractor			✓			N/A

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	Implementation Status and Remarks
				Des	C	O	Dec		
S10b.10 MVO-03	<u>Control of Operation Time</u> Minimization of the frequency of waste transportation to practical minimum (e.g. limit the reception of MSW from 8 am to 8 pm)	Project site / During Operation phase	Contractor			✓			N/A

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Appendix C Impact Monitoring Schedule of the Reporting Month

Impact Monitoring Schedule for IWMF

Jan-21

Sun	Mon	Tue	Wed	Thu	Fri	Sat
					1	2
						Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 12:48 - 16:00 Flood Tide: 06:00 - 12:48 Monitoring Time: Mid-ebb: 11:30 - 17:00 *Mid-flood: 08:00 - 11:30
3	4	5	6	7	8	9
	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 14:33 - 18:07 Flood Tide: 07:18 - 14:33 Monitoring Time: Mid-ebb: 14:35- 18:05 Mid-flood: 09:10 - 12:40 Daytime, Evening & Night time Noise monitoring for M1, M2 & M3	Impact Daytime, Evening & Night time Noise monitoring for M1, M2 & M3	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 16:00 - 20:34 Flood Tide: 08:50 - 16:00 Monitoring Time: &Mid-ebb: 15:30 - 19:00 Mid-flood: 10:40 - 14:10	Impact Ecology monitoring for WBSE		Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 07:00 - 11:00 Flood Tide: 11:00 - 18:19 Monitoring Time: *Mid-ebb: 08:00 - 11:30 Mid-flood: 12:54 - 16:24
10	11	12	13	14	15	16
	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 09:29 - 12:58 Flood Tide: 12:58 - 19:34 Monitoring Time: Mid-ebb: 09:28 - 12:58 & Mid-flood: 14:31 - 18:01 Daytime, Evening & Night time Noise monitoring for M1, M2 & M3	Impact Daytime, Evening & Night time Noise monitoring for M1, M2 & M3	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 11:00 - 14:34 Flood Tide: 14:34 - 21:00 Monitoring Time: Mid-ebb: 11:02 - 14:32 &Mid-flood: 15:30 - 19:00	Impact Ecology monitoring for WBSE	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 12:24 - 16:02 Flood Tide: 05:24 - 12:24 Monitoring Time: Mid-ebb: 12:28 - 15:58 * Mid-flood: 08:00 - 11:30 Ecology monitoring for Marine Mammals by Vessel-based Line-Transect Survey	
17	18	19	20	21	22	23
	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 14:00 - 18:15 Flood Tide: 07:00 - 14:00 Monitoring Time: Mid-ebb: 14:22 - 17:52 & Mid-flood: 08:45 - 12:15 Daytime, Evening & Night time Noise monitoring for M1, M2 & M3	Impact Daytime, Evening & Night time Noise monitoring for M1, M2 & M3	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 08:00 - 16:00 Flood Tide: 16:00 - 20:27 Monitoring Time: * Mid-ebb: 16:28 - 19:58 Mid-flood: 10:15 - 13:45	Impact Ecology monitoring for WBSE	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 03:10 - 09:00 Flood Tide: 09:00 - 17:35 Monitoring Time: * Mid-ebb: 08:00 - 11:30 Mid-flood: 13:02 - 16:32	
24	25	26	27	28	29	30
	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 08:00 - 12:00 Flood Tide: 12:00 - 18:44 Monitoring Time: Mid-ebb: 08:15 - 11:45 Mid-flood: 13:37 - 17:07 Daytime, Evening & Night time Noise monitoring for M1, M2 & M3 Ecology monitoring for Marine Mammals by Vessel-based Line-Transect Survey	Impact Daytime, Evening & Night time Noise monitoring for M1, M2 & M3	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 10:00 - 13:00 Flood Tide: 13:00 - 20:00 Monitoring Time: Mid-ebb: 09:45 - 13:15 Mid-flood: 14:45 - 18:15	Impact Ecology monitoring for WBSE	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 11:00 - 15:00 Flood Tide: 15:00 - 21:00 Monitoring Time: Mid-ebb: 11:15 - 14:45 &Mid-flood: 15:30 - 19:00	
31						
Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 12:00 - 16:33 Flood Tide: 05:32 - 12:00 Monitoring Time: Mid-ebb: 12:31 - 16:01 *Mid-flood: 08:00 - 11:30						

Remarks:
1. Daytime Noise Monitoring (07:00-1900), Evening Time Noise Monitoring (1900-2300), Night Time Noise Monitoring (2300-0700)
2. Water Quality Monitoring for S1,S2 and S3 will only conduct during DCM works, refer to Detailed DCM Plan

Note:
* - as per Marine Department Notice No 107 of 2018, all vessels employed for the works should stay in the works area outside the hours of works (0700 to 2300). Due to safty concern, Water Quality Monitoring would start at 0800.
- Prioritized routing: Mid-Ebb: C1→S3→CR2→CR1→H1→Remaining stations and Mid-Flood: C2→CR1→S3→CR2→H1→Remaining stations
$ - Since predicted tide is shorter than 3.5 hours, method of 90% tidal period as monitoring time is approached.
& - Due to safety concern for sampling event in night-time, method of 90% tidal period as monitoring time is approached and end at 1900.

Appendix D Water Quality Monitoring Data

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B1	20210102	Sunny	Moderate	Mid-Flood	Bottom	3.6	10:22	10.6	8.3	30.7	17.6	2.9	4	-	-	-
B1	20210102	Sunny	Moderate	Mid-Flood	Bottom	3.6	10:22	9.9	8.4	31.1	17.7	3.4	5	-	-	-
B1	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	10:23	10.2	8.4	30.6	17.6	2.3	5	-	-	-
B1	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	10:23	9.2	8.3	30.6	17.9	2.6	4	-	-	-
B2	20210102	Sunny	Moderate	Mid-Flood	Bottom	4.0	10:09	9.3	8.5	30.7	17.6	3.0	4	-	-	-
B2	20210102	Sunny	Moderate	Mid-Flood	Bottom	4.0	10:09	10.1	8.3	30.9	17.7	3.4	5	-	-	-
B2	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	10:10	9.7	8.3	30.9	17.8	2.7	6	-	-	-
B2	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	10:10	9.6	8.3	30.8	17.8	2.9	5	-	-	-
B3	20210102	Sunny	Moderate	Mid-Flood	Bottom	3.5	9:51	9.5	8.2	30.9	17.7	3.9	4	-	-	-
B3	20210102	Sunny	Moderate	Mid-Flood	Bottom	3.5	9:51	9.4	8.4	30.9	17.7	3.5	4	-	-	-
B3	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	9:52	9.7	8.4	31.2	17.4	2.7	4	-	-	-
B3	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	9:52	9.7	8.3	31.1	17.7	2.8	5	-	-	-
B4	20210102	Sunny	Moderate	Mid-Flood	Bottom	4.5	9:43	9.8	8.3	30.7	17.5	3.0	5	-	-	-
B4	20210102	Sunny	Moderate	Mid-Flood	Bottom	4.5	9:43	9.7	8.4	31.2	17.6	2.8	4	-	-	-
B4	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	9:44	10.8	8.4	30.7	17.6	2.9	4	-	-	-
B4	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	9:44	10.2	8.2	30.9	17.7	3.2	5	-	-	-
C1A	20210102	Sunny	Moderate	Mid-Flood	Bottom	9.7	8:56	10.6	8.5	31.2	17.2	3.1	4	-	-	-
C1A	20210102	Sunny	Moderate	Mid-Flood	Bottom	9.7	8:56	9.8	8.4	31.1	17.5	3.4	5	-	-	-
C1A	20210102	Sunny	Moderate	Mid-Flood	Middle	5.4	8:57	10.7	8.3	30.9	16.2	2.7	4	-	-	-
C1A	20210102	Sunny	Moderate	Mid-Flood	Middle	5.4	8:57	10.2	8.5	31.0	16.3	2.9	5	-	-	-
C1A	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	8:58	10.0	8.3	30.6	16.3	2.9	5	-	-	-
C1A	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	8:58	10.7	8.3	30.9	17.2	2.4	5	-	-	-
C2A	20210102	Sunny	Moderate	Mid-Flood	Bottom	10.6	8:00	10.4	8.5	31.1	17.0	3.9	4	-	-	-
C2A	20210102	Sunny	Moderate	Mid-Flood	Bottom	10.6	8:00	10.7	8.3	30.6	17.1	3.7	4	-	-	-
C2A	20210102	Sunny	Moderate	Mid-Flood	Middle	5.8	8:01	9.8	8.3	31.0	17.1	2.6	5	-	-	-
C2A	20210102	Sunny	Moderate	Mid-Flood	Middle	5.8	8:01	10.6	8.6	30.7	17.3	2.8	4	-	-	-
C2A	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	8:02	9.8	8.2	31.1	16.9	2.4	4	-	-	-
C2A	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	8:02	10.2	8.4	31.1	17.1	2.5	5	-	-	-
CR1	20210102	Sunny	Moderate	Mid-Flood	Bottom	11.7	8:22	10.5	8.4	30.7	17.1	3.3	5	-	-	-
CR1	20210102	Sunny	Moderate	Mid-Flood	Bottom	11.7	8:22	9.3	8.3	31.1	17.2	3.6	4	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
CR1	20210102	Sunny	Moderate	Mid-Flood	Middle	6.4	8:23	10.4	8.5	30.6	17.2	3.3	5	-	-	-
CR1	20210102	Sunny	Moderate	Mid-Flood	Middle	6.4	8:23	9.8	8.3	31.3	17.3	3.3	6	-	-	-
CR1	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	8:24	9.1	8.4	30.9	17.3	2.9	5	-	-	-
CR1	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	8:24	9.2	8.2	30.8	17.0	2.8	6	-	-	-
CR2	20210102	Sunny	Moderate	Mid-Flood	Bottom	10.4	8:36	10.2	8.5	30.6	17.5	4.0	6	-	-	-
CR2	20210102	Sunny	Moderate	Mid-Flood	Bottom	10.4	8:36	9.7	8.5	31.1	17.0	3.3	6	-	-	-
CR2	20210102	Sunny	Moderate	Mid-Flood	Middle	5.7	8:37	9.1	8.4	30.8	17.3	3.1	6	-	-	-
CR2	20210102	Sunny	Moderate	Mid-Flood	Middle	5.7	8:37	9.1	8.2	30.9	17.1	2.7	6	-	-	-
CR2	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	8:38	10.0	8.5	30.8	17.2	3.2	7	-	-	-
CR2	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	8:38	10.0	8.6	30.9	17.2	3.1	7	-	-	-
F1A	20210102	Sunny	Moderate	Mid-Flood	Bottom	6.7	9:20	10.4	8.5	31.2	17.6	3.4	5	-	-	-
F1A	20210102	Sunny	Moderate	Mid-Flood	Bottom	6.7	9:20	10.1	8.3	30.8	17.6	2.9	6	-	-	-
F1A	20210102	Sunny	Moderate	Mid-Flood	Middle	3.9	9:21	9.5	8.6	30.8	17.6	3.2	5	-	-	-
F1A	20210102	Sunny	Moderate	Mid-Flood	Middle	3.9	9:21	9.1	8.5	30.7	17.6	2.7	6	-	-	-
F1A	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	9:22	10.3	8.3	31.1	17.6	2.8	5	-	-	-
F1A	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	9:22	10.0	8.3	31.0	17.6	2.5	6	-	-	-
H1	20210102	Sunny	Moderate	Mid-Flood	Bottom	7.6	9:22	10.3	8.4	30.6	17.5	3.4	3	-	-	-
H1	20210102	Sunny	Moderate	Mid-Flood	Bottom	7.6	9:22	10.5	8.3	30.6	17.5	3.4	4	-	-	-
H1	20210102	Sunny	Moderate	Mid-Flood	Middle	4.3	9:23	10.0	8.3	31.3	17.4	3.2	5	-	-	-
H1	20210102	Sunny	Moderate	Mid-Flood	Middle	4.3	9:23	9.4	8.3	30.7	17.6	3.2	5	-	-	-
H1	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	9:24	9.6	8.6	30.9	17.2	2.8	5	-	-	-
H1	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	9:24	9.9	8.2	30.7	17.3	3.4	6	-	-	-
M1	20210102	Sunny	Moderate	Mid-Flood	Bottom	7.2	8:59	9.2	8.3	31.0	17.2	3.0	4	-	-	-
M1	20210102	Sunny	Moderate	Mid-Flood	Bottom	7.2	8:59	10.1	8.4	30.7	17.3	2.8	3	-	-	-
M1	20210102	Sunny	Moderate	Mid-Flood	Middle	4.1	9:00	9.7	8.5	30.7	17.2	3.2	5	-	-	-
M1	20210102	Sunny	Moderate	Mid-Flood	Middle	4.1	9:00	10.1	8.4	31.0	17.6	2.9	6	-	-	-
M1	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	9:01	9.1	8.3	31.2	17.5	3.0	6	-	-	-
M1	20210102	Sunny	Moderate	Mid-Flood	Surface	1.0	9:01	9.6	8.3	30.9	17.3	2.6	5	-	-	-
B1	20210102	Sunny	Moderate	Mid-Ebb	Bottom	3.7	13:30	9.3	8.5	31.0	18.7	3.3	5	-	-	-
B1	20210102	Sunny	Moderate	Mid-Ebb	Bottom	3.7	13:30	9.5	8.5	30.7	18.5	3.1	6	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B1	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:31	9.6	8.5	31.0	18.4	2.8	6	-	-	-
B1	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:31	10.2	8.5	31.1	18.6	2.5	6	-	-	-
B2	20210102	Sunny	Moderate	Mid-Ebb	Bottom	4.7	13:44	9.2	8.4	30.9	18.7	2.9	7	-	-	-
B2	20210102	Sunny	Moderate	Mid-Ebb	Bottom	4.7	13:44	10.4	8.5	31.1	18.4	3.1	8	-	-	-
B2	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:45	10.3	8.3	30.7	18.8	3.0	7	-	-	-
B2	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:45	10.4	8.3	30.5	18.8	3.2	6	-	-	-
B3	20210102	Sunny	Moderate	Mid-Ebb	Bottom	3.5	14:02	9.5	8.4	30.8	18.3	3.3	6	-	-	-
B3	20210102	Sunny	Moderate	Mid-Ebb	Bottom	3.5	14:02	9.9	8.4	31.0	18.4	3.0	6	-	-	-
B3	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:03	10.2	8.3	30.6	18.5	2.2	4	-	-	-
B3	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:03	9.1	8.4	30.8	18.7	2.4	5	-	-	-
B4	20210102	Sunny	Moderate	Mid-Ebb	Bottom	3.1	14:10	9.3	8.4	30.7	18.3	3.0	5	-	-	-
B4	20210102	Sunny	Moderate	Mid-Ebb	Bottom	3.1	14:10	10.0	8.3	30.6	18.4	2.9	6	-	-	-
B4	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:11	10.3	8.4	30.9	18.5	2.4	7	-	-	-
B4	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:11	10.1	8.4	30.6	18.4	2.5	7	-	-	-
C1A	20210102	Sunny	Moderate	Mid-Ebb	Bottom	8.8	13:30	9.6	8.5	30.9	18.6	3.0	7	-	-	-
C1A	20210102	Sunny	Moderate	Mid-Ebb	Bottom	8.8	13:30	9.7	8.4	30.4	18.6	2.6	8	-	-	-
C1A	20210102	Sunny	Moderate	Mid-Ebb	Middle	4.9	13:31	10.5	8.5	30.7	18.5	2.6	8	-	-	-
C1A	20210102	Sunny	Moderate	Mid-Ebb	Middle	4.9	13:31	9.9	8.3	31.1	18.4	2.4	7	-	-	-
C1A	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:32	10.0	8.3	31.1	18.3	2.5	6	-	-	-
C1A	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:32	9.8	8.3	31.1	18.4	2.4	6	-	-	-
C2A	20210102	Sunny	Moderate	Mid-Ebb	Bottom	11.5	14:45	9.9	8.3	30.6	18.2	3.1	4	-	-	-
C2A	20210102	Sunny	Moderate	Mid-Ebb	Bottom	11.5	14:45	10.0	8.4	30.7	18.5	2.7	5	-	-	-
C2A	20210102	Sunny	Moderate	Mid-Ebb	Middle	6.3	14:46	9.3	8.4	30.7	18.2	2.4	4	-	-	-
C2A	20210102	Sunny	Moderate	Mid-Ebb	Middle	6.3	14:46	9.6	8.5	30.7	18.5	2.7	5	-	-	-
C2A	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:47	10.0	8.4	30.6	18.5	2.9	4	-	-	-
C2A	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:47	9.6	8.4	31.2	18.5	3.1	5	-	-	-
CR1	20210102	Sunny	Moderate	Mid-Ebb	Bottom	12.1	14:21	10.1	8.5	30.8	18.3	3.5	5	-	-	-
CR1	20210102	Sunny	Moderate	Mid-Ebb	Bottom	12.1	14:21	9.6	8.6	31.1	18.3	3.1	5	-	-	-
CR1	20210102	Sunny	Moderate	Mid-Ebb	Middle	6.6	14:22	10.0	8.3	31.0	18.4	3.3	4	-	-	-
CR1	20210102	Sunny	Moderate	Mid-Ebb	Middle	6.6	14:22	9.9	8.4	31.0	18.4	3.1	5	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
CR1	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:23	9.9	8.3	30.8	18.2	3.1	3	-	-	-
CR1	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:23	10.4	8.4	30.7	18.3	2.6	4	-	-	-
CR2	20210102	Sunny	Moderate	Mid-Ebb	Bottom	10.3	14:08	10.3	8.4	31.0	18.6	3.8	4	-	-	-
CR2	20210102	Sunny	Moderate	Mid-Ebb	Bottom	10.3	14:08	9.2	8.4	30.7	18.6	3.8	5	-	-	-
CR2	20210102	Sunny	Moderate	Mid-Ebb	Middle	5.7	14:09	10.0	8.3	30.5	18.5	3.5	5	-	-	-
CR2	20210102	Sunny	Moderate	Mid-Ebb	Middle	5.7	14:09	10.6	8.5	31.1	18.3	3.0	5	-	-	-
CR2	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:10	10.2	8.3	31.0	18.5	2.7	5	-	-	-
CR2	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:10	9.4	8.5	31.0	18.5	2.7	5	-	-	-
F1A	20210102	Sunny	Moderate	Mid-Ebb	Bottom	7.3	14:56	9.0	8.5	30.8	18.4	3.4	5	-	-	-
F1A	20210102	Sunny	Moderate	Mid-Ebb	Bottom	7.3	14:56	10.5	8.5	30.8	18.1	3.1	6	-	-	-
F1A	20210102	Sunny	Moderate	Mid-Ebb	Middle	4.2	14:57	9.0	8.3	30.6	18.3	3.0	5	-	-	-
F1A	20210102	Sunny	Moderate	Mid-Ebb	Middle	4.2	14:57	10.0	8.3	31.2	18.2	2.9	6	-	-	-
F1A	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:58	9.6	8.5	31.1	18.2	2.7	5	-	-	-
F1A	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:58	9.0	8.6	30.8	18.1	2.9	5	-	-	-
H1	20210102	Sunny	Moderate	Mid-Ebb	Bottom	7.3	13:54	9.1	8.5	30.5	18.7	3.1	4	-	-	-
H1	20210102	Sunny	Moderate	Mid-Ebb	Bottom	7.3	13:54	9.2	8.3	30.9	18.6	2.8	5	-	-	-
H1	20210102	Sunny	Moderate	Mid-Ebb	Middle	4.2	13:55	9.1	8.5	30.6	18.6	2.5	4	-	-	-
H1	20210102	Sunny	Moderate	Mid-Ebb	Middle	4.2	13:55	10.0	8.3	30.6	18.8	2.8	5	-	-	-
H1	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:56	10.3	8.4	30.6	18.8	2.9	5	-	-	-
H1	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:56	9.0	8.3	30.5	18.7	3.2	6	-	-	-
M1	20210102	Sunny	Moderate	Mid-Ebb	Bottom	7.9	14:34	10.5	8.3	31.0	18.4	3.7	5	-	-	-
M1	20210102	Sunny	Moderate	Mid-Ebb	Bottom	7.9	14:34	9.8	8.5	31.0	18.6	3.7	6	-	-	-
M1	20210102	Sunny	Moderate	Mid-Ebb	Middle	4.5	14:35	9.0	8.5	30.4	18.4	2.9	5	-	-	-
M1	20210102	Sunny	Moderate	Mid-Ebb	Middle	4.5	14:35	9.5	8.5	31.1	18.4	3.3	6	-	-	-
M1	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:36	10.4	8.3	31.0	18.5	2.5	7	-	-	-
M1	20210102	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:36	9.6	8.3	30.8	18.2	2.1	7	-	-	-
B1	20210104	Cloudy	Moderate	Mid-Flood	Bottom	4.0	11:23	9.8	8.4	31.1	18.8	2.3	4	-	-	-
B1	20210104	Cloudy	Moderate	Mid-Flood	Bottom	4.0	11:23	9.6	8.4	30.4	18.7	2.1	5	-	-	-
B1	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:24	9.7	8.4	30.4	19.0	3.3	6	-	-	-
B1	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:24	10.0	8.4	30.5	18.8	2.8	5	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B2	20210104	Cloudy	Moderate	Mid-Flood	Bottom	4.0	11:10	10.3	8.5	30.7	18.9	3.0	8	-	-	-
B2	20210104	Cloudy	Moderate	Mid-Flood	Bottom	4.0	11:10	9.4	8.6	31.0	18.9	3.4	7	-	-	-
B2	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:11	9.7	8.6	30.5	18.9	2.1	5	-	-	-
B2	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:11	8.9	8.6	30.5	18.9	2.4	5	-	-	-
B3	20210104	Cloudy	Moderate	Mid-Flood	Bottom	4.2	10:51	9.1	8.5	31.1	18.7	2.7	5	-	-	-
B3	20210104	Cloudy	Moderate	Mid-Flood	Bottom	4.2	10:51	9.9	8.6	30.9	18.8	2.9	4	-	-	-
B3	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:52	8.8	8.6	30.4	18.8	2.5	6	-	-	-
B3	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:52	9.1	8.6	30.4	18.8	2.1	5	-	-	-
B4	20210104	Cloudy	Moderate	Mid-Flood	Bottom	3.9	10:43	10.1	8.4	30.7	18.7	3.6	7	-	-	-
B4	20210104	Cloudy	Moderate	Mid-Flood	Bottom	3.9	10:43	10.4	8.5	30.4	18.6	3.7	6	-	-	-
B4	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:44	9.1	8.6	30.7	18.7	3.1	7	-	-	-
B4	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:44	8.7	8.5	30.9	18.6	3.3	7	-	-	-
C1A	20210104	Cloudy	Moderate	Mid-Flood	Bottom	10.0	10:08	9.0	8.6	31.1	18.7	3.4	5	-	-	-
C1A	20210104	Cloudy	Moderate	Mid-Flood	Bottom	10.0	10:08	10.0	8.4	31.0	18.7	3.1	4	-	-	-
C1A	20210104	Cloudy	Moderate	Mid-Flood	Middle	5.5	10:09	8.8	8.4	30.9	18.5	3.0	6	-	-	-
C1A	20210104	Cloudy	Moderate	Mid-Flood	Middle	5.5	10:09	8.7	8.6	30.8	18.5	2.7	5	-	-	-
C1A	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:10	10.5	8.4	31.0	18.6	2.8	6	-	-	-
C1A	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:10	9.0	8.6	30.7	18.7	2.4	6	-	-	-
C2A	20210104	Cloudy	Moderate	Mid-Flood	Bottom	10.9	9:10	9.6	8.5	30.8	18.5	3.5	6	-	-	-
C2A	20210104	Cloudy	Moderate	Mid-Flood	Bottom	10.9	9:10	9.1	8.6	30.5	18.5	3.2	7	-	-	-
C2A	20210104	Cloudy	Moderate	Mid-Flood	Middle	6.0	9:11	9.0	8.3	30.5	18.6	2.5	5	-	-	-
C2A	20210104	Cloudy	Moderate	Mid-Flood	Middle	6.0	9:11	9.8	8.3	30.7	18.4	2.7	6	-	-	-
C2A	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	9:12	9.8	8.4	30.7	18.5	3.2	5	-	-	-
C2A	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	9:12	10.2	8.5	31.0	18.4	2.9	6	-	-	-
CR1	20210104	Cloudy	Moderate	Mid-Flood	Bottom	11.7	9:34	10.1	8.5	31.0	18.4	3.3	4	-	-	-
CR1	20210104	Cloudy	Moderate	Mid-Flood	Bottom	11.7	9:34	9.7	8.6	30.7	18.7	3.7	5	-	-	-
CR1	20210104	Cloudy	Moderate	Mid-Flood	Middle	6.4	9:35	9.1	8.5	31.0	18.6	3.0	4	-	-	-
CR1	20210104	Cloudy	Moderate	Mid-Flood	Middle	6.4	9:35	8.8	8.4	30.7	18.5	2.9	4	-	-	-
CR1	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	9:36	10.2	8.4	30.7	18.6	2.9	4	-	-	-
CR1	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	9:36	8.8	8.4	30.7	18.7	3.4	4	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
CR2	20210104	Cloudy	Moderate	Mid-Flood	Bottom	10.1	9:49	9.9	8.5	30.8	18.7	3.2	6	-	-	-
CR2	20210104	Cloudy	Moderate	Mid-Flood	Bottom	10.1	9:49	10.0	8.3	30.9	18.7	3.3	5	-	-	-
CR2	20210104	Cloudy	Moderate	Mid-Flood	Middle	5.6	9:50	10.1	8.6	30.8	18.5	3.2	5	-	-	-
CR2	20210104	Cloudy	Moderate	Mid-Flood	Middle	5.6	9:50	9.3	8.5	30.7	18.6	3.2	5	-	-	-
CR2	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	9:51	9.7	8.7	30.6	18.5	2.9	5	-	-	-
CR2	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	9:51	10.4	8.5	31.0	18.6	3.4	5	-	-	-
F1A	20210104	Cloudy	Moderate	Mid-Flood	Bottom	7.7	10:21	9.0	8.4	30.6	18.6	2.7	5	-	-	-
F1A	20210104	Cloudy	Moderate	Mid-Flood	Bottom	7.7	10:21	9.8	8.4	30.7	18.5	2.9	5	-	-	-
F1A	20210104	Cloudy	Moderate	Mid-Flood	Middle	4.4	10:22	9.0	8.5	30.7	18.7	2.5	4	-	-	-
F1A	20210104	Cloudy	Moderate	Mid-Flood	Middle	4.4	10:22	9.6	8.5	30.8	18.6	2.7	5	-	-	-
F1A	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:23	8.9	8.5	30.5	18.7	2.5	4	-	-	-
F1A	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:23	9.7	8.5	31.1	18.6	2.9	3	-	-	-
H1	20210104	Cloudy	Moderate	Mid-Flood	Bottom	7.4	10:42	9.7	8.5	31.0	18.8	3.5	4	-	-	-
H1	20210104	Cloudy	Moderate	Mid-Flood	Bottom	7.4	10:42	10.1	8.4	30.5	18.6	3.0	4	-	-	-
H1	20210104	Cloudy	Moderate	Mid-Flood	Middle	4.2	10:43	9.7	8.4	30.7	18.5	2.9	4	-	-	-
H1	20210104	Cloudy	Moderate	Mid-Flood	Middle	4.2	10:43	9.1	8.5	31.0	18.6	3.2	4	-	-	-
H1	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:44	9.2	8.3	30.7	18.7	2.4	3	-	-	-
H1	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:44	9.5	8.6	30.4	18.7	2.7	3	-	-	-
M1	20210104	Cloudy	Moderate	Mid-Flood	Bottom	7.6	9:58	10.4	8.5	30.9	18.7	3.2	2	-	-	-
M1	20210104	Cloudy	Moderate	Mid-Flood	Bottom	7.6	9:58	10.1	8.3	30.7	18.5	3.3	3	-	-	-
M1	20210104	Cloudy	Moderate	Mid-Flood	Middle	4.3	9:59	8.9	8.3	30.5	18.7	2.9	3	-	-	-
M1	20210104	Cloudy	Moderate	Mid-Flood	Middle	4.3	9:59	10.3	8.6	30.8	18.5	3.3	3	-	-	-
M1	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:00	9.5	8.5	30.7	18.7	2.8	3	-	-	-
M1	20210104	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:00	9.1	8.3	30.5	18.6	3.0	3	-	-	-
B1	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	3.8	14:35	9.0	8.6	30.8	19.2	3.0	4	-	-	-
B1	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	3.8	14:35	9.6	8.4	31.0	19.3	3.1	4	-	-	-
B1	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	14:36	9.2	8.3	30.9	19.2	2.3	5	-	-	-
B1	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	14:36	9.4	8.3	31.2	19.3	2.3	4	-	-	-
B2	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	4.4	14:45	9.6	8.4	30.9	19.0	2.9	5	-	-	-
B2	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	4.4	14:45	9.2	8.4	31.1	19.2	3.3	4	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B2	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	14:46	9.1	8.4	31.0	19.0	2.9	5	-	-	-
B2	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	14:46	9.4	8.3	31.0	19.2	2.6	6	-	-	-
B3	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	4.4	15:03	9.2	8.4	31.3	18.9	3.2	5	-	-	-
B3	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	4.4	15:03	10.3	8.4	30.8	19.1	2.8	6	-	-	-
B3	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:04	9.0	8.3	30.8	18.9	2.8	3	-	-	-
B3	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:04	10.5	8.2	30.8	19.2	2.5	4	-	-	-
B4	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	3.5	15:11	9.6	8.3	31.3	19.0	3.0	3	-	-	-
B4	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	3.5	15:11	9.2	8.3	31.3	18.8	2.8	4	-	-	-
B4	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:12	9.5	8.6	31.0	18.8	2.5	3	-	-	-
B4	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:12	10.0	8.5	31.2	19.3	2.6	4	-	-	-
C1A	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	9.1	14:35	9.1	8.5	30.9	19.3	3.6	5	-	-	-
C1A	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	9.1	14:35	9.7	8.3	31.1	19.2	3.3	5	-	-	-
C1A	20210104	Cloudy	Moderate	Mid-Ebb	Middle	5.1	14:36	8.9	8.5	31.2	19.1	3.6	4	-	-	-
C1A	20210104	Cloudy	Moderate	Mid-Ebb	Middle	5.1	14:36	10.5	8.3	30.9	19.3	3.3	4	-	-	-
C1A	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	14:37	9.4	8.2	30.9	19.4	3.2	4	-	-	-
C1A	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	14:37	9.2	8.6	31.4	19.0	2.8	4	-	-	-
C2A	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	10.7	15:44	9.0	8.3	30.9	18.9	3.3	4	-	-	-
C2A	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	10.7	15:44	9.8	8.3	31.3	18.8	2.8	3	-	-	-
C2A	20210104	Cloudy	Moderate	Mid-Ebb	Middle	5.9	15:45	8.9	8.5	30.9	19.0	2.4	3	-	-	-
C2A	20210104	Cloudy	Moderate	Mid-Ebb	Middle	5.9	15:45	9.3	8.5	31.3	18.8	2.7	4	-	-	-
C2A	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:46	9.6	8.3	31.2	18.9	3.3	3	-	-	-
C2A	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:46	10.3	8.4	31.3	18.7	3.4	3	-	-	-
CR1	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	11.7	15:23	8.9	8.4	31.2	19.0	3.3	4	-	-	-
CR1	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	11.7	15:23	9.3	8.6	31.0	19.1	3.1	4	-	-	-
CR1	20210104	Cloudy	Moderate	Mid-Ebb	Middle	6.4	15:24	9.2	8.3	31.2	19.0	3.1	4	-	-	-
CR1	20210104	Cloudy	Moderate	Mid-Ebb	Middle	6.4	15:24	9.3	8.4	31.0	19.0	2.6	4	-	-	-
CR1	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:25	9.7	8.5	31.0	18.9	3.2	3	-	-	-
CR1	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:25	9.8	8.5	31.0	18.9	2.9	3	-	-	-
CR2	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	11.0	15:10	9.4	8.3	31.0	19.2	3.1	3	-	-	-
CR2	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	11.0	15:10	10.1	8.4	31.0	18.9	3.7	4	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
CR2	20210104	Cloudy	Moderate	Mid-Ebb	Middle	6.0	15:11	10.5	8.3	31.0	19.2	3.0	5	-	-	-
CR2	20210104	Cloudy	Moderate	Mid-Ebb	Middle	6.0	15:11	9.2	8.3	30.9	19.0	2.9	4	-	-	-
CR2	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:12	9.4	8.2	31.2	18.9	3.4	5	-	-	-
CR2	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:12	9.5	8.5	31.1	19.2	3.0	4	-	-	-
F1A	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	8.2	15:56	8.9	8.4	30.9	19.0	3.3	5	-	-	-
F1A	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	8.2	15:56	10.4	8.6	31.3	18.9	3.3	4	-	-	-
F1A	20210104	Cloudy	Moderate	Mid-Ebb	Middle	4.6	15:57	9.5	8.5	30.8	18.9	2.8	4	-	-	-
F1A	20210104	Cloudy	Moderate	Mid-Ebb	Middle	4.6	15:57	8.9	8.5	31.2	19.0	3.1	3	-	-	-
F1A	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:58	9.6	8.5	30.8	19.2	2.4	3	-	-	-
F1A	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:58	10.5	8.2	30.9	18.9	2.6	4	-	-	-
H1	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	7.2	14:56	10.4	8.5	31.2	18.9	2.9	4	-	-	-
H1	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	7.2	14:56	9.2	8.4	30.8	19.2	2.8	5	-	-	-
H1	20210104	Cloudy	Moderate	Mid-Ebb	Middle	4.1	14:57	9.5	8.5	31.3	18.9	3.5	5	-	-	-
H1	20210104	Cloudy	Moderate	Mid-Ebb	Middle	4.1	14:57	9.2	8.6	31.1	19.3	3.0	6	-	-	-
H1	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	14:58	10.5	8.4	30.9	19.3	2.5	5	-	-	-
H1	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	14:58	9.7	8.2	31.2	19.4	2.7	6	-	-	-
M1	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	8.0	15:37	10.1	8.5	31.1	18.9	3.7	4	-	-	-
M1	20210104	Cloudy	Moderate	Mid-Ebb	Bottom	8.0	15:37	9.7	8.5	31.2	19.0	3.2	5	-	-	-
M1	20210104	Cloudy	Moderate	Mid-Ebb	Middle	4.5	15:38	9.9	8.3	31.3	19.0	2.9	6	-	-	-
M1	20210104	Cloudy	Moderate	Mid-Ebb	Middle	4.5	15:38	8.8	8.3	31.0	18.9	2.6	5	-	-	-
M1	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:39	9.1	8.5	31.3	18.9	2.7	6	-	-	-
M1	20210104	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:39	9.2	8.5	30.8	18.9	2.8	6	-	-	-
B1	20210106	Cloudy	Moderate	Mid-Flood	Bottom	4.4	12:09	9.7	8.3	30.5	18.4	3.0	4	-	-	-
B1	20210106	Cloudy	Moderate	Mid-Flood	Bottom	4.4	12:09	8.6	8.4	30.9	18.6	2.6	5	-	-	-
B1	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	12:10	10.0	8.3	30.5	18.3	2.9	5	-	-	-
B1	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	12:10	8.8	8.3	31.2	18.5	2.7	6	-	-	-
B2	20210106	Cloudy	Moderate	Mid-Flood	Bottom	4.1	11:56	10.0	8.3	30.7	18.1	2.9	5	-	-	-
B2	20210106	Cloudy	Moderate	Mid-Flood	Bottom	4.1	11:56	9.4	8.3	31.3	18.3	2.6	5	-	-	-
B2	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:57	9.1	8.4	31.4	18.4	3.0	6	-	-	-
B2	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:57	8.4	8.6	30.6	18.2	3.1	6	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B3	20210106	Cloudy	Moderate	Mid-Flood	Bottom	4.1	11:39	9.4	8.6	30.6	18.1	2.9	5	-	-	-
B3	20210106	Cloudy	Moderate	Mid-Flood	Bottom	4.1	11:39	9.3	8.4	30.4	18.0	3.3	5	-	-	-
B3	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:40	8.2	8.4	31.3	18.3	2.3	5	-	-	-
B3	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:40	8.8	8.4	31.1	18.1	2.6	5	-	-	-
B4	20210106	Cloudy	Moderate	Mid-Flood	Bottom	3.8	11:31	9.2	8.6	30.7	18.0	3.0	7	-	-	-
B4	20210106	Cloudy	Moderate	Mid-Flood	Bottom	3.8	11:31	8.7	8.5	30.9	18.1	2.7	6	-	-	-
B4	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:32	10.0	8.5	30.9	18.2	2.9	5	-	-	-
B4	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:32	9.8	8.4	31.1	18.0	3.1	5	-	-	-
C1A	20210106	Cloudy	Moderate	Mid-Flood	Bottom	9.8	11:38	9.2	8.6	31.0	18.3	2.5	8	-	-	-
C1A	20210106	Cloudy	Moderate	Mid-Flood	Bottom	9.8	11:38	8.3	8.3	30.8	18.2	2.9	8	-	-	-
C1A	20210106	Cloudy	Moderate	Mid-Flood	Middle	5.4	11:39	8.6	8.3	30.7	18.2	2.8	6	-	-	-
C1A	20210106	Cloudy	Moderate	Mid-Flood	Middle	5.4	11:39	8.9	8.5	30.4	18.2	3.3	7	-	-	-
C1A	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:40	9.7	8.6	31.3	18.1	2.7	6	-	-	-
C1A	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:40	9.4	8.3	31.2	18.3	2.8	6	-	-	-
C2A	20210106	Cloudy	Moderate	Mid-Flood	Bottom	11.0	10:40	9.2	8.5	31.3	17.8	3.6	6	-	-	-
C2A	20210106	Cloudy	Moderate	Mid-Flood	Bottom	11.0	10:40	9.7	8.4	30.9	18.0	3.3	6	-	-	-
C2A	20210106	Cloudy	Moderate	Mid-Flood	Middle	6.0	10:41	10.2	8.5	31.3	18.0	2.7	8	-	-	-
C2A	20210106	Cloudy	Moderate	Mid-Flood	Middle	6.0	10:41	9.2	8.6	31.0	17.8	2.9	8	-	-	-
C2A	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:42	9.9	8.4	30.7	17.8	2.8	9	-	-	-
C2A	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:42	9.4	8.5	31.1	17.8	2.5	9	-	-	-
CR1	20210106	Cloudy	Moderate	Mid-Flood	Bottom	11.6	11:02	8.5	8.6	30.9	18.1	3.2	6	-	-	-
CR1	20210106	Cloudy	Moderate	Mid-Flood	Bottom	11.6	11:02	9.8	8.4	31.2	18.0	2.7	6	-	-	-
CR1	20210106	Cloudy	Moderate	Mid-Flood	Middle	6.3	11:03	8.3	8.3	30.6	18.1	2.9	6	-	-	-
CR1	20210106	Cloudy	Moderate	Mid-Flood	Middle	6.3	11:03	9.8	8.6	30.7	17.9	2.9	6	-	-	-
CR1	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:04	9.4	8.6	30.6	17.9	2.2	6	-	-	-
CR1	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:04	9.1	8.4	30.8	18.1	2.5	6	-	-	-
CR2	20210106	Cloudy	Moderate	Mid-Flood	Bottom	10.5	11:17	8.3	8.3	31.5	18.0	3.5	7	-	-	-
CR2	20210106	Cloudy	Moderate	Mid-Flood	Bottom	10.5	11:17	9.5	8.3	31.5	18.2	3.6	7	-	-	-
CR2	20210106	Cloudy	Moderate	Mid-Flood	Middle	5.8	11:18	9.0	8.3	30.9	18.2	3.2	6	-	-	-
CR2	20210106	Cloudy	Moderate	Mid-Flood	Middle	5.8	11:18	10.0	8.3	31.0	18.0	3.0	6	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
CR2	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:19	8.4	8.6	31.3	18.2	2.2	6	-	-	-
CR2	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:19	9.7	8.5	31.2	18.1	2.0	6	-	-	-
F1A	20210106	Cloudy	Moderate	Mid-Flood	Bottom	6.9	11:09	8.7	8.3	31.1	18.1	2.8	9	-	-	-
F1A	20210106	Cloudy	Moderate	Mid-Flood	Bottom	6.9	11:09	10.1	8.5	31.2	17.9	3.4	9	-	-	-
F1A	20210106	Cloudy	Moderate	Mid-Flood	Middle	4.0	11:10	9.2	8.6	31.1	18.0	3.1	8	-	-	-
F1A	20210106	Cloudy	Moderate	Mid-Flood	Middle	4.0	11:10	9.5	8.5	31.1	18.0	2.8	8	-	-	-
F1A	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:11	8.3	8.4	30.9	18.0	2.6	6	-	-	-
F1A	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:11	10.1	8.5	31.1	18.0	2.5	6	-	-	-
H1	20210106	Cloudy	Moderate	Mid-Flood	Bottom	7.3	12:05	9.1	8.5	30.7	18.2	2.9	6	-	-	-
H1	20210106	Cloudy	Moderate	Mid-Flood	Bottom	7.3	12:05	8.6	8.4	31.1	18.2	3.2	6	-	-	-
H1	20210106	Cloudy	Moderate	Mid-Flood	Middle	4.2	12:06	9.5	8.6	30.7	18.4	3.0	6	-	-	-
H1	20210106	Cloudy	Moderate	Mid-Flood	Middle	4.2	12:06	8.6	8.4	31.5	18.5	3.0	6	-	-	-
H1	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	12:07	8.4	8.4	30.9	18.5	2.1	6	-	-	-
H1	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	12:07	8.3	8.4	31.4	18.5	2.1	6	-	-	-
M1	20210106	Cloudy	Moderate	Mid-Flood	Bottom	7.0	10:48	8.9	8.5	31.0	17.9	3.2	7	-	-	-
M1	20210106	Cloudy	Moderate	Mid-Flood	Bottom	7.0	10:48	10.2	8.5	30.5	17.7	2.8	7	-	-	-
M1	20210106	Cloudy	Moderate	Mid-Flood	Middle	4.0	10:49	8.5	8.3	31.1	17.8	3.0	6	-	-	-
M1	20210106	Cloudy	Moderate	Mid-Flood	Middle	4.0	10:49	9.8	8.6	31.0	17.9	3.3	6	-	-	-
M1	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:50	9.5	8.3	30.9	17.7	2.4	6	-	-	-
M1	20210106	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:50	9.1	8.4	30.7	17.9	2.6	6	-	-	-
B1	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	4.2	15:59	9.3	8.5	30.9	18.1	3.5	7	-	-	-
B1	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	4.2	15:59	9.6	8.4	31.1	18.2	3.2	7	-	-	-
B1	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:00	9.5	8.3	31.1	18.3	2.2	5	-	-	-
B1	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:00	9.0	8.3	31.2	18.5	2.6	5	-	-	-
B2	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	4.7	16:16	9.6	8.5	30.9	18.2	3.4	5	-	-	-
B2	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	4.7	16:16	8.9	8.4	31.3	18.2	3.1	6	-	-	-
B2	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:17	9.2	8.5	31.2	18.4	2.3	4	-	-	-
B2	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:17	8.4	8.6	30.8	18.3	2.7	4	-	-	-
B3	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	4.0	15:38	9.9	8.3	31.0	18.7	3.2	5	-	-	-
B3	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	4.0	15:38	9.6	8.6	30.8	18.3	2.9	5	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B3	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:39	9.9	8.4	30.6	18.7	2.6	8	-	-	-
B3	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:39	9.2	8.4	30.5	18.6	2.2	9	-	-	-
B4	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	3.8	15:46	9.5	8.3	31.0	18.5	2.5	6	-	-	-
B4	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	3.8	15:46	8.7	8.4	30.6	18.6	2.8	5	-	-	-
B4	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:47	8.4	8.5	31.0	18.9	2.3	4	-	-	-
B4	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:47	9.6	8.3	30.5	18.7	2.5	5	-	-	-
C1A	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	8.6	15:30	9.7	8.3	31.1	18.6	2.7	4	-	-	-
C1A	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	8.6	15:30	8.5	8.5	30.6	18.4	3.2	5	-	-	-
C1A	20210106	Cloudy	Moderate	Mid-Ebb	Middle	4.8	15:31	8.7	8.3	30.5	18.5	2.5	4	-	-	-
C1A	20210106	Cloudy	Moderate	Mid-Ebb	Middle	4.8	15:31	9.7	8.6	30.4	18.7	2.7	4	-	-	-
C1A	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:32	9.9	8.4	30.7	18.6	1.9	4	-	-	-
C1A	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:32	9.6	8.5	30.8	18.7	1.9	4	-	-	-
C2A	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	11.0	17:26	9.7	8.4	31.2	17.9	3.3	5	-	-	-
C2A	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	11.0	17:26	9.6	8.3	30.9	18.0	2.9	5	-	-	-
C2A	20210106	Cloudy	Moderate	Mid-Ebb	Middle	6.0	17:27	9.4	8.4	30.5	18.0	2.4	4	-	-	-
C2A	20210106	Cloudy	Moderate	Mid-Ebb	Middle	6.0	17:27	9.4	8.5	31.0	17.8	2.7	4	-	-	-
C2A	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	17:28	9.5	8.5	31.3	18.0	2.8	4	-	-	-
C2A	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	17:28	8.4	8.3	31.0	17.8	2.5	4	-	-	-
CR1	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	12.2	17:05	9.3	8.3	31.3	18.0	3.2	5	-	-	-
CR1	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	12.2	17:05	9.0	8.4	30.5	18.1	3.4	5	-	-	-
CR1	20210106	Cloudy	Moderate	Mid-Ebb	Middle	6.6	17:06	9.3	8.3	30.9	18.0	2.9	4	-	-	-
CR1	20210106	Cloudy	Moderate	Mid-Ebb	Middle	6.6	17:06	9.9	8.5	30.9	17.8	2.6	4	-	-	-
CR1	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	17:07	9.7	8.6	30.5	18.2	2.7	4	-	-	-
CR1	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	17:07	8.5	8.4	30.9	18.0	2.7	4	-	-	-
CR2	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	10.7	16:51	8.4	8.6	30.8	18.0	2.8	7	-	-	-
CR2	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	10.7	16:51	9.7	8.4	30.9	18.0	2.5	6	-	-	-
CR2	20210106	Cloudy	Moderate	Mid-Ebb	Middle	5.9	16:52	9.3	8.4	30.8	18.0	3.1	6	-	-	-
CR2	20210106	Cloudy	Moderate	Mid-Ebb	Middle	5.9	16:52	9.6	8.5	31.1	18.0	2.9	6	-	-	-
CR2	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:53	8.4	8.5	30.6	17.9	2.5	6	-	-	-
CR2	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:53	9.9	8.5	30.9	17.9	2.7	6	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
F1A	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	7.0	16:35	8.7	8.3	31.1	18.1	3.0	5	-	-	-
F1A	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	7.0	16:35	8.7	8.6	30.9	18.1	3.4	5	-	-	-
F1A	20210106	Cloudy	Moderate	Mid-Ebb	Middle	4.0	16:36	8.6	8.4	31.1	18.1	2.1	5	-	-	-
F1A	20210106	Cloudy	Moderate	Mid-Ebb	Middle	4.0	16:36	9.6	8.3	30.6	18.0	2.4	5	-	-	-
F1A	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:37	9.6	8.5	30.8	18.2	2.8	5	-	-	-
F1A	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:37	8.4	8.4	30.5	18.1	2.5	5	-	-	-
H1	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	6.8	15:30	9.8	8.4	31.3	18.6	3.5	4	-	-	-
H1	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	6.8	15:30	8.6	8.5	31.3	18.7	3.2	4	-	-	-
H1	20210106	Cloudy	Moderate	Mid-Ebb	Middle	3.9	15:31	8.7	8.5	30.5	18.4	2.2	6	-	-	-
H1	20210106	Cloudy	Moderate	Mid-Ebb	Middle	3.9	15:31	9.9	8.5	30.4	18.6	2.5	6	-	-	-
H1	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:32	8.4	8.4	31.1	18.4	2.9	8	-	-	-
H1	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	15:32	9.5	8.4	31.0	18.3	2.8	8	-	-	-
M1	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	8.6	16:15	9.5	8.4	30.5	18.5	3.5	7	-	-	-
M1	20210106	Cloudy	Moderate	Mid-Ebb	Bottom	8.6	16:15	9.7	8.4	30.5	18.2	3.3	7	-	-	-
M1	20210106	Cloudy	Moderate	Mid-Ebb	Middle	4.8	16:16	9.9	8.5	30.6	18.0	2.2	6	-	-	-
M1	20210106	Cloudy	Moderate	Mid-Ebb	Middle	4.8	16:16	9.0	8.5	30.6	18.3	2.4	6	-	-	-
M1	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:17	9.1	8.5	30.6	18.1	2.4	5	-	-	-
M1	20210106	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:17	8.6	8.4	30.8	18.1	2.6	4	-	-	-
B1	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	4.2	10:24	9.9	8.5	31.2	16.3	2.9	7	-	-	-
B1	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	4.2	10:24	9.8	8.6	30.8	16.5	2.6	7	-	-	-
B1	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:25	10.0	8.6	30.8	16.5	2.5	7	-	-	-
B1	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:25	9.2	8.5	31.0	16.5	2.4	7	-	-	-
B2	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	4.5	10:07	9.0	8.5	31.4	16.4	2.6	9	-	-	-
B2	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	4.5	10:07	9.1	8.6	30.8	16.4	2.9	8	-	-	-
B2	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:08	10.3	8.3	31.5	16.5	2.7	8	-	-	-
B2	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:08	9.2	8.6	31.3	16.3	2.7	7	-	-	-
B3	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	3.7	9:49	9.3	8.4	31.4	16.2	3.7	7	-	-	-
B3	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	3.7	9:49	10.3	8.3	30.8	16.4	3.2	7	-	-	-
B3	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:50	9.9	8.5	30.9	16.4	3.0	8	-	-	-
B3	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:50	9.4	8.5	31.1	16.4	3.1	8	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B4	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	3.1	9:41	10.3	8.3	31.3	16.1	3.5	9	-	-	-
B4	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	3.1	9:41	10.4	8.6	30.9	16.1	3.2	9	-	-	-
B4	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:42	10.4	8.4	31.4	16.2	2.8	8	-	-	-
B4	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:42	9.3	8.6	31.6	16.2	2.5	8	-	-	-
C1A	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	8.8	8:22	9.9	8.4	31.0	15.7	3.1	8	-	-	-
C1A	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	8.8	8:22	9.1	8.6	30.8	15.9	3.6	8	-	-	-
C1A	20210109	Cloudy	Moderate	Mid-Ebb	Middle	4.9	8:23	9.0	8.4	31.4	15.9	3.4	8	-	-	-
C1A	20210109	Cloudy	Moderate	Mid-Ebb	Middle	4.9	8:23	9.1	8.6	31.1	16.0	3.0	8	-	-	-
C1A	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:24	9.7	8.3	30.8	16.0	3.0	7	-	-	-
C1A	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:24	9.8	8.6	31.3	15.9	3.4	7	-	-	-
C2A	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	11.2	9:38	9.0	8.3	31.3	16.2	3.0	8	-	-	-
C2A	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	11.2	9:38	9.9	8.4	30.8	16.2	3.0	8	-	-	-
C2A	20210109	Cloudy	Moderate	Mid-Ebb	Middle	6.1	9:39	10.4	8.3	30.9	16.2	3.5	9	-	-	-
C2A	20210109	Cloudy	Moderate	Mid-Ebb	Middle	6.1	9:39	10.1	8.4	31.6	16.0	3.3	9	-	-	-
C2A	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:40	9.8	8.5	31.3	16.1	3.4	10	-	-	-
C2A	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:40	9.2	8.5	30.8	16.2	3.3	10	-	-	-
CR1	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	11.5	9:17	9.8	8.3	30.7	16.1	4.0	10	-	-	-
CR1	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	11.5	9:17	9.5	8.4	31.3	16.1	4.0	10	-	-	-
CR1	20210109	Cloudy	Moderate	Mid-Ebb	Middle	6.3	9:18	9.0	8.3	31.5	16.1	3.2	8	-	-	-
CR1	20210109	Cloudy	Moderate	Mid-Ebb	Middle	6.3	9:18	9.7	8.6	30.7	16.0	3.5	8	-	-	-
CR1	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:19	9.1	8.3	31.3	16.0	3.4	8	-	-	-
CR1	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:19	10.1	8.6	31.1	16.2	3.1	8	-	-	-
CR2	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	10.8	9:03	9.4	8.6	31.4	16.1	3.7	10	-	-	-
CR2	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	10.8	9:03	9.6	8.5	31.3	16.1	4.0	10	-	-	-
CR2	20210109	Cloudy	Moderate	Mid-Ebb	Middle	5.9	9:04	10.3	8.5	31.5	16.1	3.6	9	-	-	-
CR2	20210109	Cloudy	Moderate	Mid-Ebb	Middle	5.9	9:04	9.4	8.4	31.1	16.0	3.2	9	-	-	-
CR2	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:05	10.3	8.6	30.8	16.0	3.0	9	-	-	-
CR2	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:05	9.6	8.6	30.9	16.0	3.0	8	-	-	-
F1A	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	8.0	9:20	9.4	8.5	31.4	16.2	3.2	7	-	-	-
F1A	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	8.0	9:20	10.3	8.6	31.5	16.0	3.3	6	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
F1A	20210109	Cloudy	Moderate	Mid-Ebb	Middle	4.5	9:21	10.3	8.4	31.4	16.0	3.6	7	-	-	-
F1A	20210109	Cloudy	Moderate	Mid-Ebb	Middle	4.5	9:21	9.7	8.4	31.4	16.0	3.4	8	-	-	-
F1A	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:22	10.0	8.3	31.5	16.1	2.8	9	-	-	-
F1A	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:22	9.5	8.6	31.2	16.1	2.9	9	-	-	-
H1	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	7.4	8:47	10.0	8.3	31.5	16.0	3.9	9	-	-	-
H1	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	7.4	8:47	10.2	8.4	31.1	15.9	3.8	9	-	-	-
H1	20210109	Cloudy	Moderate	Mid-Ebb	Middle	4.2	8:48	9.2	8.4	31.5	16.0	2.5	9	-	-	-
H1	20210109	Cloudy	Moderate	Mid-Ebb	Middle	4.2	8:48	9.2	8.5	31.4	16.1	2.6	9	-	-	-
H1	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:49	10.0	8.3	31.5	16.0	3.3	9	-	-	-
H1	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:49	9.1	8.3	31.1	16.0	3.1	9	-	-	-
M1	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	7.9	8:59	10.4	8.5	31.5	16.1	3.5	7	-	-	-
M1	20210109	Cloudy	Moderate	Mid-Ebb	Bottom	7.9	8:59	9.5	8.5	31.5	16.0	3.9	8	-	-	-
M1	20210109	Cloudy	Moderate	Mid-Ebb	Middle	4.5	9:00	9.9	8.5	31.4	16.0	3.5	9	-	-	-
M1	20210109	Cloudy	Moderate	Mid-Ebb	Middle	4.5	9:00	9.5	8.4	31.0	15.9	3.3	9	-	-	-
M1	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:01	9.9	8.6	30.9	16.0	2.2	9	-	-	-
M1	20210109	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:01	10.0	8.5	31.2	16.1	2.3	9	-	-	-
B1	20210109	Cloudy	Moderate	Mid-Flood	Bottom	4.3	12:59	8.9	8.4	30.5	16.7	3.1	7	-	-	-
B1	20210109	Cloudy	Moderate	Mid-Flood	Bottom	4.3	12:59	9.4	8.3	31.2	16.8	3.1	7	-	-	-
B1	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:00	10.2	8.4	30.3	16.8	4.0	9	-	-	-
B1	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:00	9.4	8.6	30.8	16.7	3.5	9	-	-	-
B2	20210109	Cloudy	Moderate	Mid-Flood	Bottom	3.4	13:12	9.2	8.4	30.5	16.8	3.4	9	-	-	-
B2	20210109	Cloudy	Moderate	Mid-Flood	Bottom	3.4	13:12	10.0	8.4	30.9	16.7	3.5	9	-	-	-
B2	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:13	9.9	8.3	30.3	16.6	2.9	11	-	-	-
B2	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:13	8.9	8.3	30.8	16.5	3.2	11	-	-	-
B3	20210109	Cloudy	Moderate	Mid-Flood	Bottom	4.3	13:31	10.0	8.3	30.7	16.8	4.0	7	-	-	-
B3	20210109	Cloudy	Moderate	Mid-Flood	Bottom	4.3	13:31	9.0	8.4	30.8	16.7	3.7	7	-	-	-
B3	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:32	9.8	8.4	30.2	16.8	4.5	9	-	-	-
B3	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:32	9.9	8.4	30.5	16.8	4.5	9	-	-	-
B4	20210109	Cloudy	Moderate	Mid-Flood	Bottom	4.1	13:39	9.5	8.4	31.0	16.6	3.7	8	-	-	-
B4	20210109	Cloudy	Moderate	Mid-Flood	Bottom	4.1	13:39	9.8	8.4	30.9	16.8	4.0	8	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B4	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:40	9.8	8.5	30.6	16.6	3.9	5	-	-	-
B4	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:40	9.4	8.3	31.3	16.8	3.6	5	-	-	-
C1A	20210109	Cloudy	Moderate	Mid-Flood	Bottom	11.0	13:49	10.1	8.4	30.4	16.9	4.2	9	-	-	-
C1A	20210109	Cloudy	Moderate	Mid-Flood	Bottom	11.0	13:49	9.0	8.5	31.2	16.7	4.5	9	-	-	-
C1A	20210109	Cloudy	Moderate	Mid-Flood	Middle	6.0	13:50	9.1	8.6	31.2	16.7	4.1	8	-	-	-
C1A	20210109	Cloudy	Moderate	Mid-Flood	Middle	6.0	13:50	9.6	8.6	31.1	16.8	3.7	7	-	-	-
C1A	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:51	10.0	8.5	30.8	16.7	3.5	7	-	-	-
C1A	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:51	9.8	8.3	31.2	16.7	3.5	7	-	-	-
C2A	20210109	Cloudy	Moderate	Mid-Flood	Bottom	10.5	12:55	10.3	8.5	31.2	16.8	3.4	9	-	-	-
C2A	20210109	Cloudy	Moderate	Mid-Flood	Bottom	10.5	12:55	9.6	8.5	30.9	16.7	3.4	10	-	-	-
C2A	20210109	Cloudy	Moderate	Mid-Flood	Middle	5.8	12:56	10.0	8.4	30.8	16.9	2.6	10	-	-	-
C2A	20210109	Cloudy	Moderate	Mid-Flood	Middle	5.8	12:56	9.3	8.5	30.8	16.9	2.6	9	-	-	-
C2A	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	12:57	9.1	8.4	30.2	16.8	2.9	10	-	-	-
C2A	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	12:57	9.5	8.4	30.3	16.7	3.2	9	-	-	-
CR1	20210109	Cloudy	Moderate	Mid-Flood	Bottom	11.6	13:15	10.3	8.5	31.2	16.6	3.1	8	-	-	-
CR1	20210109	Cloudy	Moderate	Mid-Flood	Bottom	11.6	13:15	9.3	8.4	31.0	16.6	2.8	8	-	-	-
CR1	20210109	Cloudy	Moderate	Mid-Flood	Middle	6.3	13:16	9.3	8.6	30.9	16.6	3.5	10	-	-	-
CR1	20210109	Cloudy	Moderate	Mid-Flood	Middle	6.3	13:16	9.5	8.4	30.9	16.7	3.2	10	-	-	-
CR1	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:17	9.9	8.4	30.9	16.6	3.9	10	-	-	-
CR1	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:17	9.1	8.4	30.7	16.8	3.3	9	-	-	-
CR2	20210109	Cloudy	Moderate	Mid-Flood	Bottom	10.2	13:29	9.7	8.5	31.1	16.7	3.5	11	-	-	-
CR2	20210109	Cloudy	Moderate	Mid-Flood	Bottom	10.2	13:29	9.9	8.4	30.7	16.9	3.8	11	-	-	-
CR2	20210109	Cloudy	Moderate	Mid-Flood	Middle	5.6	13:30	9.9	8.5	30.3	16.7	3.5	9	-	-	-
CR2	20210109	Cloudy	Moderate	Mid-Flood	Middle	5.6	13:30	9.7	8.3	31.1	16.6	3.5	10	-	-	-
CR2	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:31	10.1	8.5	30.4	16.7	2.9	8	-	-	-
CR2	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:31	8.9	8.5	31.2	16.6	2.8	8	-	-	-
F1A	20210109	Cloudy	Moderate	Mid-Flood	Bottom	7.6	14:28	9.8	8.4	31.0	16.6	3.5	8	-	-	-
F1A	20210109	Cloudy	Moderate	Mid-Flood	Bottom	7.6	14:28	9.7	8.5	31.1	16.6	3.3	8	-	-	-
F1A	20210109	Cloudy	Moderate	Mid-Flood	Middle	4.3	14:29	9.6	8.3	30.6	16.7	2.8	9	-	-	-
F1A	20210109	Cloudy	Moderate	Mid-Flood	Middle	4.3	14:29	9.0	8.3	30.5	16.7	2.6	9	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
F1A	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:30	10.2	8.4	30.3	16.7	3.2	9	-	-	-
F1A	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:30	9.7	8.4	30.5	16.7	2.7	9	-	-	-
H1	20210109	Cloudy	Moderate	Mid-Flood	Bottom	6.8	14:11	9.0	8.6	31.1	16.6	4.3	9	-	-	-
H1	20210109	Cloudy	Moderate	Mid-Flood	Bottom	6.8	14:11	8.9	8.4	30.3	16.6	4.1	9	-	-	-
H1	20210109	Cloudy	Moderate	Mid-Flood	Middle	3.9	14:12	9.1	8.5	30.5	16.6	2.9	9	-	-	-
H1	20210109	Cloudy	Moderate	Mid-Flood	Middle	3.9	14:12	9.3	8.5	31.0	16.5	3.0	9	-	-	-
H1	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:13	9.1	8.4	30.9	16.7	2.6	11	-	-	-
H1	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:13	10.2	8.3	31.2	16.7	2.9	11	-	-	-
M1	20210109	Cloudy	Moderate	Mid-Flood	Bottom	7.4	14:08	9.7	8.5	30.5	16.5	3.5	10	-	-	-
M1	20210109	Cloudy	Moderate	Mid-Flood	Bottom	7.4	14:08	9.1	8.6	31.3	16.6	3.6	10	-	-	-
M1	20210109	Cloudy	Moderate	Mid-Flood	Middle	4.2	14:09	9.3	8.5	30.3	16.7	3.9	10	-	-	-
M1	20210109	Cloudy	Moderate	Mid-Flood	Middle	4.2	14:09	10.0	8.3	30.6	16.5	3.8	10	-	-	-
M1	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:10	9.0	8.3	30.9	16.6	3.2	10	-	-	-
M1	20210109	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:10	10.1	8.6	30.8	16.6	3.2	10	-	-	-
B1	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	3.5	12:11	9.9	8.4	30.5	15.7	3.1	13	-	-	-
B1	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	3.5	12:11	9.5	8.4	30.3	15.7	3.5	13	-	-	-
B1	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	12:12	9.9	8.5	30.4	15.5	2.3	12	-	-	-
B1	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	12:12	9.9	8.5	30.6	15.5	2.4	12	-	-	-
B2	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	4.9	12:26	9.7	8.5	31.1	15.4	3.3	14	-	-	-
B2	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	4.9	12:26	8.8	8.3	30.8	15.7	3.1	14	-	-	-
B2	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	12:27	8.9	8.3	30.6	15.8	2.5	12	-	-	-
B2	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	12:27	9.1	8.4	31.0	15.4	2.8	12	-	-	-
B3	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	3.6	11:30	9.2	8.5	30.8	15.4	3.8	14	-	-	-
B3	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	3.6	11:30	8.8	8.3	30.6	15.4	3.8	15	-	-	-
B3	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:31	10.2	8.2	30.6	15.8	2.7	12	-	-	-
B3	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:31	9.7	8.3	30.6	15.6	2.8	11	-	-	-
B4	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	3.7	11:42	9.4	8.3	30.4	15.7	2.8	12	-	-	-
B4	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	3.7	11:42	9.0	8.4	30.4	15.8	3.3	12	-	-	-
B4	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:43	9.1	8.3	31.0	15.8	2.9	14	-	-	-
B4	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:43	9.6	8.4	30.7	15.3	2.5	14	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
C1A	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	9.7	9:28	10.1	8.3	30.7	15.3	2.7	14	-	-	-
C1A	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	9.7	9:28	8.8	8.3	30.7	15.4	3.2	14	-	-	-
C1A	20210111	Cloudy	Moderate	Mid-Ebb	Middle	5.4	9:29	10.4	8.4	31.1	15.4	2.8	14	-	-	-
C1A	20210111	Cloudy	Moderate	Mid-Ebb	Middle	5.4	9:29	9.7	8.3	31.2	15.2	3.0	14	-	-	-
C1A	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:30	9.1	8.5	30.3	15.2	2.9	13	-	-	-
C1A	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:30	8.8	8.3	30.3	15.2	2.5	14	-	-	-
C2A	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	11.3	10:42	9.0	8.4	30.4	15.4	3.9	12	-	-	-
C2A	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	11.3	10:42	10.3	8.3	30.5	15.5	3.5	12	-	-	-
C2A	20210111	Cloudy	Moderate	Mid-Ebb	Middle	6.2	10:43	9.0	8.4	30.4	15.6	3.1	13	-	-	-
C2A	20210111	Cloudy	Moderate	Mid-Ebb	Middle	6.2	10:43	10.0	8.5	30.5	15.7	3.3	13	-	-	-
C2A	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:44	10.1	8.2	30.3	15.5	2.9	13	-	-	-
C2A	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:44	10.1	8.3	30.6	15.3	3.3	13	-	-	-
CR1	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	12.7	10:19	10.3	8.3	30.7	15.4	3.2	13	-	-	-
CR1	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	12.7	10:19	10.1	8.3	30.3	15.4	3.5	13	-	-	-
CR1	20210111	Cloudy	Moderate	Mid-Ebb	Middle	6.9	10:20	10.1	8.3	30.3	15.1	2.9	13	-	-	-
CR1	20210111	Cloudy	Moderate	Mid-Ebb	Middle	6.9	10:20	8.9	8.5	30.8	15.1	3.4	13	-	-	-
CR1	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:21	9.1	8.4	30.3	15.3	3.0	14	-	-	-
CR1	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:21	9.2	8.4	30.6	15.3	2.6	14	-	-	-
CR2	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	11.2	10:05	8.9	8.3	30.5	15.3	3.2	13	-	-	-
CR2	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	11.2	10:05	8.9	8.4	30.7	15.4	3.7	13	-	-	-
CR2	20210111	Cloudy	Moderate	Mid-Ebb	Middle	6.1	10:06	9.1	8.3	30.6	15.3	3.3	14	-	-	-
CR2	20210111	Cloudy	Moderate	Mid-Ebb	Middle	6.1	10:06	10.0	8.3	31.2	15.2	3.2	14	-	-	-
CR2	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:07	9.9	8.3	31.2	15.5	3.0	16	-	-	-
CR2	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:07	10.1	8.3	31.1	15.3	3.0	16	-	-	-
F1A	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	7.2	11:07	9.1	8.4	31.1	15.3	3.5	15	-	-	-
F1A	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	7.2	11:07	9.4	8.3	30.9	15.8	3.2	15	-	-	-
F1A	20210111	Cloudy	Moderate	Mid-Ebb	Middle	4.1	11:08	10.2	8.2	30.5	15.5	2.8	14	-	-	-
F1A	20210111	Cloudy	Moderate	Mid-Ebb	Middle	4.1	11:08	9.5	8.4	30.3	15.7	3.1	14	-	-	-
F1A	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:09	9.5	8.5	31.1	15.3	2.9	14	-	-	-
F1A	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:09	10.0	8.4	31.2	15.3	2.6	14	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
H1	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	7.0	9:50	8.9	8.5	30.3	15.5	3.5	17	-	-	-
H1	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	7.0	9:50	9.2	8.5	30.9	15.3	3.0	17	-	-	-
H1	20210111	Cloudy	Moderate	Mid-Ebb	Middle	4.0	9:51	10.1	8.4	30.9	15.5	2.8	17	-	-	-
H1	20210111	Cloudy	Moderate	Mid-Ebb	Middle	4.0	9:51	9.2	8.4	31.2	15.3	2.8	17	-	-	-
H1	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:52	9.7	8.4	30.7	15.4	3.2	16	-	-	-
H1	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:52	8.9	8.5	30.9	15.3	2.8	15	-	-	-
M1	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	8.8	11:33	9.9	8.3	30.9	15.5	2.9	16	-	-	-
M1	20210111	Cloudy	Moderate	Mid-Ebb	Bottom	8.8	11:33	10.4	8.5	30.3	15.3	3.2	16	-	-	-
M1	20210111	Cloudy	Moderate	Mid-Ebb	Middle	4.9	11:34	10.1	8.5	31.0	15.5	2.6	14	-	-	-
M1	20210111	Cloudy	Moderate	Mid-Ebb	Middle	4.9	11:34	10.0	8.3	30.6	15.6	2.4	14	-	-	-
M1	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:35	10.3	8.4	30.5	15.7	2.9	12	-	-	-
M1	20210111	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:35	10.2	8.5	30.8	15.8	3.2	12	-	-	-
B1	20210111	Cloudy	Moderate	Mid-Flood	Bottom	3.9	14:31	8.8	8.4	30.7	15.9	2.9	14	-	-	-
B1	20210111	Cloudy	Moderate	Mid-Flood	Bottom	3.9	14:31	9.8	8.2	30.7	16.0	3.4	14	-	-	-
B1	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:32	9.2	8.4	30.7	16.0	2.9	16	-	-	-
B1	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:32	9.4	8.4	30.5	16.0	3.3	16	-	-	-
B2	20210111	Cloudy	Moderate	Mid-Flood	Bottom	4.2	14:43	9.9	8.4	30.4	15.9	3.0	13	-	-	-
B2	20210111	Cloudy	Moderate	Mid-Flood	Bottom	4.2	14:43	9.2	8.3	30.3	16.1	3.6	13	-	-	-
B2	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:44	10.1	8.5	31.1	16.1	2.8	13	-	-	-
B2	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:44	10.0	8.5	31.1	16.2	3.0	14	-	-	-
B3	20210111	Cloudy	Moderate	Mid-Flood	Bottom	4.0	15:00	9.8	8.3	31.1	16.0	3.2	11	-	-	-
B3	20210111	Cloudy	Moderate	Mid-Flood	Bottom	4.0	15:00	8.9	8.4	30.5	16.1	3.7	11	-	-	-
B3	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:01	9.7	8.4	31.3	16.1	2.8	15	-	-	-
B3	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:01	9.9	8.5	30.9	16.0	3.2	15	-	-	-
B4	20210111	Cloudy	Moderate	Mid-Flood	Bottom	4.0	15:10	10.1	8.3	30.6	15.9	2.7	16	-	-	-
B4	20210111	Cloudy	Moderate	Mid-Flood	Bottom	4.0	15:10	8.9	8.6	30.5	15.9	2.7	16	-	-	-
B4	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:11	9.5	8.5	30.2	16.0	2.3	14	-	-	-
B4	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:11	9.0	8.5	31.0	15.9	2.4	14	-	-	-
C1A	20210111	Cloudy	Moderate	Mid-Flood	Bottom	11.0	15:22	9.8	8.4	30.7	16.1	3.0	13	-	-	-
C1A	20210111	Cloudy	Moderate	Mid-Flood	Bottom	11.0	15:22	9.3	8.4	30.6	16.1	2.8	13	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
C1A	20210111	Cloudy	Moderate	Mid-Flood	Middle	6.0	15:23	8.9	8.3	30.1	16.1	3.1	14	-	-	-
C1A	20210111	Cloudy	Moderate	Mid-Flood	Middle	6.0	15:23	9.4	8.4	30.9	16.1	3.4	14	-	-	-
C1A	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:24	10.2	8.3	30.7	15.9	2.4	15	-	-	-
C1A	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:24	9.4	8.3	30.7	16.2	2.6	15	-	-	-
C2A	20210111	Cloudy	Moderate	Mid-Flood	Bottom	10.8	14:31	9.8	8.3	30.4	16.1	3.0	15	-	-	-
C2A	20210111	Cloudy	Moderate	Mid-Flood	Bottom	10.8	14:31	8.8	8.4	30.1	16.2	3.2	15	-	-	-
C2A	20210111	Cloudy	Moderate	Mid-Flood	Middle	5.9	14:32	8.9	8.4	31.0	16.1	2.7	13	-	-	-
C2A	20210111	Cloudy	Moderate	Mid-Flood	Middle	5.9	14:32	9.6	8.5	31.0	16.1	2.4	14	-	-	-
C2A	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:33	9.2	8.4	31.0	16.0	2.3	12	-	-	-
C2A	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:33	9.3	8.6	31.3	16.0	2.8	12	-	-	-
CR1	20210111	Cloudy	Moderate	Mid-Flood	Bottom	11.4	14:50	10.0	8.4	30.6	16.1	3.6	13	-	-	-
CR1	20210111	Cloudy	Moderate	Mid-Flood	Bottom	11.4	14:50	9.9	8.4	30.6	16.2	3.5	13	-	-	-
CR1	20210111	Cloudy	Moderate	Mid-Flood	Middle	6.2	14:51	8.9	8.4	30.9	16.1	2.9	13	-	-	-
CR1	20210111	Cloudy	Moderate	Mid-Flood	Middle	6.2	14:51	9.7	8.4	30.8	16.0	3.4	13	-	-	-
CR1	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:52	9.7	8.5	31.3	16.1	3.2	15	-	-	-
CR1	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:52	10.2	8.5	31.0	16.1	3.3	15	-	-	-
CR2	20210111	Cloudy	Moderate	Mid-Flood	Bottom	10.2	15:02	9.8	8.5	31.0	16.2	3.1	18	-	-	-
CR2	20210111	Cloudy	Moderate	Mid-Flood	Bottom	10.2	15:02	10.2	8.3	31.0	15.9	3.1	18	-	-	-
CR2	20210111	Cloudy	Moderate	Mid-Flood	Middle	5.6	15:03	9.8	8.5	30.6	15.9	2.5	16	-	-	-
CR2	20210111	Cloudy	Moderate	Mid-Flood	Middle	5.6	15:03	8.8	8.3	30.8	16.0	2.7	16	-	-	-
CR2	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:04	9.1	8.6	31.3	16.2	3.0	14	-	-	-
CR2	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:04	9.0	8.4	31.2	16.2	3.0	13	-	-	-
F1A	20210111	Cloudy	Moderate	Mid-Flood	Bottom	7.6	15:55	9.7	8.5	31.1	16.1	3.4	14	-	-	-
F1A	20210111	Cloudy	Moderate	Mid-Flood	Bottom	7.6	15:55	9.8	8.5	31.1	15.9	3.7	14	-	-	-
F1A	20210111	Cloudy	Moderate	Mid-Flood	Middle	4.3	15:56	9.3	8.2	30.9	16.1	2.2	15	-	-	-
F1A	20210111	Cloudy	Moderate	Mid-Flood	Middle	4.3	15:56	9.1	8.4	31.2	16.1	2.4	13	-	-	-
F1A	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:57	10.0	8.5	30.3	15.9	2.3	16	-	-	-
F1A	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:57	9.8	8.4	31.0	16.1	2.7	16	-	-	-
H1	20210111	Cloudy	Moderate	Mid-Flood	Bottom	6.5	15:44	9.6	8.3	31.3	15.9	3.5	15	-	-	-
H1	20210111	Cloudy	Moderate	Mid-Flood	Bottom	6.5	15:44	9.1	8.4	30.5	16.1	3.0	15	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
H1	20210111	Cloudy	Moderate	Mid-Flood	Middle	3.8	15:45	8.8	8.4	31.1	16.2	2.9	15	-	-	-
H1	20210111	Cloudy	Moderate	Mid-Flood	Middle	3.8	15:45	8.7	8.3	30.4	16.1	2.7	14	-	-	-
H1	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:46	9.3	8.4	30.7	16.0	2.5	14	-	-	-
H1	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:46	8.7	8.4	30.5	16.0	2.4	14	-	-	-
M1	20210111	Cloudy	Moderate	Mid-Flood	Bottom	7.6	15:36	9.5	8.4	31.0	16.0	3.8	14	-	-	-
M1	20210111	Cloudy	Moderate	Mid-Flood	Bottom	7.6	15:36	9.2	8.4	31.1	16.2	3.5	14	-	-	-
M1	20210111	Cloudy	Moderate	Mid-Flood	Middle	4.3	15:37	8.9	8.4	30.2	16.2	3.0	15	-	-	-
M1	20210111	Cloudy	Moderate	Mid-Flood	Middle	4.3	15:37	9.9	8.3	30.5	16.0	3.4	15	-	-	-
M1	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:38	9.5	8.4	30.9	16.1	2.5	17	-	-	-
M1	20210111	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:38	9.4	8.6	30.6	15.9	2.2	17	-	-	-
B1	20210113	Sunny	Moderate	Mid-Ebb	Bottom	3.5	12:54	10.1	8.3	30.6	17.4	2.6	6	-	-	-
B1	20210113	Sunny	Moderate	Mid-Ebb	Bottom	3.5	12:54	10.1	8.2	31.0	17.6	3.0	6	-	-	-
B1	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:55	10.2	8.3	30.8	17.6	2.3	6	-	-	-
B1	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:55	10.4	8.5	30.9	17.4	2.2	8	-	-	-
B2	20210113	Sunny	Moderate	Mid-Ebb	Bottom	4.7	13:07	10.7	8.5	30.9	17.6	3.5	8	-	-	-
B2	20210113	Sunny	Moderate	Mid-Ebb	Bottom	4.7	13:07	10.2	8.5	30.7	17.6	3.3	8	-	-	-
B2	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:08	10.5	8.4	31.3	17.6	2.6	8	-	-	-
B2	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:08	10.1	8.2	30.9	17.6	2.6	8	-	-	-
B3	20210113	Sunny	Moderate	Mid-Ebb	Bottom	3.6	12:27	10.6	8.4	30.5	17.1	2.7	9	-	-	-
B3	20210113	Sunny	Moderate	Mid-Ebb	Bottom	3.6	12:27	9.9	8.3	31.2	17.2	2.6	7	-	-	-
B3	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:28	10.6	8.4	30.6	17.1	3.1	8	-	-	-
B3	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:28	10.4	8.4	30.7	17.3	2.8	6	-	-	-
B4	20210113	Sunny	Moderate	Mid-Ebb	Bottom	3.9	12:17	10.1	8.4	31.4	17.1	2.9	6	-	-	-
B4	20210113	Sunny	Moderate	Mid-Ebb	Bottom	3.9	12:17	10.8	8.3	30.6	17.4	2.6	7	-	-	-
B4	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:18	10.8	8.4	31.0	17.1	2.6	7	-	-	-
B4	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:18	10.4	8.5	30.5	17.1	3.0	8	-	-	-
C1A	20210113	Sunny	Moderate	Mid-Ebb	Bottom	9.1	11:03	9.9	8.5	31.0	17.0	2.8	7	-	-	-
C1A	20210113	Sunny	Moderate	Mid-Ebb	Bottom	9.1	11:03	10.2	8.3	31.3	17.3	2.9	7	-	-	-
C1A	20210113	Sunny	Moderate	Mid-Ebb	Middle	5.1	11:04	10.1	8.2	30.5	17.2	3.0	7	-	-	-
C1A	20210113	Sunny	Moderate	Mid-Ebb	Middle	5.1	11:04	9.9	8.2	31.0	17.1	3.2	8	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
C1A	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:05	9.8	8.3	30.8	17.1	3.0	5	-	-	-
C1A	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:05	10.4	8.4	30.8	17.1	2.8	4	-	-	-
C2A	20210113	Sunny	Moderate	Mid-Ebb	Bottom	10.4	12:14	10.3	8.4	30.9	17.1	2.9	4	-	-	-
C2A	20210113	Sunny	Moderate	Mid-Ebb	Bottom	10.4	12:14	9.9	8.3	31.1	17.3	2.8	6	-	-	-
C2A	20210113	Sunny	Moderate	Mid-Ebb	Middle	5.7	12:15	10.2	8.4	30.6	17.2	3.2	5	-	-	-
C2A	20210113	Sunny	Moderate	Mid-Ebb	Middle	5.7	12:15	10.6	8.5	31.4	17.1	3.5	6	-	-	-
C2A	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:16	10.4	8.5	31.4	17.3	2.7	7	-	-	-
C2A	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:16	10.6	8.3	30.8	17.2	2.7	7	-	-	-
CR1	20210113	Sunny	Moderate	Mid-Ebb	Bottom	12.2	11:53	10.4	8.2	30.7	17.4	2.7	6	-	-	-
CR1	20210113	Sunny	Moderate	Mid-Ebb	Bottom	12.2	11:53	10.4	8.5	30.9	17.2	2.6	6	-	-	-
CR1	20210113	Sunny	Moderate	Mid-Ebb	Middle	6.6	11:54	10.1	8.4	30.7	17.4	2.7	6	-	-	-
CR1	20210113	Sunny	Moderate	Mid-Ebb	Middle	6.6	11:54	10.5	8.2	30.5	17.4	2.5	7	-	-	-
CR1	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:55	10.4	8.2	31.0	17.1	2.4	7	-	-	-
CR1	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:55	10.8	8.2	31.2	17.2	2.6	6	-	-	-
CR2	20210113	Sunny	Moderate	Mid-Ebb	Bottom	9.9	11:39	10.0	8.4	30.9	17.2	2.8	5	-	-	-
CR2	20210113	Sunny	Moderate	Mid-Ebb	Bottom	9.9	11:39	10.8	8.2	30.7	17.1	3.2	6	-	-	-
CR2	20210113	Sunny	Moderate	Mid-Ebb	Middle	5.5	11:40	10.2	8.5	31.1	17.1	2.6	6	-	-	-
CR2	20210113	Sunny	Moderate	Mid-Ebb	Middle	5.5	11:40	10.2	8.2	30.5	17.3	2.7	5	-	-	-
CR2	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:41	9.8	8.3	30.5	17.2	2.9	6	-	-	-
CR2	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:41	10.4	8.5	31.4	17.3	2.6	6	-	-	-
F1A	20210113	Sunny	Moderate	Mid-Ebb	Bottom	8.1	11:55	9.9	8.2	31.2	17.3	2.8	4	-	-	-
F1A	20210113	Sunny	Moderate	Mid-Ebb	Bottom	8.1	11:55	10.4	8.5	31.3	17.2	2.4	4	-	-	-
F1A	20210113	Sunny	Moderate	Mid-Ebb	Middle	4.6	11:56	10.5	8.2	31.0	17.1	2.7	6	-	-	-
F1A	20210113	Sunny	Moderate	Mid-Ebb	Middle	4.6	11:56	10.6	8.4	30.8	17.4	2.5	6	-	-	-
F1A	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:57	10.5	8.3	31.4	17.4	2.6	5	-	-	-
F1A	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:57	10.8	8.4	31.1	17.1	2.4	4	-	-	-
H1	20210113	Sunny	Moderate	Mid-Ebb	Bottom	7.2	11:24	10.8	8.3	30.6	17.1	3.0	6	-	-	-
H1	20210113	Sunny	Moderate	Mid-Ebb	Bottom	7.2	11:24	10.5	8.2	30.7	17.2	2.6	6	-	-	-
H1	20210113	Sunny	Moderate	Mid-Ebb	Middle	4.1	11:25	9.9	8.2	30.6	17.2	2.9	6	-	-	-
H1	20210113	Sunny	Moderate	Mid-Ebb	Middle	4.1	11:25	10.4	8.4	31.0	17.1	3.1	6	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
H1	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:26	10.7	8.2	31.1	17.0	2.9	5	-	-	-
H1	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:26	10.2	8.5	30.7	17.0	3.1	5	-	-	-
M1	20210113	Sunny	Moderate	Mid-Ebb	Bottom	8.1	11:33	9.9	8.2	30.9	17.4	3.4	5	-	-	-
M1	20210113	Sunny	Moderate	Mid-Ebb	Bottom	8.1	11:33	10.7	8.5	31.2	17.0	3.2	6	-	-	-
M1	20210113	Sunny	Moderate	Mid-Ebb	Middle	4.6	11:34	10.7	8.3	30.7	17.0	2.3	6	-	-	-
M1	20210113	Sunny	Moderate	Mid-Ebb	Middle	4.6	11:34	10.7	8.3	31.0	17.1	2.7	6	-	-	-
M1	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:35	10.8	8.2	30.5	17.3	2.8	8	-	-	-
M1	20210113	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:35	9.8	8.5	31.2	17.2	2.4	9	-	-	-
B1	20210113	Sunny	Moderate	Mid-Flood	Bottom	3.6	15:32	10.6	8.4	31.0	17.2	3.3	8	-	-	-
B1	20210113	Sunny	Moderate	Mid-Flood	Bottom	3.6	15:32	10.1	8.6	30.7	17.2	3.3	8	-	-	-
B1	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	15:33	9.8	8.4	31.3	17.3	3.2	6	-	-	-
B1	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	15:33	10.6	8.2	30.6	17.2	2.7	5	-	-	-
B2	20210113	Sunny	Moderate	Mid-Flood	Bottom	4.0	15:44	10.1	8.5	31.0	17.1	3.7	5	-	-	-
B2	20210113	Sunny	Moderate	Mid-Flood	Bottom	4.0	15:44	10.5	8.4	31.3	17.0	3.4	4	-	-	-
B2	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	15:45	10.0	8.4	31.2	17.4	3.2	7	-	-	-
B2	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	15:45	9.8	8.5	30.5	17.1	3.3	7	-	-	-
B3	20210113	Sunny	Moderate	Mid-Flood	Bottom	3.7	16:02	9.8	8.4	30.8	16.9	3.7	6	-	-	-
B3	20210113	Sunny	Moderate	Mid-Flood	Bottom	3.7	16:02	10.4	8.4	31.0	17.3	3.4	5	-	-	-
B3	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	16:03	10.7	8.5	30.6	17.3	3.0	7	-	-	-
B3	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	16:03	10.3	8.2	31.1	17.2	3.3	8	-	-	-
B4	20210113	Sunny	Moderate	Mid-Flood	Bottom	4.4	16:09	10.1	8.4	30.9	17.0	3.0	6	-	-	-
B4	20210113	Sunny	Moderate	Mid-Flood	Bottom	4.4	16:09	9.9	8.3	30.8	17.2	3.4	7	-	-	-
B4	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	16:10	10.7	8.2	31.3	17.3	3.0	5	-	-	-
B4	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	16:10	9.7	8.3	31.3	17.1	2.7	6	-	-	-
C1A	20210113	Sunny	Moderate	Mid-Flood	Bottom	9.5	16:25	10.3	8.4	30.9	16.9	3.2	6	-	-	-
C1A	20210113	Sunny	Moderate	Mid-Flood	Bottom	9.5	16:25	9.8	8.5	31.1	16.9	2.8	6	-	-	-
C1A	20210113	Sunny	Moderate	Mid-Flood	Middle	5.3	16:26	9.8	8.4	30.9	16.9	3.1	4	-	-	-
C1A	20210113	Sunny	Moderate	Mid-Flood	Middle	5.3	16:26	9.9	8.3	30.7	17.0	3.4	4	-	-	-
C1A	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	16:27	10.2	8.3	30.6	17.0	2.9	6	-	-	-
C1A	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	16:27	9.6	8.5	30.6	17.1	3.2	5	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
C2A	20210113	Sunny	Moderate	Mid-Flood	Bottom	10.9	15:30	9.9	8.5	31.3	17.4	3.6	7	-	-	-
C2A	20210113	Sunny	Moderate	Mid-Flood	Bottom	10.9	15:30	10.2	8.2	31.3	17.4	3.2	8	-	-	-
C2A	20210113	Sunny	Moderate	Mid-Flood	Middle	6.0	15:31	10.5	8.5	31.1	17.1	3.5	8	-	-	-
C2A	20210113	Sunny	Moderate	Mid-Flood	Middle	6.0	15:31	9.8	8.5	30.9	17.1	3.5	8	-	-	-
C2A	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	15:32	10.3	8.2	30.7	17.3	2.5	7	-	-	-
C2A	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	15:32	10.6	8.3	30.7	17.4	2.4	6	-	-	-
CR1	20210113	Sunny	Moderate	Mid-Flood	Bottom	11.4	15:51	10.0	8.3	31.3	17.2	3.5	7	-	-	-
CR1	20210113	Sunny	Moderate	Mid-Flood	Bottom	11.4	15:51	10.1	8.4	31.0	17.0	3.6	9	-	-	-
CR1	20210113	Sunny	Moderate	Mid-Flood	Middle	6.2	15:52	10.0	8.4	31.1	16.9	2.7	8	-	-	-
CR1	20210113	Sunny	Moderate	Mid-Flood	Middle	6.2	15:52	9.7	8.4	31.2	17.3	3.2	7	-	-	-
CR1	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	15:53	10.1	8.3	30.9	17.2	3.2	8	-	-	-
CR1	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	15:53	10.1	8.4	31.3	17.3	3.3	8	-	-	-
CR2	20210113	Sunny	Moderate	Mid-Flood	Bottom	10.8	16:05	9.8	8.5	31.0	16.9	3.7	7	-	-	-
CR2	20210113	Sunny	Moderate	Mid-Flood	Bottom	10.8	16:05	10.1	8.3	31.1	17.3	3.3	7	-	-	-
CR2	20210113	Sunny	Moderate	Mid-Flood	Middle	5.9	16:06	10.4	8.5	31.1	17.1	2.8	10	-	-	-
CR2	20210113	Sunny	Moderate	Mid-Flood	Middle	5.9	16:06	9.8	8.5	31.3	16.9	3.0	9	-	-	-
CR2	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	16:07	9.7	8.3	31.1	17.3	2.6	5	-	-	-
CR2	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	16:07	10.3	8.6	30.8	16.9	3.0	4	-	-	-
F1A	20210113	Sunny	Moderate	Mid-Flood	Bottom	7.0	16:53	9.7	8.5	30.6	16.8	2.8	4	-	-	-
F1A	20210113	Sunny	Moderate	Mid-Flood	Bottom	7.0	16:53	10.7	8.3	30.8	16.8	2.9	4	-	-	-
F1A	20210113	Sunny	Moderate	Mid-Flood	Middle	4.0	16:54	10.6	8.5	30.7	16.9	3.3	4	-	-	-
F1A	20210113	Sunny	Moderate	Mid-Flood	Middle	4.0	16:54	10.7	8.4	31.1	17.1	3.5	5	-	-	-
F1A	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	16:55	10.1	8.6	31.0	16.8	3.1	5	-	-	-
F1A	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	16:55	9.9	8.3	30.9	16.9	2.8	5	-	-	-
H1	20210113	Sunny	Moderate	Mid-Flood	Bottom	6.8	16:47	9.9	8.4	31.0	16.8	2.9	6	-	-	-
H1	20210113	Sunny	Moderate	Mid-Flood	Bottom	6.8	16:47	10.2	8.5	31.0	16.9	2.7	5	-	-	-
H1	20210113	Sunny	Moderate	Mid-Flood	Middle	3.9	16:48	9.8	8.4	31.2	17.1	3.1	5	-	-	-
H1	20210113	Sunny	Moderate	Mid-Flood	Middle	3.9	16:48	10.6	8.2	30.8	17.1	3.2	6	-	-	-
H1	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	16:49	9.7	8.4	31.2	17.2	3.1	7	-	-	-
H1	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	16:49	10.2	8.4	31.2	16.9	3.1	7	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
M1	20210113	Sunny	Moderate	Mid-Flood	Bottom	7.0	16:34	10.3	8.3	30.7	16.8	3.4	8	-	-	-
M1	20210113	Sunny	Moderate	Mid-Flood	Bottom	7.0	16:34	9.8	8.3	31.1	16.9	3.7	7	-	-	-
M1	20210113	Sunny	Moderate	Mid-Flood	Middle	4.0	16:35	10.3	8.4	30.5	16.9	3.0	8	-	-	-
M1	20210113	Sunny	Moderate	Mid-Flood	Middle	4.0	16:35	9.9	8.4	31.1	17.0	3.4	7	-	-	-
M1	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	16:36	10.6	8.5	31.0	17.0	2.3	4	-	-	-
M1	20210113	Sunny	Moderate	Mid-Flood	Surface	1.0	16:36	9.9	8.3	30.7	16.9	2.4	4	-	-	-
B1	20210115	Sunny	Moderate	Mid-Flood	Bottom	3.9	10:34	9.2	8.4	30.3	18.7	2.9	4	-	-	-
B1	20210115	Sunny	Moderate	Mid-Flood	Bottom	3.9	10:34	9.0	8.4	30.7	18.8	2.7	5	-	-	-
B1	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	10:35	8.7	8.4	30.6	19.0	2.5	4	-	-	-
B1	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	10:35	9.6	8.5	30.8	19.0	3.0	5	-	-	-
B2	20210115	Sunny	Moderate	Mid-Flood	Bottom	3.8	10:22	8.9	8.5	30.8	18.5	3.1	4	-	-	-
B2	20210115	Sunny	Moderate	Mid-Flood	Bottom	3.8	10:22	9.7	8.4	30.7	18.8	3.3	5	-	-	-
B2	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	10:23	9.3	8.4	30.3	18.7	3.1	4	-	-	-
B2	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	10:23	9.0	8.5	30.3	18.8	2.8	5	-	-	-
B3	20210115	Sunny	Moderate	Mid-Flood	Bottom	3.7	10:03	9.6	8.5	30.2	18.6	3.9	4	-	-	-
B3	20210115	Sunny	Moderate	Mid-Flood	Bottom	3.7	10:03	9.1	8.6	30.9	18.7	3.5	5	-	-	-
B3	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	10:04	9.6	8.4	30.2	18.4	2.8	4	-	-	-
B3	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	10:04	9.7	8.6	30.5	18.7	2.8	4	-	-	-
B4	20210115	Sunny	Moderate	Mid-Flood	Bottom	3.7	9:54	9.5	8.5	30.5	18.9	3.3	4	-	-	-
B4	20210115	Sunny	Moderate	Mid-Flood	Bottom	3.7	9:54	9.8	8.6	30.8	18.8	3.3	4	-	-	-
B4	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	9:55	9.5	8.5	30.8	18.6	3.2	5	-	-	-
B4	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	9:55	8.8	8.3	30.9	18.7	3.3	5	-	-	-
C1A	20210115	Sunny	Moderate	Mid-Flood	Bottom	10.5	8:55	9.5	8.3	30.6	18.2	3.2	5	-	-	-
C1A	20210115	Sunny	Moderate	Mid-Flood	Bottom	10.5	8:55	8.8	8.3	30.2	18.3	2.9	5	-	-	-
C1A	20210115	Sunny	Moderate	Mid-Flood	Middle	5.8	8:56	9.8	8.5	30.5	18.2	3.5	5	-	-	-
C1A	20210115	Sunny	Moderate	Mid-Flood	Middle	5.8	8:56	8.7	8.5	30.5	18.2	3.5	5	-	-	-
C1A	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	8:57	8.9	8.6	30.3	18.2	2.3	4	-	-	-
C1A	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	8:57	9.8	8.4	30.4	18.3	2.3	5	-	-	-
C2A	20210115	Sunny	Moderate	Mid-Flood	Bottom	10.1	8:00	9.2	8.3	30.3	17.8	3.0	6	-	-	-
C2A	20210115	Sunny	Moderate	Mid-Flood	Bottom	10.1	8:00	9.8	8.3	30.7	17.8	3.5	5	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
C2A	20210115	Sunny	Moderate	Mid-Flood	Middle	5.6	8:01	9.4	8.6	30.4	17.8	3.3	6	-	-	-
C2A	20210115	Sunny	Moderate	Mid-Flood	Middle	5.6	8:01	9.2	8.4	30.7	17.9	3.5	5	-	-	-
C2A	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	8:02	8.8	8.4	30.8	17.7	2.5	5	-	-	-
C2A	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	8:02	9.8	8.5	30.6	17.9	2.3	4	-	-	-
CR1	20210115	Sunny	Moderate	Mid-Flood	Bottom	11.7	8:24	8.8	8.4	30.8	17.9	3.1	5	-	-	-
CR1	20210115	Sunny	Moderate	Mid-Flood	Bottom	11.7	8:24	9.4	8.6	30.4	18.0	3.7	5	-	-	-
CR1	20210115	Sunny	Moderate	Mid-Flood	Middle	6.4	8:25	9.6	8.5	30.6	18.1	3.0	5	-	-	-
CR1	20210115	Sunny	Moderate	Mid-Flood	Middle	6.4	8:25	8.8	8.5	30.4	18.2	3.1	5	-	-	-
CR1	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	8:26	9.6	8.4	30.8	18.0	2.8	6	-	-	-
CR1	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	8:26	9.5	8.4	30.7	18.1	2.7	6	-	-	-
CR2	20210115	Sunny	Moderate	Mid-Flood	Bottom	9.8	8:36	9.1	8.4	30.5	18.0	3.0	5	-	-	-
CR2	20210115	Sunny	Moderate	Mid-Flood	Bottom	9.8	8:36	9.6	8.6	30.1	18.1	3.5	4	-	-	-
CR2	20210115	Sunny	Moderate	Mid-Flood	Middle	5.4	8:37	9.9	8.4	30.6	18.0	3.4	5	-	-	-
CR2	20210115	Sunny	Moderate	Mid-Flood	Middle	5.4	8:37	9.2	8.4	30.6	18.1	3.4	4	-	-	-
CR2	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	8:38	8.8	8.5	30.1	18.0	2.5	4	-	-	-
CR2	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	8:38	9.8	8.4	30.2	18.0	2.3	4	-	-	-
F1A	20210115	Sunny	Moderate	Mid-Flood	Bottom	7.3	9:06	9.7	8.5	30.5	18.2	2.9	4	-	-	-
F1A	20210115	Sunny	Moderate	Mid-Flood	Bottom	7.3	9:06	9.5	8.4	30.1	18.2	3.1	4	-	-	-
F1A	20210115	Sunny	Moderate	Mid-Flood	Middle	4.2	9:07	9.7	8.6	30.6	18.2	2.8	4	-	-	-
F1A	20210115	Sunny	Moderate	Mid-Flood	Middle	4.2	9:07	9.8	8.5	30.6	18.4	2.6	5	-	-	-
F1A	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	9:08	9.5	8.5	30.7	18.2	2.6	4	-	-	-
F1A	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	9:08	9.0	8.4	30.3	18.1	2.3	5	-	-	-
H1	20210115	Sunny	Moderate	Mid-Flood	Bottom	7.3	9:20	8.9	8.4	30.7	18.2	3.5	4	-	-	-
H1	20210115	Sunny	Moderate	Mid-Flood	Bottom	7.3	9:20	9.9	8.4	30.6	18.5	3.3	5	-	-	-
H1	20210115	Sunny	Moderate	Mid-Flood	Middle	4.2	9:21	9.6	8.3	30.2	18.3	3.4	5	-	-	-
H1	20210115	Sunny	Moderate	Mid-Flood	Middle	4.2	9:21	9.8	8.5	30.7	18.5	3.0	4	-	-	-
H1	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	9:22	8.7	8.4	30.7	18.2	2.9	5	-	-	-
H1	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	9:22	9.5	8.4	30.6	18.3	3.3	6	-	-	-
M1	20210115	Sunny	Moderate	Mid-Flood	Bottom	7.6	9:29	9.9	8.4	30.8	18.5	3.7	5	-	-	-
M1	20210115	Sunny	Moderate	Mid-Flood	Bottom	7.6	9:29	8.9	8.5	30.7	18.3	3.6	5	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
M1	20210115	Sunny	Moderate	Mid-Flood	Middle	4.3	9:30	8.9	8.6	30.2	18.4	3.4	5	-	-	-
M1	20210115	Sunny	Moderate	Mid-Flood	Middle	4.3	9:30	9.6	8.5	30.7	18.4	3.4	4	-	-	-
M1	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	9:31	9.4	8.6	30.8	18.4	2.5	4	-	-	-
M1	20210115	Sunny	Moderate	Mid-Flood	Surface	1.0	9:31	8.9	8.3	30.7	18.2	2.8	4	-	-	-
B1	20210115	Sunny	Moderate	Mid-Ebb	Bottom	4.0	12:58	9.7	8.5	30.3	18.8	3.0	4	-	-	-
B1	20210115	Sunny	Moderate	Mid-Ebb	Bottom	4.0	12:58	8.9	8.4	30.0	18.8	3.2	5	-	-	-
B1	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:59	9.2	8.5	29.8	18.8	2.3	5	-	-	-
B1	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:59	9.8	8.6	30.1	18.8	2.2	6	-	-	-
B2	20210115	Sunny	Moderate	Mid-Ebb	Bottom	4.5	13:14	9.6	8.5	30.3	18.7	3.7	5	-	-	-
B2	20210115	Sunny	Moderate	Mid-Ebb	Bottom	4.5	13:14	9.7	8.4	29.9	18.7	3.1	4	-	-	-
B2	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:15	9.0	8.6	30.1	18.8	2.5	4	-	-	-
B2	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:15	9.4	8.4	29.9	18.9	2.6	4	-	-	-
B3	20210115	Sunny	Moderate	Mid-Ebb	Bottom	4.1	13:32	8.8	8.5	29.9	18.7	3.1	6	-	-	-
B3	20210115	Sunny	Moderate	Mid-Ebb	Bottom	4.1	13:32	9.3	8.5	29.7	18.8	3.1	7	-	-	-
B3	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:33	9.3	8.5	29.9	18.7	2.6	5	-	-	-
B3	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:33	9.7	8.5	30.3	18.8	3.1	6	-	-	-
B4	20210115	Sunny	Moderate	Mid-Ebb	Bottom	3.7	13:39	9.2	8.4	29.8	18.7	3.8	5	-	-	-
B4	20210115	Sunny	Moderate	Mid-Ebb	Bottom	3.7	13:39	9.9	8.5	29.6	18.8	3.8	6	-	-	-
B4	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:40	9.5	8.5	30.5	18.8	2.2	5	-	-	-
B4	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:40	9.9	8.4	30.2	18.6	2.2	6	-	-	-
C1A	20210115	Sunny	Moderate	Mid-Ebb	Bottom	9.0	12:28	9.3	8.4	30.4	18.8	2.7	6	-	-	-
C1A	20210115	Sunny	Moderate	Mid-Ebb	Bottom	9.0	12:28	9.8	8.5	30.2	18.9	3.0	5	-	-	-
C1A	20210115	Sunny	Moderate	Mid-Ebb	Middle	5.0	12:29	9.6	8.4	30.3	18.9	3.4	5	-	-	-
C1A	20210115	Sunny	Moderate	Mid-Ebb	Middle	5.0	12:29	8.9	8.5	29.8	18.8	3.2	6	-	-	-
C1A	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:30	9.0	8.6	29.6	18.9	2.9	4	-	-	-
C1A	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:30	9.9	8.4	30.5	18.9	3.0	5	-	-	-
C2A	20210115	Sunny	Moderate	Mid-Ebb	Bottom	11.5	13:37	9.6	8.4	29.8	18.7	3.3	3	-	-	-
C2A	20210115	Sunny	Moderate	Mid-Ebb	Bottom	11.5	13:37	9.7	8.5	30.4	18.7	3.1	3	-	-	-
C2A	20210115	Sunny	Moderate	Mid-Ebb	Middle	6.3	13:38	9.5	8.5	30.3	18.7	3.3	3	-	-	-
C2A	20210115	Sunny	Moderate	Mid-Ebb	Middle	6.3	13:38	9.5	8.6	29.7	18.8	3.1	4	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
C2A	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:39	9.1	8.4	29.8	18.7	2.9	3	-	-	-
C2A	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:39	9.4	8.4	30.3	18.7	2.7	4	-	-	-
CR1	20210115	Sunny	Moderate	Mid-Ebb	Bottom	11.5	13:18	8.9	8.5	30.0	18.7	3.4	5	-	-	-
CR1	20210115	Sunny	Moderate	Mid-Ebb	Bottom	11.5	13:18	9.7	8.5	30.1	18.8	3.7	4	-	-	-
CR1	20210115	Sunny	Moderate	Mid-Ebb	Middle	6.3	13:19	9.2	8.4	29.7	18.8	3.1	4	-	-	-
CR1	20210115	Sunny	Moderate	Mid-Ebb	Middle	6.3	13:19	8.9	8.5	30.0	18.8	3.3	5	-	-	-
CR1	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:20	9.2	8.4	30.2	18.8	2.7	5	-	-	-
CR1	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:20	10.0	8.5	29.9	18.9	2.7	4	-	-	-
CR2	20210115	Sunny	Moderate	Mid-Ebb	Bottom	9.9	13:05	9.4	8.5	30.2	18.8	2.7	5	-	-	-
CR2	20210115	Sunny	Moderate	Mid-Ebb	Bottom	9.9	13:05	9.4	8.5	30.4	18.8	3.2	4	-	-	-
CR2	20210115	Sunny	Moderate	Mid-Ebb	Middle	5.5	13:06	9.8	8.4	29.9	18.8	3.1	4	-	-	-
CR2	20210115	Sunny	Moderate	Mid-Ebb	Middle	5.5	13:06	9.4	8.5	30.4	18.8	3.3	3	-	-	-
CR2	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:07	10.0	8.5	29.7	18.9	3.0	4	-	-	-
CR2	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:07	8.9	8.6	30.3	18.7	3.3	3	-	-	-
F1A	20210115	Sunny	Moderate	Mid-Ebb	Bottom	7.0	14:43	8.9	8.4	29.8	18.6	3.1	4	-	-	-
F1A	20210115	Sunny	Moderate	Mid-Ebb	Bottom	7.0	14:43	8.9	8.5	30.1	18.5	3.6	5	-	-	-
F1A	20210115	Sunny	Moderate	Mid-Ebb	Middle	4.0	14:44	9.9	8.4	30.2	18.7	3.2	3	-	-	-
F1A	20210115	Sunny	Moderate	Mid-Ebb	Middle	4.0	14:44	9.5	8.5	29.7	18.7	3.4	4	-	-	-
F1A	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:45	9.3	8.5	29.7	18.5	3.1	3	-	-	-
F1A	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:45	9.1	8.5	30.3	18.5	3.2	4	-	-	-
H1	20210115	Sunny	Moderate	Mid-Ebb	Bottom	7.6	12:50	8.8	8.5	30.4	18.7	2.7	6	-	-	-
H1	20210115	Sunny	Moderate	Mid-Ebb	Bottom	7.6	12:50	9.0	8.5	29.7	18.9	2.8	7	-	-	-
H1	20210115	Sunny	Moderate	Mid-Ebb	Middle	4.3	12:51	9.0	8.4	30.0	18.9	2.8	4	-	-	-
H1	20210115	Sunny	Moderate	Mid-Ebb	Middle	4.3	12:51	9.8	8.5	30.3	18.8	2.4	4	-	-	-
H1	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:52	9.8	8.5	30.1	18.9	2.6	3	-	-	-
H1	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:52	9.0	8.6	29.8	18.9	2.3	4	-	-	-
M1	20210115	Sunny	Moderate	Mid-Ebb	Bottom	7.9	14:23	9.2	8.4	29.6	18.7	2.8	6	-	-	-
M1	20210115	Sunny	Moderate	Mid-Ebb	Bottom	7.9	14:23	9.9	8.4	30.2	18.5	3.2	7	-	-	-
M1	20210115	Sunny	Moderate	Mid-Ebb	Middle	4.5	14:24	9.2	8.4	30.3	18.5	3.3	5	-	-	-
M1	20210115	Sunny	Moderate	Mid-Ebb	Middle	4.5	14:24	9.2	8.5	29.6	18.5	3.5	5	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
M1	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:25	9.5	8.6	29.6	18.8	2.5	5	-	-	-
M1	20210115	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:25	9.1	8.4	30.5	18.5	2.4	5	-	-	-
B1	20210118	Sunny	Moderate	Mid-Flood	Bottom	4.4	10:51	10.8	8.1	30.9	17.3	3.6	5	-	-	-
B1	20210118	Sunny	Moderate	Mid-Flood	Bottom	4.4	10:51	9.5	8.1	30.6	17.1	3.7	5	-	-	-
B1	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	10:52	9.7	8.2	30.7	17.2	2.3	5	-	-	-
B1	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	10:52	10.0	8.2	30.4	17.4	2.8	4	-	-	-
B2	20210118	Sunny	Moderate	Mid-Flood	Bottom	3.5	10:39	10.4	8.4	30.5	17.4	2.8	5	-	-	-
B2	20210118	Sunny	Moderate	Mid-Flood	Bottom	3.5	10:39	10.6	8.3	30.8	17.2	3.0	5	-	-	-
B2	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	10:40	9.3	8.4	30.5	17.2	2.8	5	-	-	-
B2	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	10:40	10.9	8.4	30.4	17.1	3.1	4	-	-	-
B3	20210118	Sunny	Moderate	Mid-Flood	Bottom	3.3	10:21	9.6	8.5	30.6	17.2	3.5	5	-	-	-
B3	20210118	Sunny	Moderate	Mid-Flood	Bottom	3.3	10:21	9.6	8.2	30.5	17.1	3.6	5	-	-	-
B3	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	10:22	9.1	8.1	31.2	17.4	2.7	4	-	-	-
B3	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	10:22	10.9	8.2	30.4	17.1	2.6	5	-	-	-
B4	20210118	Sunny	Moderate	Mid-Flood	Bottom	4.1	10:12	10.9	8.1	30.8	17.3	3.0	5	-	-	-
B4	20210118	Sunny	Moderate	Mid-Flood	Bottom	4.1	10:12	9.0	8.5	30.8	17.3	3.6	6	-	-	-
B4	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	10:13	10.0	8.2	31.1	17.0	2.8	6	-	-	-
B4	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	10:13	10.7	8.3	31.0	17.2	2.9	6	-	-	-
C1A	20210118	Sunny	Moderate	Mid-Flood	Bottom	10.7	9:48	10.0	8.1	30.6	16.9	3.5	5	-	-	-
C1A	20210118	Sunny	Moderate	Mid-Flood	Bottom	10.7	9:48	10.3	8.1	30.5	17.1	3.7	5	-	-	-
C1A	20210118	Sunny	Moderate	Mid-Flood	Middle	5.9	9:49	10.4	8.5	31.1	17.1	3.1	5	-	-	-
C1A	20210118	Sunny	Moderate	Mid-Flood	Middle	5.9	9:49	8.8	8.4	30.5	17.0	2.6	6	-	-	-
C1A	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	9:50	9.9	8.4	31.0	17.1	2.5	7	-	-	-
C1A	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	9:50	10.6	8.5	30.6	17.1	2.6	7	-	-	-
C2A	20210118	Sunny	Moderate	Mid-Flood	Bottom	10.3	8:48	10.8	8.2	30.8	16.9	3.4	6	-	-	-
C2A	20210118	Sunny	Moderate	Mid-Flood	Bottom	10.3	8:48	10.7	8.4	30.7	16.8	3.1	6	-	-	-
C2A	20210118	Sunny	Moderate	Mid-Flood	Middle	5.7	8:49	9.6	8.4	30.9	16.6	3.3	6	-	-	-
C2A	20210118	Sunny	Moderate	Mid-Flood	Middle	5.7	8:49	10.7	8.1	31.1	16.8	2.8	6	-	-	-
C2A	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	8:50	9.1	8.2	31.2	16.7	2.6	6	-	-	-
C2A	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	8:50	10.5	8.1	30.8	16.8	2.7	5	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
CR1	20210118	Sunny	Moderate	Mid-Flood	Bottom	12.1	9:08	10.7	8.4	31.0	16.7	3.1	6	-	-	-
CR1	20210118	Sunny	Moderate	Mid-Flood	Bottom	12.1	9:08	10.9	8.5	30.5	16.9	2.7	5	-	-	-
CR1	20210118	Sunny	Moderate	Mid-Flood	Middle	6.6	9:09	10.4	8.1	30.8	16.8	2.9	6	-	-	-
CR1	20210118	Sunny	Moderate	Mid-Flood	Middle	6.6	9:09	10.3	8.3	31.0	16.8	2.8	6	-	-	-
CR1	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	9:10	8.7	8.5	31.2	16.7	2.6	6	-	-	-
CR1	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	9:10	8.7	8.3	31.2	16.9	2.8	7	-	-	-
CR2	20210118	Sunny	Moderate	Mid-Flood	Bottom	10.4	9:24	9.7	8.2	30.8	16.8	3.1	7	-	-	-
CR2	20210118	Sunny	Moderate	Mid-Flood	Bottom	10.4	9:24	8.8	8.5	30.6	16.9	2.8	7	-	-	-
CR2	20210118	Sunny	Moderate	Mid-Flood	Middle	5.7	9:25	10.9	8.3	31.0	16.8	2.8	6	-	-	-
CR2	20210118	Sunny	Moderate	Mid-Flood	Middle	5.7	9:25	10.1	8.2	31.2	16.8	3.1	6	-	-	-
CR2	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	9:26	9.5	8.1	30.6	17.0	3.3	5	-	-	-
CR2	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	9:26	10.4	8.1	30.4	16.8	2.9	6	-	-	-
F1A	20210118	Sunny	Moderate	Mid-Flood	Bottom	7.1	9:48	9.4	8.4	30.5	16.9	3.5	6	-	-	-
F1A	20210118	Sunny	Moderate	Mid-Flood	Bottom	7.1	9:48	10.4	8.4	30.9	16.9	3.3	7	-	-	-
F1A	20210118	Sunny	Moderate	Mid-Flood	Middle	4.1	9:49	9.6	8.4	30.4	16.9	2.8	7	-	-	-
F1A	20210118	Sunny	Moderate	Mid-Flood	Middle	4.1	9:49	9.5	8.4	31.1	16.9	2.9	6	-	-	-
F1A	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	9:50	10.2	8.3	30.3	17.1	2.2	7	-	-	-
F1A	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	9:50	9.4	8.2	30.9	17.0	2.4	6	-	-	-
H1	20210118	Sunny	Moderate	Mid-Flood	Bottom	6.6	10:10	10.4	8.3	30.5	17.1	3.8	6	-	-	-
H1	20210118	Sunny	Moderate	Mid-Flood	Bottom	6.6	10:10	10.0	8.2	31.2	17.1	3.8	6	-	-	-
H1	20210118	Sunny	Moderate	Mid-Flood	Middle	3.8	10:11	10.0	8.2	30.6	17.3	3.2	7	-	-	-
H1	20210118	Sunny	Moderate	Mid-Flood	Middle	3.8	10:11	9.1	8.1	31.1	17.3	3.5	6	-	-	-
H1	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	10:12	9.8	8.4	30.9	17.3	2.3	7	-	-	-
H1	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	10:12	8.8	8.1	30.5	17.0	2.8	7	-	-	-
M1	20210118	Sunny	Moderate	Mid-Flood	Bottom	7.1	9:27	10.7	8.5	30.6	16.8	3.1	6	-	-	-
M1	20210118	Sunny	Moderate	Mid-Flood	Bottom	7.1	9:27	10.8	8.1	30.5	16.9	2.9	6	-	-	-
M1	20210118	Sunny	Moderate	Mid-Flood	Middle	4.1	9:28	10.4	8.3	30.5	16.9	3.0	7	-	-	-
M1	20210118	Sunny	Moderate	Mid-Flood	Middle	4.1	9:28	10.8	8.5	31.0	17.0	3.1	6	-	-	-
M1	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	9:29	10.8	8.4	30.5	17.0	2.9	7	-	-	-
M1	20210118	Sunny	Moderate	Mid-Flood	Surface	1.0	9:29	9.6	8.1	30.5	16.8	3.0	6	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B1	20210118	Sunny	Moderate	Mid-Ebb	Bottom	3.7	14:24	10.6	8.4	30.7	17.9	3.8	8	-	-	-
B1	20210118	Sunny	Moderate	Mid-Ebb	Bottom	3.7	14:24	10.9	8.3	30.3	17.9	3.6	7	-	-	-
B1	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:25	9.1	8.5	31.0	18.0	2.4	6	-	-	-
B1	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:25	10.0	8.3	30.8	18.1	2.4	7	-	-	-
B2	20210118	Sunny	Moderate	Mid-Ebb	Bottom	4.6	14:37	9.5	8.1	30.3	18.1	2.9	5	-	-	-
B2	20210118	Sunny	Moderate	Mid-Ebb	Bottom	4.6	14:37	10.9	8.3	30.5	18.1	3.2	6	-	-	-
B2	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:38	10.6	8.1	31.1	17.9	3.3	5	-	-	-
B2	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:38	10.0	8.3	30.2	17.9	3.1	6	-	-	-
B3	20210118	Sunny	Moderate	Mid-Ebb	Bottom	4.5	14:54	10.1	8.4	30.5	18.0	3.5	6	-	-	-
B3	20210118	Sunny	Moderate	Mid-Ebb	Bottom	4.5	14:54	9.7	8.2	31.0	18.0	3.3	7	-	-	-
B3	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:55	10.1	8.2	30.5	17.8	2.8	6	-	-	-
B3	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:55	10.5	8.4	30.9	18.0	2.8	6	-	-	-
B4	20210118	Sunny	Moderate	Mid-Ebb	Bottom	4.0	15:02	10.8	8.2	31.1	17.8	3.0	6	-	-	-
B4	20210118	Sunny	Moderate	Mid-Ebb	Bottom	4.0	15:02	10.5	8.4	30.4	17.9	2.7	6	-	-	-
B4	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	15:03	10.1	8.2	30.8	17.8	3.0	6	-	-	-
B4	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	15:03	10.0	8.5	30.6	17.7	2.7	5	-	-	-
C1A	20210118	Sunny	Moderate	Mid-Ebb	Bottom	9.0	14:22	10.4	8.3	30.6	18.1	3.5	6	-	-	-
C1A	20210118	Sunny	Moderate	Mid-Ebb	Bottom	9.0	14:22	10.1	8.4	30.5	18.0	3.3	6	-	-	-
C1A	20210118	Sunny	Moderate	Mid-Ebb	Middle	5.0	14:23	9.4	8.4	30.8	18.1	3.4	6	-	-	-
C1A	20210118	Sunny	Moderate	Mid-Ebb	Middle	5.0	14:23	10.6	8.3	30.9	18.1	3.0	6	-	-	-
C1A	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:24	9.0	8.3	30.6	18.2	3.0	5	-	-	-
C1A	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:24	10.4	8.3	31.0	18.1	2.7	6	-	-	-
C2A	20210118	Sunny	Moderate	Mid-Ebb	Bottom	11.3	15:29	9.4	8.4	31.1	17.6	3.3	7	-	-	-
C2A	20210118	Sunny	Moderate	Mid-Ebb	Bottom	11.3	15:29	10.5	8.4	30.6	17.8	3.7	7	-	-	-
C2A	20210118	Sunny	Moderate	Mid-Ebb	Middle	6.2	15:30	10.0	8.3	30.5	17.8	3.5	7	-	-	-
C2A	20210118	Sunny	Moderate	Mid-Ebb	Middle	6.2	15:30	9.4	8.3	31.1	17.7	3.1	6	-	-	-
C2A	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	15:31	9.7	8.1	31.2	17.8	2.9	5	-	-	-
C2A	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	15:31	10.7	8.3	30.6	17.6	3.3	6	-	-	-
CR1	20210118	Sunny	Moderate	Mid-Ebb	Bottom	11.8	15:10	10.5	8.3	31.0	17.7	3.2	6	-	-	-
CR1	20210118	Sunny	Moderate	Mid-Ebb	Bottom	11.8	15:10	9.1	8.2	30.9	17.7	3.8	6	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
CR1	20210118	Sunny	Moderate	Mid-Ebb	Middle	6.4	15:11	10.4	8.2	30.6	17.8	2.9	6	-	-	-
CR1	20210118	Sunny	Moderate	Mid-Ebb	Middle	6.4	15:11	10.2	8.3	30.8	17.8	3.0	6	-	-	-
CR1	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	15:12	9.7	8.3	30.5	17.8	3.0	6	-	-	-
CR1	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	15:12	9.2	8.2	30.7	17.9	2.5	7	-	-	-
CR2	20210118	Sunny	Moderate	Mid-Ebb	Bottom	10.9	14:57	10.3	8.3	30.8	17.8	3.5	6	-	-	-
CR2	20210118	Sunny	Moderate	Mid-Ebb	Bottom	10.9	14:57	10.4	8.3	30.4	18.0	3.0	5	-	-	-
CR2	20210118	Sunny	Moderate	Mid-Ebb	Middle	6.0	14:58	11.0	8.4	31.0	17.9	3.2	6	-	-	-
CR2	20210118	Sunny	Moderate	Mid-Ebb	Middle	6.0	14:58	9.2	8.3	30.6	18.0	3.5	6	-	-	-
CR2	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:59	9.5	8.5	31.0	17.9	2.7	6	-	-	-
CR2	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:59	9.0	8.3	30.9	18.0	2.8	7	-	-	-
F1A	20210118	Sunny	Moderate	Mid-Ebb	Bottom	7.7	15:50	10.2	8.3	30.7	17.6	2.8	7	-	-	-
F1A	20210118	Sunny	Moderate	Mid-Ebb	Bottom	7.7	15:50	10.2	8.2	30.6	17.7	3.0	7	-	-	-
F1A	20210118	Sunny	Moderate	Mid-Ebb	Middle	4.4	15:51	10.4	8.3	30.4	17.6	3.3	6	-	-	-
F1A	20210118	Sunny	Moderate	Mid-Ebb	Middle	4.4	15:51	10.2	8.3	30.9	17.7	3.2	6	-	-	-
F1A	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	15:52	11.0	8.2	30.9	17.6	3.0	6	-	-	-
F1A	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	15:52	10.8	8.5	30.6	17.6	2.9	6	-	-	-
H1	20210118	Sunny	Moderate	Mid-Ebb	Bottom	6.8	14:41	10.9	8.2	31.1	18.0	2.8	7	-	-	-
H1	20210118	Sunny	Moderate	Mid-Ebb	Bottom	6.8	14:41	9.4	8.3	30.9	18.1	2.7	7	-	-	-
H1	20210118	Sunny	Moderate	Mid-Ebb	Middle	3.9	14:42	9.1	8.3	30.6	17.9	3.4	7	-	-	-
H1	20210118	Sunny	Moderate	Mid-Ebb	Middle	3.9	14:42	9.2	8.2	30.6	18.2	3.1	7	-	-	-
H1	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:43	9.4	8.2	31.0	18.1	3.3	7	-	-	-
H1	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:43	10.5	8.4	30.8	18.0	3.0	8	-	-	-
M1	20210118	Sunny	Moderate	Mid-Ebb	Bottom	8.7	15:28	10.6	8.1	31.0	17.7	3.1	6	-	-	-
M1	20210118	Sunny	Moderate	Mid-Ebb	Bottom	8.7	15:28	10.3	8.1	30.9	17.8	3.1	5	-	-	-
M1	20210118	Sunny	Moderate	Mid-Ebb	Middle	4.9	15:29	10.7	8.4	30.4	17.7	3.3	6	-	-	-
M1	20210118	Sunny	Moderate	Mid-Ebb	Middle	4.9	15:29	9.5	8.1	30.6	17.8	3.4	5	-	-	-
M1	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	15:30	10.4	8.4	30.6	17.8	2.7	7	-	-	-
M1	20210118	Sunny	Moderate	Mid-Ebb	Surface	1.0	15:30	10.1	8.3	30.8	17.8	2.7	6	-	-	-
B1	20210120	Cloudy	Moderate	Mid-Flood	Bottom	4.5	12:14	9.0	8.3	31.2	19.0	3.1	6	-	-	-
B1	20210120	Cloudy	Moderate	Mid-Flood	Bottom	4.5	12:14	9.2	8.3	31.0	19.2	3.3	5	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B1	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	12:15	8.8	8.3	30.7	19.2	2.4	5	-	-	-
B1	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	12:15	9.2	8.3	31.0	18.9	2.6	5	-	-	-
B2	20210120	Cloudy	Moderate	Mid-Flood	Bottom	3.4	12:28	9.5	8.3	30.6	19.4	2.8	5	-	-	-
B2	20210120	Cloudy	Moderate	Mid-Flood	Bottom	3.4	12:28	8.9	8.2	30.7	19.3	3.3	5	-	-	-
B2	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	12:29	9.5	8.4	30.8	19.2	2.9	5	-	-	-
B2	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	12:29	8.8	8.4	30.5	19.1	2.5	5	-	-	-
B3	20210120	Cloudy	Moderate	Mid-Flood	Bottom	3.9	11:52	9.4	8.2	30.8	18.9	3.6	5	-	-	-
B3	20210120	Cloudy	Moderate	Mid-Flood	Bottom	3.9	11:52	9.1	8.5	30.4	19.2	3.7	5	-	-	-
B3	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:53	8.9	8.4	30.8	19.1	2.6	6	-	-	-
B3	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:53	9.3	8.2	31.2	19.0	2.6	6	-	-	-
B4	20210120	Cloudy	Moderate	Mid-Flood	Bottom	3.7	11:42	9.5	8.4	30.9	19.1	3.1	5	-	-	-
B4	20210120	Cloudy	Moderate	Mid-Flood	Bottom	3.7	11:42	9.1	8.4	31.1	18.9	2.7	5	-	-	-
B4	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:43	9.2	8.3	30.5	18.9	2.6	5	-	-	-
B4	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:43	9.0	8.5	30.7	18.9	2.4	5	-	-	-
C1A	20210120	Cloudy	Moderate	Mid-Flood	Bottom	10.5	11:12	9.4	8.5	30.7	18.9	3.8	5	-	-	-
C1A	20210120	Cloudy	Moderate	Mid-Flood	Bottom	10.5	11:12	9.1	8.3	30.8	18.9	3.6	5	-	-	-
C1A	20210120	Cloudy	Moderate	Mid-Flood	Middle	5.8	11:13	9.3	8.3	31.2	19.0	3.0	5	-	-	-
C1A	20210120	Cloudy	Moderate	Mid-Flood	Middle	5.8	11:13	9.1	8.5	30.8	19.0	3.3	5	-	-	-
C1A	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:14	9.3	8.4	30.8	19.1	3.1	5	-	-	-
C1A	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:14	9.2	8.4	30.8	19.1	3.2	5	-	-	-
C2A	20210120	Cloudy	Moderate	Mid-Flood	Bottom	10.5	10:15	9.4	8.5	31.1	18.9	3.3	5	-	-	-
C2A	20210120	Cloudy	Moderate	Mid-Flood	Bottom	10.5	10:15	8.7	8.4	30.5	18.9	3.0	5	-	-	-
C2A	20210120	Cloudy	Moderate	Mid-Flood	Middle	5.8	10:16	9.3	8.3	31.0	18.9	3.2	6	-	-	-
C2A	20210120	Cloudy	Moderate	Mid-Flood	Middle	5.8	10:16	9.4	8.1	31.2	18.8	2.8	6	-	-	-
C2A	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:17	9.6	8.2	31.0	18.8	2.8	6	-	-	-
C2A	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:17	9.1	8.2	31.0	18.9	2.4	6	-	-	-
CR1	20210120	Cloudy	Moderate	Mid-Flood	Bottom	11.7	10:37	9.6	8.3	31.0	18.8	3.4	5	-	-	-
CR1	20210120	Cloudy	Moderate	Mid-Flood	Bottom	11.7	10:37	8.7	8.1	30.6	18.9	3.7	5	-	-	-
CR1	20210120	Cloudy	Moderate	Mid-Flood	Middle	6.4	10:38	8.8	8.5	31.2	18.9	2.9	4	-	-	-
CR1	20210120	Cloudy	Moderate	Mid-Flood	Middle	6.4	10:38	9.2	8.2	30.6	18.8	2.6	4	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
CR1	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:39	9.3	8.3	31.1	19.0	3.1	4	-	-	-
CR1	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:39	9.0	8.2	30.9	18.8	3.1	4	-	-	-
CR2	20210120	Cloudy	Moderate	Mid-Flood	Bottom	10.7	10:52	8.7	8.1	30.9	18.8	3.1	5	-	-	-
CR2	20210120	Cloudy	Moderate	Mid-Flood	Bottom	10.7	10:52	8.8	8.4	30.8	19.0	3.3	5	-	-	-
CR2	20210120	Cloudy	Moderate	Mid-Flood	Middle	5.9	10:53	8.7	8.4	30.5	18.9	3.0	5	-	-	-
CR2	20210120	Cloudy	Moderate	Mid-Flood	Middle	5.9	10:53	9.1	8.1	31.0	18.8	2.8	5	-	-	-
CR2	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:54	9.4	8.1	31.0	18.9	3.1	5	-	-	-
CR2	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	10:54	9.3	8.1	31.1	19.1	2.9	4	-	-	-
F1A	20210120	Cloudy	Moderate	Mid-Flood	Bottom	7.5	11:19	9.5	8.1	31.0	19.1	3.3	5	-	-	-
F1A	20210120	Cloudy	Moderate	Mid-Flood	Bottom	7.5	11:19	9.5	8.4	31.1	18.8	3.2	5	-	-	-
F1A	20210120	Cloudy	Moderate	Mid-Flood	Middle	4.3	11:20	8.9	8.2	30.5	19.1	3.4	5	-	-	-
F1A	20210120	Cloudy	Moderate	Mid-Flood	Middle	4.3	11:20	9.4	8.5	30.6	19.2	2.8	4	-	-	-
F1A	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:21	9.6	8.3	31.1	19.1	3.0	4	-	-	-
F1A	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:21	8.9	8.4	30.5	18.9	2.7	4	-	-	-
H1	20210120	Cloudy	Moderate	Mid-Flood	Bottom	7.2	11:36	8.7	8.1	31.1	19.0	3.0	6	-	-	-
H1	20210120	Cloudy	Moderate	Mid-Flood	Bottom	7.2	11:36	9.5	8.3	30.6	19.0	3.0	7	-	-	-
H1	20210120	Cloudy	Moderate	Mid-Flood	Middle	4.1	11:37	9.0	8.1	30.4	19.1	2.7	5	-	-	-
H1	20210120	Cloudy	Moderate	Mid-Flood	Middle	4.1	11:37	8.8	8.2	31.0	18.9	2.8	5	-	-	-
H1	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:38	9.2	8.2	30.8	19.0	3.0	5	-	-	-
H1	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:38	9.5	8.2	31.1	18.9	2.6	4	-	-	-
M1	20210120	Cloudy	Moderate	Mid-Flood	Bottom	6.7	10:59	8.7	8.3	31.1	19.0	2.9	6	-	-	-
M1	20210120	Cloudy	Moderate	Mid-Flood	Bottom	6.7	10:59	8.8	8.4	30.6	19.0	3.4	6	-	-	-
M1	20210120	Cloudy	Moderate	Mid-Flood	Middle	3.9	11:00	9.1	8.4	30.8	19.0	3.2	5	-	-	-
M1	20210120	Cloudy	Moderate	Mid-Flood	Middle	3.9	11:00	9.3	8.4	30.5	18.9	2.8	4	-	-	-
M1	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:01	8.7	8.4	30.7	18.9	3.0	3	-	-	-
M1	20210120	Cloudy	Moderate	Mid-Flood	Surface	1.0	11:01	9.0	8.5	30.9	19.1	2.9	3	-	-	-
B1	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	4.0	16:32	8.9	8.2	30.4	19.4	3.5	3	-	-	-
B1	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	4.0	16:32	9.3	8.1	31.1	19.4	3.6	3	-	-	-
B1	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:33	9.6	8.4	30.7	19.3	3.3	4	-	-	-
B1	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:33	9.3	8.2	30.7	19.4	2.7	5	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B2	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	4.4	16:50	9.1	8.3	31.1	19.3	3.5	8	-	-	-
B2	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	4.4	16:50	9.6	8.4	30.9	19.6	3.1	8	-	-	-
B2	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:51	8.8	8.2	30.4	19.4	2.3	6	-	-	-
B2	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:51	9.6	8.4	30.9	19.5	2.3	6	-	-	-
B3	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	4.3	16:14	9.0	8.4	30.4	19.4	3.7	4	-	-	-
B3	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	4.3	16:14	9.7	8.4	30.6	19.4	3.7	4	-	-	-
B3	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:15	9.1	8.2	30.5	19.5	2.8	3	-	-	-
B3	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:15	9.4	8.4	31.0	19.3	3.3	3	-	-	-
B4	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	3.5	16:22	9.4	8.5	30.8	19.5	2.9	5	-	-	-
B4	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	3.5	16:22	9.2	8.1	30.4	19.4	3.1	5	-	-	-
B4	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:23	9.1	8.1	30.7	19.6	2.9	5	-	-	-
B4	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:23	9.5	8.2	30.4	19.4	2.7	5	-	-	-
C1A	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	9.9	16:05	9.3	8.2	31.0	19.4	3.0	4	-	-	-
C1A	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	9.9	16:05	8.9	8.5	31.0	19.4	3.5	4	-	-	-
C1A	20210120	Cloudy	Moderate	Mid-Ebb	Middle	5.5	16:06	8.9	8.2	30.8	19.3	3.3	5	-	-	-
C1A	20210120	Cloudy	Moderate	Mid-Ebb	Middle	5.5	16:06	8.9	8.1	30.6	19.4	2.9	5	-	-	-
C1A	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:07	9.5	8.4	30.6	19.5	3.2	7	-	-	-
C1A	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:07	9.6	8.5	30.4	19.6	3.2	7	-	-	-
C2A	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	10.3	17:58	9.1	8.2	30.7	19.1	3.2	4	-	-	-
C2A	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	10.3	17:58	9.5	8.3	30.6	19.3	3.0	4	-	-	-
C2A	20210120	Cloudy	Moderate	Mid-Ebb	Middle	5.7	17:59	9.3	8.2	30.4	19.2	3.2	4	-	-	-
C2A	20210120	Cloudy	Moderate	Mid-Ebb	Middle	5.7	17:59	9.2	8.1	30.5	19.1	3.0	4	-	-	-
C2A	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	18:00	9.1	8.2	30.4	19.3	3.0	3	-	-	-
C2A	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	18:00	9.4	8.4	31.0	19.3	3.0	3	-	-	-
CR1	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	11.3	17:37	9.5	8.1	30.4	19.2	2.7	6	-	-	-
CR1	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	11.3	17:37	9.0	8.2	30.8	19.2	2.7	6	-	-	-
CR1	20210120	Cloudy	Moderate	Mid-Ebb	Middle	6.2	17:38	9.3	8.4	31.0	19.3	2.7	5	-	-	-
CR1	20210120	Cloudy	Moderate	Mid-Ebb	Middle	6.2	17:38	9.1	8.1	30.8	19.2	3.0	6	-	-	-
CR1	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	17:39	9.2	8.2	30.9	19.3	2.8	5	-	-	-
CR1	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	17:39	8.9	8.4	30.4	19.1	2.7	5	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
CR2	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	10.4	17:24	9.0	8.4	30.7	19.4	3.3	7	-	-	-
CR2	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	10.4	17:24	9.2	8.3	30.8	19.3	3.8	6	-	-	-
CR2	20210120	Cloudy	Moderate	Mid-Ebb	Middle	5.7	17:25	9.0	8.3	30.5	19.3	2.8	5	-	-	-
CR2	20210120	Cloudy	Moderate	Mid-Ebb	Middle	5.7	17:25	9.1	8.4	31.0	19.2	3.2	5	-	-	-
CR2	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	17:26	9.2	8.1	30.8	19.3	2.4	5	-	-	-
CR2	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	17:26	9.0	8.4	30.4	19.2	2.3	5	-	-	-
F1A	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	7.9	17:06	9.4	8.3	31.0	19.2	3.0	5	-	-	-
F1A	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	7.9	17:06	8.9	8.3	31.0	19.3	3.5	5	-	-	-
F1A	20210120	Cloudy	Moderate	Mid-Ebb	Middle	4.5	17:07	9.4	8.3	31.1	19.3	2.5	5	-	-	-
F1A	20210120	Cloudy	Moderate	Mid-Ebb	Middle	4.5	17:07	9.2	8.3	30.6	19.3	2.3	5	-	-	-
F1A	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	17:08	9.3	8.4	30.8	19.4	2.7	4	-	-	-
F1A	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	17:08	9.4	8.5	30.6	19.4	3.2	4	-	-	-
H1	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	7.8	16:05	9.3	8.4	30.4	19.4	2.8	7	-	-	-
H1	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	7.8	16:05	9.0	8.2	30.7	19.6	3.3	7	-	-	-
H1	20210120	Cloudy	Moderate	Mid-Ebb	Middle	4.4	16:06	9.3	8.2	30.6	19.6	3.3	5	-	-	-
H1	20210120	Cloudy	Moderate	Mid-Ebb	Middle	4.4	16:06	9.7	8.2	31.0	19.4	3.1	6	-	-	-
H1	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:07	9.1	8.1	30.7	19.5	2.7	5	-	-	-
H1	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:07	9.4	8.3	30.9	19.6	2.5	4	-	-	-
M1	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	8.9	16:47	9.2	8.4	30.5	19.5	3.2	6	-	-	-
M1	20210120	Cloudy	Moderate	Mid-Ebb	Bottom	8.9	16:47	9.1	8.4	30.6	19.4	2.7	6	-	-	-
M1	20210120	Cloudy	Moderate	Mid-Ebb	Middle	5.0	16:48	9.1	8.3	30.6	19.4	3.4	5	-	-	-
M1	20210120	Cloudy	Moderate	Mid-Ebb	Middle	5.0	16:48	9.6	8.1	30.9	19.5	3.0	5	-	-	-
M1	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:49	9.0	8.4	30.9	19.5	2.7	5	-	-	-
M1	20210120	Cloudy	Moderate	Mid-Ebb	Surface	1.0	16:49	9.3	8.4	30.6	19.5	3.2	5	-	-	-
B1	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	4.1	10:37	8.8	8.4	30.9	19.8	2.5	3	-	-	-
B1	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	4.1	10:37	8.8	8.5	31.1	19.7	2.2	4	-	-	-
B1	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:38	8.8	8.5	31.1	19.5	2.7	4	-	-	-
B1	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:38	9.5	8.3	30.8	19.6	2.6	5	-	-	-
B2	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	4.9	10:23	9.0	8.5	30.7	19.7	3.3	3	-	-	-
B2	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	4.9	10:23	9.8	8.5	31.0	19.5	3.2	4	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B2	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:24	9.9	8.4	31.0	19.4	2.0	4	-	-	-
B2	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:24	9.5	8.3	31.1	19.4	1.8	4	-	-	-
B3	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	4.4	9:57	9.6	8.5	31.0	19.6	2.8	5	-	-	-
B3	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	4.4	9:57	8.9	8.4	31.1	19.4	3.0	4	-	-	-
B3	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:58	9.7	8.3	30.9	19.4	2.4	4	-	-	-
B3	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:58	9.9	8.4	31.2	19.3	2.6	5	-	-	-
B4	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	3.7	9:48	9.7	8.4	30.9	19.5	3.0	4	-	-	-
B4	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	3.7	9:48	10.1	8.4	31.0	19.3	2.6	4	-	-	-
B4	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:49	9.3	8.3	30.7	19.2	2.8	5	-	-	-
B4	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:49	8.8	8.4	30.8	19.5	2.6	4	-	-	-
C1A	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	8.9	8:19	9.1	8.3	31.0	18.8	2.5	4	-	-	-
C1A	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	8.9	8:19	9.0	8.4	30.9	18.7	2.9	5	-	-	-
C1A	20210122	Cloudy	Moderate	Mid-Ebb	Middle	5.0	8:20	8.8	8.4	31.3	18.6	2.8	4	-	-	-
C1A	20210122	Cloudy	Moderate	Mid-Ebb	Middle	5.0	8:20	9.4	8.3	31.2	18.6	2.6	4	-	-	-
C1A	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:21	9.6	8.3	31.2	18.8	2.8	3	-	-	-
C1A	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:21	9.9	8.4	31.1	18.7	2.9	3	-	-	-
C2A	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	11.4	9:41	9.7	8.3	30.9	19.4	3.2	3	-	-	-
C2A	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	11.4	9:41	9.4	8.3	30.8	19.4	2.9	4	-	-	-
C2A	20210122	Cloudy	Moderate	Mid-Ebb	Middle	6.2	9:42	9.5	8.4	30.7	19.5	2.8	4	-	-	-
C2A	20210122	Cloudy	Moderate	Mid-Ebb	Middle	6.2	9:42	8.8	8.3	30.8	19.5	2.7	3	-	-	-
C2A	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:43	9.6	8.3	31.1	19.2	2.8	3	-	-	-
C2A	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:43	9.3	8.4	31.2	19.4	2.7	2	-	-	-
CR1	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	11.8	9:29	8.8	8.3	31.1	19.2	2.2	5	-	-	-
CR1	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	11.8	9:29	10.1	8.4	30.8	19.3	2.6	4	-	-	-
CR1	20210122	Cloudy	Moderate	Mid-Ebb	Middle	6.4	9:30	8.8	8.4	31.2	19.1	2.1	3	-	-	-
CR1	20210122	Cloudy	Moderate	Mid-Ebb	Middle	6.4	9:30	9.7	8.4	31.0	19.3	2.4	4	-	-	-
CR1	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:31	9.6	8.4	30.7	19.3	2.1	2	-	-	-
CR1	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:31	8.6	8.5	31.1	19.3	2.1	3	-	-	-
CR2	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	11.0	9:19	10.0	8.4	30.9	19.2	2.7	3	-	-	-
CR2	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	11.0	9:19	8.8	8.3	31.0	19.0	2.6	4	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
CR2	20210122	Cloudy	Moderate	Mid-Ebb	Middle	6.0	9:20	9.8	8.3	31.2	19.1	2.5	3	-	-	-
CR2	20210122	Cloudy	Moderate	Mid-Ebb	Middle	6.0	9:20	9.2	8.5	30.9	19.1	2.6	3	-	-	-
CR2	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:21	8.9	8.3	31.2	19.0	2.4	3	-	-	-
CR2	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:21	9.5	8.4	30.9	19.0	2.5	3	-	-	-
F1A	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	7.0	9:25	10.0	8.4	30.8	19.2	2.8	5	-	-	-
F1A	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	7.0	9:25	9.3	8.3	31.2	19.1	3.0	4	-	-	-
F1A	20210122	Cloudy	Moderate	Mid-Ebb	Middle	4.0	9:26	8.7	8.4	30.9	19.1	2.4	3	-	-	-
F1A	20210122	Cloudy	Moderate	Mid-Ebb	Middle	4.0	9:26	9.1	8.4	30.8	19.1	2.7	3	-	-	-
F1A	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:27	8.7	8.4	31.1	19.2	2.3	3	-	-	-
F1A	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:27	9.9	8.4	30.8	19.2	2.0	3	-	-	-
H1	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	7.7	8:45	9.2	8.3	30.7	18.7	2.9	2	-	-	-
H1	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	7.7	8:45	9.1	8.5	31.0	18.7	3.3	3	-	-	-
H1	20210122	Cloudy	Moderate	Mid-Ebb	Middle	4.4	8:46	8.7	8.3	31.2	18.9	2.3	3	-	-	-
H1	20210122	Cloudy	Moderate	Mid-Ebb	Middle	4.4	8:46	10.1	8.3	30.9	18.9	1.9	4	-	-	-
H1	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:47	10.1	8.4	31.0	18.8	1.8	6	-	-	-
H1	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:47	9.1	8.5	31.0	18.8	1.8	5	-	-	-
M1	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	8.7	8:57	8.7	8.3	30.7	19.0	2.9	3	-	-	-
M1	20210122	Cloudy	Moderate	Mid-Ebb	Bottom	8.7	8:57	10.1	8.5	31.2	18.7	3.3	4	-	-	-
M1	20210122	Cloudy	Moderate	Mid-Ebb	Middle	4.9	8:58	9.1	8.5	30.8	19.0	2.4	3	-	-	-
M1	20210122	Cloudy	Moderate	Mid-Ebb	Middle	4.9	8:58	9.1	8.3	31.2	18.9	2.7	4	-	-	-
M1	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:59	9.2	8.3	31.0	18.8	2.4	2	-	-	-
M1	20210122	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:59	9.8	8.3	30.9	18.8	2.7	2	-	-	-
B1	20210122	Cloudy	Moderate	Mid-Flood	Bottom	4.3	13:24	6.9	8.3	30.5	20.5	3.1	4	-	-	-
B1	20210122	Cloudy	Moderate	Mid-Flood	Bottom	4.3	13:24	6.5	8.1	31.0	20.3	3.1	5	-	-	-
B1	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:25	7.5	8.5	30.7	20.7	2.4	5	-	-	-
B1	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:25	7.3	8.1	30.6	20.4	2.6	6	-	-	-
B2	20210122	Cloudy	Moderate	Mid-Flood	Bottom	4.1	13:37	6.8	8.2	30.9	20.6	2.3	4	-	-	-
B2	20210122	Cloudy	Moderate	Mid-Flood	Bottom	4.1	13:37	7.2	8.1	30.3	20.6	2.4	5	-	-	-
B2	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:38	7.4	8.4	30.8	20.4	2.5	3	-	-	-
B2	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:38	7.9	8.3	30.9	20.5	2.4	3	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B3	20210122	Cloudy	Moderate	Mid-Flood	Bottom	3.3	13:57	6.5	8.1	30.4	20.7	2.7	3	-	-	-
B3	20210122	Cloudy	Moderate	Mid-Flood	Bottom	3.3	13:57	6.4	8.2	30.7	20.6	2.9	4	-	-	-
B3	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:58	8.0	8.4	30.9	20.5	1.8	5	-	-	-
B3	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:58	7.4	8.1	30.7	20.7	1.7	4	-	-	-
B4	20210122	Cloudy	Moderate	Mid-Flood	Bottom	4.4	14:06	7.2	8.1	30.3	20.5	2.9	5	-	-	-
B4	20210122	Cloudy	Moderate	Mid-Flood	Bottom	4.4	14:06	7.2	8.5	30.8	20.5	2.5	4	-	-	-
B4	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:07	6.9	8.2	30.3	20.6	2.6	5	-	-	-
B4	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:07	6.3	8.2	30.3	20.5	2.3	4	-	-	-
C1A	20210122	Cloudy	Moderate	Mid-Flood	Bottom	9.3	13:03	7.7	8.3	30.5	20.5	3.5	4	-	-	-
C1A	20210122	Cloudy	Moderate	Mid-Flood	Bottom	9.3	13:03	7.9	8.4	30.9	20.5	3.2	3	-	-	-
C1A	20210122	Cloudy	Moderate	Mid-Flood	Middle	5.2	13:04	6.8	8.1	30.5	20.5	2.5	4	-	-	-
C1A	20210122	Cloudy	Moderate	Mid-Flood	Middle	5.2	13:04	7.2	8.5	30.7	20.5	2.9	4	-	-	-
C1A	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:05	7.4	8.2	30.8	20.5	2.9	5	-	-	-
C1A	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:05	6.4	8.2	30.6	20.3	2.5	6	-	-	-
C2A	20210122	Cloudy	Moderate	Mid-Flood	Bottom	10.2	13:02	10.1	8.3	30.5	20.5	2.8	3	-	-	-
C2A	20210122	Cloudy	Moderate	Mid-Flood	Bottom	10.2	13:02	7.7	8.3	30.8	20.4	2.4	4	-	-	-
C2A	20210122	Cloudy	Moderate	Mid-Flood	Middle	5.6	13:03	6.6	8.2	30.3	20.3	2.7	3	-	-	-
C2A	20210122	Cloudy	Moderate	Mid-Flood	Middle	5.6	13:03	7.6	8.1	30.7	20.4	2.9	4	-	-	-
C2A	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:04	7.7	8.5	30.5	20.3	2.1	4	-	-	-
C2A	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:04	7.9	8.4	30.3	20.5	2.3	4	-	-	-
CR1	20210122	Cloudy	Moderate	Mid-Flood	Bottom	12.0	13:24	6.6	8.1	30.8	20.4	3.0	3	-	-	-
CR1	20210122	Cloudy	Moderate	Mid-Flood	Bottom	12.0	13:24	6.9	8.5	30.9	20.6	2.9	4	-	-	-
CR1	20210122	Cloudy	Moderate	Mid-Flood	Middle	6.5	13:25	6.8	8.5	30.7	20.6	2.2	3	-	-	-
CR1	20210122	Cloudy	Moderate	Mid-Flood	Middle	6.5	13:25	7.3	8.3	30.3	20.6	2.1	4	-	-	-
CR1	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:26	7.4	8.3	30.5	20.4	2.5	4	-	-	-
CR1	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:26	7.2	8.2	30.7	20.6	2.8	4	-	-	-
CR2	20210122	Cloudy	Moderate	Mid-Flood	Bottom	10.5	13:39	7.7	8.1	30.9	20.7	3.4	4	-	-	-
CR2	20210122	Cloudy	Moderate	Mid-Flood	Bottom	10.5	13:39	6.4	8.2	31.0	20.6	3.3	5	-	-	-
CR2	20210122	Cloudy	Moderate	Mid-Flood	Middle	5.8	13:40	7.0	8.1	30.9	20.6	3.0	4	-	-	-
CR2	20210122	Cloudy	Moderate	Mid-Flood	Middle	5.8	13:40	7.3	8.2	30.4	20.5	2.7	3	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
CR2	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:41	7.0	8.1	30.5	20.4	2.9	4	-	-	-
CR2	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:41	7.6	8.3	30.2	20.4	2.5	3	-	-	-
F1A	20210122	Cloudy	Moderate	Mid-Flood	Bottom	7.2	14:53	7.1	8.2	30.6	20.4	2.9	4	-	-	-
F1A	20210122	Cloudy	Moderate	Mid-Flood	Bottom	7.2	14:53	7.8	8.2	31.0	20.5	2.9	3	-	-	-
F1A	20210122	Cloudy	Moderate	Mid-Flood	Middle	4.1	14:54	6.6	8.1	30.3	20.4	2.0	4	-	-	-
F1A	20210122	Cloudy	Moderate	Mid-Flood	Middle	4.1	14:54	6.8	8.2	30.5	20.4	2.0	4	-	-	-
F1A	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:55	6.5	8.3	31.0	20.4	2.6	6	-	-	-
F1A	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:55	7.8	8.5	30.8	20.6	2.7	5	-	-	-
H1	20210122	Cloudy	Moderate	Mid-Flood	Bottom	7.3	13:54	6.3	8.5	30.3	20.7	2.6	5	-	-	-
H1	20210122	Cloudy	Moderate	Mid-Flood	Bottom	7.3	13:54	6.8	8.2	30.3	20.4	3.0	4	-	-	-
H1	20210122	Cloudy	Moderate	Mid-Flood	Middle	4.2	13:55	7.7	8.4	30.9	20.5	2.6	5	-	-	-
H1	20210122	Cloudy	Moderate	Mid-Flood	Middle	4.2	13:55	7.5	8.4	30.8	20.6	2.7	4	-	-	-
H1	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:56	7.9	8.2	30.5	20.4	2.8	3	-	-	-
H1	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:56	6.3	8.1	30.9	20.8	2.7	3	-	-	-
M1	20210122	Cloudy	Moderate	Mid-Flood	Bottom	7.0	14:33	6.5	8.2	30.5	20.5	2.6	4	-	-	-
M1	20210122	Cloudy	Moderate	Mid-Flood	Bottom	7.0	14:33	7.2	8.2	30.9	20.4	3.1	5	-	-	-
M1	20210122	Cloudy	Moderate	Mid-Flood	Middle	4.0	14:34	8.0	8.3	30.8	20.4	2.5	4	-	-	-
M1	20210122	Cloudy	Moderate	Mid-Flood	Middle	4.0	14:34	6.5	8.1	30.6	20.3	2.6	3	-	-	-
M1	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:35	7.8	8.5	30.9	20.4	2.7	4	-	-	-
M1	20210122	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:35	6.9	8.1	30.8	20.3	3.0	3	-	-	-
B1	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	4.0	10:09	8.9	8.4	30.9	20.3	3.3	5	-	-	-
B1	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	4.0	10:09	8.3	8.2	31.4	20.2	3.3	4	-	-	-
B1	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:10	9.9	8.4	30.8	20.2	2.7	3	-	-	-
B1	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:10	9.0	8.3	30.6	20.2	2.5	4	-	-	-
B2	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	4.8	9:58	9.3	8.5	31.1	20.3	3.1	3	-	-	-
B2	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	4.8	9:58	9.5	8.4	31.3	20.3	2.9	3	-	-	-
B2	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:59	9.0	8.2	30.8	20.3	2.6	2	-	-	-
B2	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:59	9.7	8.4	30.9	20.1	2.8	3	-	-	-
B3	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	4.3	9:41	10.0	8.3	30.8	20.2	2.8	2	-	-	-
B3	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	4.3	9:41	10.0	8.6	30.7	20.2	3.3	2	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B3	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:42	10.2	8.2	30.8	20.3	2.7	2	-	-	-
B3	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:42	9.6	8.3	30.6	20.1	2.6	2	-	-	-
B4	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	3.7	9:33	9.9	8.5	30.9	20.2	3.2	3	-	-	-
B4	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	3.7	9:33	9.5	8.5	31.1	20.2	3.6	2	-	-	-
B4	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:34	9.3	8.5	30.6	20.1	3.0	3	-	-	-
B4	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:34	8.5	8.4	30.6	20.2	2.8	4	-	-	-
C1A	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	9.6	8:15	8.7	8.4	31.2	20.2	3.5	2	-	-	-
C1A	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	9.6	8:15	9.4	8.4	30.8	20.2	3.0	3	-	-	-
C1A	20210125	Cloudy	Moderate	Mid-Ebb	Middle	5.3	8:16	9.5	8.2	31.2	20.2	2.8	3	-	-	-
C1A	20210125	Cloudy	Moderate	Mid-Ebb	Middle	5.3	8:16	9.8	8.2	31.0	20.2	2.8	2	-	-	-
C1A	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:17	8.4	8.5	31.3	20.2	2.8	2	-	-	-
C1A	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:17	8.4	8.5	31.1	20.2	3.2	2	-	-	-
C2A	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	10.5	9:30	8.8	8.2	30.9	20.1	3.1	2	-	-	-
C2A	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	10.5	9:30	9.2	8.4	31.2	20.3	3.4	3	-	-	-
C2A	20210125	Cloudy	Moderate	Mid-Ebb	Middle	5.8	9:31	8.5	8.5	31.2	20.2	2.6	3	-	-	-
C2A	20210125	Cloudy	Moderate	Mid-Ebb	Middle	5.8	9:31	8.3	8.2	31.0	20.3	2.9	2	-	-	-
C2A	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:32	8.0	8.3	31.0	20.3	2.1	<2	-	-	-
C2A	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:32	9.2	8.4	30.9	20.3	2.2	<2	-	-	-
CR1	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	12.2	9:10	9.5	8.3	30.7	20.2	2.9	3	-	-	-
CR1	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	12.2	9:10	8.7	8.5	31.1	20.1	2.7	3	-	-	-
CR1	20210125	Cloudy	Moderate	Mid-Ebb	Middle	6.6	9:11	10.1	8.3	31.0	20.3	3.2	2	-	-	-
CR1	20210125	Cloudy	Moderate	Mid-Ebb	Middle	6.6	9:11	8.4	8.3	31.3	20.2	2.9	3	-	-	-
CR1	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:12	8.2	8.3	30.6	20.2	3.2	3	-	-	-
CR1	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:12	9.6	8.3	31.0	20.2	3.0	2	-	-	-
CR2	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	9.9	8:55	9.2	8.3	30.9	20.2	2.7	<2	-	-	-
CR2	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	9.9	8:55	8.6	8.3	30.9	20.2	2.8	<2	-	-	-
CR2	20210125	Cloudy	Moderate	Mid-Ebb	Middle	5.5	8:56	8.3	8.3	31.3	20.3	3.2	2	-	-	-
CR2	20210125	Cloudy	Moderate	Mid-Ebb	Middle	5.5	8:56	9.4	8.5	30.9	20.1	3.5	3	-	-	-
CR2	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:57	9.6	8.2	30.8	20.1	2.9	3	-	-	-
CR2	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:57	8.9	8.4	31.4	20.1	3.2	4	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
F1A	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	7.8	9:11	8.4	8.5	31.2	20.3	3.7	3	-	-	-
F1A	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	7.8	9:11	9.4	8.4	31.4	20.2	3.1	2	-	-	-
F1A	20210125	Cloudy	Moderate	Mid-Ebb	Middle	4.4	9:12	8.7	8.3	31.2	20.3	2.5	2	-	-	-
F1A	20210125	Cloudy	Moderate	Mid-Ebb	Middle	4.4	9:12	9.7	8.3	30.8	20.2	3.0	3	-	-	-
F1A	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:13	9.6	8.3	31.2	20.1	3.0	5	-	-	-
F1A	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:13	8.7	8.4	31.0	20.2	2.9	6	-	-	-
H1	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	6.9	8:41	9.6	8.5	31.3	20.2	3.2	5	-	-	-
H1	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	6.9	8:41	8.5	8.3	31.1	20.2	2.7	5	-	-	-
H1	20210125	Cloudy	Moderate	Mid-Ebb	Middle	4.0	8:42	8.9	8.2	30.7	20.1	2.6	5	-	-	-
H1	20210125	Cloudy	Moderate	Mid-Ebb	Middle	4.0	8:42	8.5	8.5	30.8	20.1	2.7	4	-	-	-
H1	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:43	8.8	8.3	31.0	20.1	3.1	3	-	-	-
H1	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:43	8.7	8.5	31.0	20.2	2.8	4	-	-	-
M1	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	8.4	8:50	9.1	8.5	30.8	20.1	3.1	2	-	-	-
M1	20210125	Cloudy	Moderate	Mid-Ebb	Bottom	8.4	8:50	8.4	8.5	31.0	20.1	3.6	2	-	-	-
M1	20210125	Cloudy	Moderate	Mid-Ebb	Middle	4.7	8:51	8.7	8.4	30.9	20.3	2.9	3	-	-	-
M1	20210125	Cloudy	Moderate	Mid-Ebb	Middle	4.7	8:51	8.9	8.5	31.2	20.1	2.8	3	-	-	-
M1	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:52	8.2	8.3	31.0	20.1	3.1	4	-	-	-
M1	20210125	Cloudy	Moderate	Mid-Ebb	Surface	1.0	8:52	9.9	8.5	31.1	20.1	2.8	3	-	-	-
B1	20210125	Cloudy	Moderate	Mid-Flood	Bottom	4.0	13:37	8.9	8.5	30.9	20.1	3.5	3	-	-	-
B1	20210125	Cloudy	Moderate	Mid-Flood	Bottom	4.0	13:37	8.3	8.4	30.5	20.3	3.4	4	-	-	-
B1	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:38	8.8	8.5	31.3	20.2	2.8	3	-	-	-
B1	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:38	8.5	8.3	30.8	20.2	2.5	4	-	-	-
B2	20210125	Cloudy	Moderate	Mid-Flood	Bottom	3.4	13:51	9.1	8.2	31.1	20.3	3.7	2	-	-	-
B2	20210125	Cloudy	Moderate	Mid-Flood	Bottom	3.4	13:51	9.7	8.2	31.0	20.1	3.3	3	-	-	-
B2	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:52	8.4	8.2	31.2	20.3	3.0	4	-	-	-
B2	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:52	9.1	8.3	30.7	20.2	2.8	3	-	-	-
B3	20210125	Cloudy	Moderate	Mid-Flood	Bottom	3.8	14:11	9.8	8.6	30.7	20.1	3.0	3	-	-	-
B3	20210125	Cloudy	Moderate	Mid-Flood	Bottom	3.8	14:11	9.8	8.3	30.9	20.1	3.4	3	-	-	-
B3	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:12	8.2	8.5	30.5	20.3	2.6	4	-	-	-
B3	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:12	8.8	8.4	30.6	20.2	2.7	5	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B4	20210125	Cloudy	Moderate	Mid-Flood	Bottom	4.6	14:19	9.5	8.4	30.7	20.3	2.9	6	-	-	-
B4	20210125	Cloudy	Moderate	Mid-Flood	Bottom	4.6	14:19	8.2	8.6	30.7	20.2	3.5	5	-	-	-
B4	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:20	8.4	8.4	31.2	20.2	3.2	3	-	-	-
B4	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:20	9.4	8.2	30.5	20.3	2.7	4	-	-	-
C1A	20210125	Cloudy	Moderate	Mid-Flood	Bottom	10.8	14:30	8.4	8.6	30.7	20.2	3.3	5	-	-	-
C1A	20210125	Cloudy	Moderate	Mid-Flood	Bottom	10.8	14:30	9.1	8.4	31.0	20.1	3.6	4	-	-	-
C1A	20210125	Cloudy	Moderate	Mid-Flood	Middle	5.9	14:31	9.5	8.5	31.3	20.3	3.0	3	-	-	-
C1A	20210125	Cloudy	Moderate	Mid-Flood	Middle	5.9	14:31	9.3	8.3	31.2	20.3	2.8	4	-	-	-
C1A	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:32	9.8	8.2	30.8	20.3	3.0	3	-	-	-
C1A	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:32	9.0	8.3	30.9	20.1	2.7	2	-	-	-
C2A	20210125	Cloudy	Moderate	Mid-Flood	Bottom	10.6	13:37	9.4	8.2	31.0	20.2	3.4	4	-	-	-
C2A	20210125	Cloudy	Moderate	Mid-Flood	Bottom	10.6	13:37	9.5	8.2	31.2	20.1	3.7	3	-	-	-
C2A	20210125	Cloudy	Moderate	Mid-Flood	Middle	5.8	13:38	9.6	8.2	31.1	20.3	3.2	3	-	-	-
C2A	20210125	Cloudy	Moderate	Mid-Flood	Middle	5.8	13:38	9.8	8.4	30.5	20.3	2.8	4	-	-	-
C2A	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:39	8.8	8.3	31.2	20.3	2.8	4	-	-	-
C2A	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:39	9.0	8.4	30.7	20.2	2.5	5	-	-	-
CR1	20210125	Cloudy	Moderate	Mid-Flood	Bottom	11.6	13:57	9.4	8.5	30.9	20.3	2.9	3	-	-	-
CR1	20210125	Cloudy	Moderate	Mid-Flood	Bottom	11.6	13:57	9.1	8.4	31.2	20.3	2.9	2	-	-	-
CR1	20210125	Cloudy	Moderate	Mid-Flood	Middle	6.3	13:58	8.1	8.6	31.1	20.2	3.5	2	-	-	-
CR1	20210125	Cloudy	Moderate	Mid-Flood	Middle	6.3	13:58	8.1	8.2	30.8	20.1	3.0	3	-	-	-
CR1	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:59	8.5	8.2	30.8	20.2	3.1	3	-	-	-
CR1	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	13:59	8.3	8.4	30.8	20.2	3.0	3	-	-	-
CR2	20210125	Cloudy	Moderate	Mid-Flood	Bottom	9.9	14:11	9.3	8.4	30.7	20.2	3.2	3	-	-	-
CR2	20210125	Cloudy	Moderate	Mid-Flood	Bottom	9.9	14:11	8.4	8.2	30.8	20.2	3.3	4	-	-	-
CR2	20210125	Cloudy	Moderate	Mid-Flood	Middle	5.5	14:12	8.9	8.2	30.7	20.2	3.2	5	-	-	-
CR2	20210125	Cloudy	Moderate	Mid-Flood	Middle	5.5	14:12	9.6	8.2	30.9	20.2	3.1	6	-	-	-
CR2	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:13	9.7	8.2	31.0	20.3	2.9	5	-	-	-
CR2	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:13	9.2	8.4	31.0	20.1	3.1	6	-	-	-
F1A	20210125	Cloudy	Moderate	Mid-Flood	Bottom	7.2	15:10	8.4	8.4	30.9	20.2	2.8	3	-	-	-
F1A	20210125	Cloudy	Moderate	Mid-Flood	Bottom	7.2	15:10	9.5	8.3	30.7	20.3	2.9	4	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
F1A	20210125	Cloudy	Moderate	Mid-Flood	Middle	4.1	15:11	8.8	8.6	30.9	20.3	3.0	3	-	-	-
F1A	20210125	Cloudy	Moderate	Mid-Flood	Middle	4.1	15:11	8.5	8.2	30.7	20.2	3.3	4	-	-	-
F1A	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:12	8.6	8.5	30.7	20.2	2.7	3	-	-	-
F1A	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:12	9.3	8.5	30.7	20.3	3.2	3	-	-	-
H1	20210125	Cloudy	Moderate	Mid-Flood	Bottom	7.6	14:55	9.7	8.3	31.2	20.3	3.5	3	-	-	-
H1	20210125	Cloudy	Moderate	Mid-Flood	Bottom	7.6	14:55	10.0	8.4	30.9	20.3	3.3	4	-	-	-
H1	20210125	Cloudy	Moderate	Mid-Flood	Middle	4.3	14:56	9.6	8.2	31.2	20.1	2.6	3	-	-	-
H1	20210125	Cloudy	Moderate	Mid-Flood	Middle	4.3	14:56	9.9	8.3	30.8	20.2	2.5	4	-	-	-
H1	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:57	9.9	8.3	30.5	20.3	3.0	3	-	-	-
H1	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:57	8.3	8.2	31.2	20.2	3.3	3	-	-	-
M1	20210125	Cloudy	Moderate	Mid-Flood	Bottom	6.5	14:50	8.8	8.3	31.0	20.3	2.8	3	-	-	-
M1	20210125	Cloudy	Moderate	Mid-Flood	Bottom	6.5	14:50	9.2	8.2	30.5	20.1	3.2	3	-	-	-
M1	20210125	Cloudy	Moderate	Mid-Flood	Middle	3.8	14:51	9.4	8.5	30.9	20.2	2.6	3	-	-	-
M1	20210125	Cloudy	Moderate	Mid-Flood	Middle	3.8	14:51	9.1	8.3	30.7	20.1	2.9	3	-	-	-
M1	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:52	8.8	8.4	30.8	20.2	3.3	3	-	-	-
M1	20210125	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:52	8.5	8.2	31.1	20.1	3.0	4	-	-	-
B1	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	4.2	11:48	9.6	8.5	30.8	20.0	3.3	5	-	-	-
B1	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	4.2	11:48	8.3	8.5	31.0	19.9	3.7	4	-	-	-
B1	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:49	8.8	8.5	31.0	19.8	2.0	5	-	-	-
B1	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:49	8.7	8.5	30.4	19.7	2.4	6	-	-	-
B2	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	4.5	11:35	9.1	8.5	30.6	20.0	3.7	6	-	-	-
B2	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	4.5	11:35	9.5	8.3	31.0	19.9	3.3	7	-	-	-
B2	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:36	8.7	8.4	30.4	19.8	2.4	5	-	-	-
B2	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:36	8.6	8.6	30.3	19.6	2.7	6	-	-	-
B3	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	4.3	10:47	9.5	8.3	30.6	19.5	3.0	6	-	-	-
B3	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	4.3	10:47	9.6	8.4	30.8	19.6	3.4	7	-	-	-
B3	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:48	8.6	8.5	30.3	19.6	2.9	5	-	-	-
B3	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:48	9.1	8.4	30.6	19.5	2.6	4	-	-	-
B4	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	3.3	10:56	9.2	8.3	30.3	19.7	3.5	4	-	-	-
B4	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	3.3	10:56	8.5	8.6	30.7	19.6	3.5	5	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
B4	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:57	8.4	8.3	30.8	19.6	2.4	5	-	-	-
B4	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:57	9.3	8.4	30.2	19.6	2.1	5	-	-	-
C1A	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	9.0	9:45	8.7	8.5	30.9	19.3	2.5	6	-	-	-
C1A	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	9.0	9:45	9.2	8.3	31.0	19.3	2.9	5	-	-	-
C1A	20210127	Cloudy	Moderate	Mid-Ebb	Middle	5.0	9:46	8.6	8.3	30.2	19.3	3.0	6	-	-	-
C1A	20210127	Cloudy	Moderate	Mid-Ebb	Middle	5.0	9:46	9.5	8.6	30.6	19.3	2.9	6	-	-	-
C1A	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:47	9.3	8.3	30.2	19.5	2.9	6	-	-	-
C1A	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	9:47	9.0	8.3	30.5	19.4	3.1	6	-	-	-
C2A	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	10.6	11:16	9.4	8.6	30.7	19.7	3.5	5	-	-	-
C2A	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	10.6	11:16	8.9	8.5	30.7	19.8	3.0	5	-	-	-
C2A	20210127	Cloudy	Moderate	Mid-Ebb	Middle	5.8	11:17	8.8	8.3	30.9	19.8	3.6	5	-	-	-
C2A	20210127	Cloudy	Moderate	Mid-Ebb	Middle	5.8	11:17	8.6	8.5	30.3	19.9	3.5	6	-	-	-
C2A	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:18	9.5	8.5	30.7	19.6	2.6	7	-	-	-
C2A	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:18	8.8	8.6	30.7	19.9	2.7	6	-	-	-
CR1	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	11.7	10:23	9.3	8.5	30.9	19.4	3.1	7	-	-	-
CR1	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	11.7	10:23	8.3	8.3	30.4	19.4	3.1	6	-	-	-
CR1	20210127	Cloudy	Moderate	Mid-Ebb	Middle	6.4	10:24	9.7	8.3	30.6	19.6	3.1	6	-	-	-
CR1	20210127	Cloudy	Moderate	Mid-Ebb	Middle	6.4	10:24	8.5	8.6	30.6	19.7	2.8	6	-	-	-
CR1	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:25	9.4	8.5	30.3	19.7	2.4	5	-	-	-
CR1	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:25	8.4	8.5	30.1	19.6	2.4	6	-	-	-
CR2	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	11.0	10:08	8.6	8.5	30.5	19.4	3.4	7	-	-	-
CR2	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	11.0	10:08	8.6	8.5	31.0	19.2	3.8	8	-	-	-
CR2	20210127	Cloudy	Moderate	Mid-Ebb	Middle	6.0	10:09	8.2	8.3	30.6	19.4	3.4	7	-	-	-
CR2	20210127	Cloudy	Moderate	Mid-Ebb	Middle	6.0	10:09	8.8	8.4	30.6	19.2	3.4	8	-	-	-
CR2	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:10	8.7	8.4	30.4	19.3	2.9	6	-	-	-
CR2	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:10	9.2	8.5	30.9	19.3	3.2	7	-	-	-
F1A	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	7.2	10:42	9.2	8.5	31.0	19.7	3.3	6	-	-	-
F1A	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	7.2	10:42	9.5	8.4	30.3	19.6	3.2	7	-	-	-
F1A	20210127	Cloudy	Moderate	Mid-Ebb	Middle	4.1	10:43	9.5	8.5	30.3	19.4	3.3	6	-	-	-
F1A	20210127	Cloudy	Moderate	Mid-Ebb	Middle	4.1	10:43	8.9	8.3	30.6	19.4	3.0	6	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
F1A	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:44	8.6	8.3	30.9	19.5	2.5	7	-	-	-
F1A	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:44	8.9	8.6	30.2	19.5	2.8	7	-	-	-
H1	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	7.3	11:13	9.6	8.5	30.9	19.9	2.6	5	-	-	-
H1	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	7.3	11:13	9.2	8.3	30.6	19.7	3.1	4	-	-	-
H1	20210127	Cloudy	Moderate	Mid-Ebb	Middle	4.2	11:14	9.5	8.4	30.9	19.8	3.0	5	-	-	-
H1	20210127	Cloudy	Moderate	Mid-Ebb	Middle	4.2	11:14	9.6	8.3	30.8	19.9	3.3	6	-	-	-
H1	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:15	9.3	8.6	30.9	19.9	2.3	5	-	-	-
H1	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	11:15	8.4	8.3	31.0	19.8	2.3	6	-	-	-
M1	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	8.4	10:21	8.8	8.3	30.5	19.3	3.4	8	-	-	-
M1	20210127	Cloudy	Moderate	Mid-Ebb	Bottom	8.4	10:21	9.3	8.3	30.3	19.4	2.9	7	-	-	-
M1	20210127	Cloudy	Moderate	Mid-Ebb	Middle	4.7	10:22	9.2	8.3	30.6	19.3	2.6	7	-	-	-
M1	20210127	Cloudy	Moderate	Mid-Ebb	Middle	4.7	10:22	9.2	8.3	31.0	19.6	2.8	8	-	-	-
M1	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:23	8.5	8.4	30.7	19.6	3.0	5	-	-	-
M1	20210127	Cloudy	Moderate	Mid-Ebb	Surface	1.0	10:23	8.9	8.3	30.2	19.4	2.8	4	-	-	-
B1	20210127	Cloudy	Moderate	Mid-Flood	Bottom	3.6	14:52	9.4	8.2	30.1	20.2	3.1	6	-	-	-
B1	20210127	Cloudy	Moderate	Mid-Flood	Bottom	3.6	14:52	9.2	8.5	30.2	19.9	2.7	6	-	-	-
B1	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:53	9.9	8.2	30.7	20.1	2.5	5	-	-	-
B1	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:53	9.8	8.3	30.1	20.2	2.4	4	-	-	-
B2	20210127	Cloudy	Moderate	Mid-Flood	Bottom	3.7	15:15	8.7	8.2	30.5	20.1	2.7	6	-	-	-
B2	20210127	Cloudy	Moderate	Mid-Flood	Bottom	3.7	15:15	9.7	8.4	30.7	20.1	3.0	5	-	-	-
B2	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:16	8.7	8.2	30.2	19.9	2.3	4	-	-	-
B2	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:16	9.0	8.4	30.2	20.0	2.5	3	-	-	-
B3	20210127	Cloudy	Moderate	Mid-Flood	Bottom	3.6	15:34	9.1	8.3	30.8	19.9	3.1	6	-	-	-
B3	20210127	Cloudy	Moderate	Mid-Flood	Bottom	3.6	15:34	8.4	8.5	30.3	19.8	3.0	7	-	-	-
B3	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:35	8.7	8.4	30.4	19.7	2.5	5	-	-	-
B3	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:35	9.4	8.3	30.6	20.0	2.9	6	-	-	-
B4	20210127	Cloudy	Moderate	Mid-Flood	Bottom	3.5	15:42	8.6	8.3	30.6	19.8	3.3	8	-	-	-
B4	20210127	Cloudy	Moderate	Mid-Flood	Bottom	3.5	15:42	8.5	8.4	30.4	19.9	3.2	7	-	-	-
B4	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:43	9.4	8.2	30.3	19.6	2.9	6	-	-	-
B4	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:43	8.5	8.4	29.9	19.7	2.5	7	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
C1A	20210127	Cloudy	Moderate	Mid-Flood	Bottom	10.0	15:37	9.1	8.2	30.5	19.7	2.8	6	-	-	-
C1A	20210127	Cloudy	Moderate	Mid-Flood	Bottom	10.0	15:37	9.6	8.3	30.5	19.9	3.0	7	-	-	-
C1A	20210127	Cloudy	Moderate	Mid-Flood	Middle	5.5	15:38	9.6	8.5	30.5	19.8	2.9	5	-	-	-
C1A	20210127	Cloudy	Moderate	Mid-Flood	Middle	5.5	15:38	8.8	8.4	30.2	19.6	2.7	6	-	-	-
C1A	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:39	9.9	8.3	30.3	19.8	2.7	4	-	-	-
C1A	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:39	9.8	8.3	30.2	19.9	3.0	5	-	-	-
C2A	20210127	Cloudy	Moderate	Mid-Flood	Bottom	10.4	14:45	8.4	8.4	30.1	19.9	3.2	5	-	-	-
C2A	20210127	Cloudy	Moderate	Mid-Flood	Bottom	10.4	14:45	8.5	8.3	30.1	19.7	2.8	4	-	-	-
C2A	20210127	Cloudy	Moderate	Mid-Flood	Middle	5.7	14:46	8.7	8.2	30.4	20.0	2.9	6	-	-	-
C2A	20210127	Cloudy	Moderate	Mid-Flood	Middle	5.7	14:46	8.4	8.3	30.7	19.9	2.6	6	-	-	-
C2A	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:47	9.2	8.3	30.1	19.7	2.3	6	-	-	-
C2A	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	14:47	9.3	8.5	30.4	19.8	2.2	7	-	-	-
CR1	20210127	Cloudy	Moderate	Mid-Flood	Bottom	11.3	15:05	9.2	8.3	29.9	19.8	3.2	6	-	-	-
CR1	20210127	Cloudy	Moderate	Mid-Flood	Bottom	11.3	15:05	8.8	8.2	30.7	20.1	2.9	5	-	-	-
CR1	20210127	Cloudy	Moderate	Mid-Flood	Middle	6.2	15:06	9.5	8.3	30.2	19.8	3.3	5	-	-	-
CR1	20210127	Cloudy	Moderate	Mid-Flood	Middle	6.2	15:06	9.4	8.5	30.8	19.8	3.1	5	-	-	-
CR1	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:07	8.8	8.4	30.0	19.6	2.5	5	-	-	-
CR1	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:07	9.7	8.2	30.4	19.9	2.2	5	-	-	-
CR2	20210127	Cloudy	Moderate	Mid-Flood	Bottom	9.7	15:19	9.6	8.3	30.1	20.0	3.0	5	-	-	-
CR2	20210127	Cloudy	Moderate	Mid-Flood	Bottom	9.7	15:19	8.9	8.2	30.0	19.6	3.1	5	-	-	-
CR2	20210127	Cloudy	Moderate	Mid-Flood	Middle	5.4	15:20	9.9	8.3	30.4	20.1	3.1	5	-	-	-
CR2	20210127	Cloudy	Moderate	Mid-Flood	Middle	5.4	15:20	9.6	8.4	30.1	19.7	2.7	5	-	-	-
CR2	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:21	9.1	8.4	30.1	19.6	2.7	7	-	-	-
CR2	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	15:21	9.3	8.2	30.4	19.8	2.8	6	-	-	-
F1A	20210127	Cloudy	Moderate	Mid-Flood	Bottom	7.1	16:26	9.1	8.2	30.2	19.6	3.1	6	-	-	-
F1A	20210127	Cloudy	Moderate	Mid-Flood	Bottom	7.1	16:26	8.6	8.2	30.4	19.5	2.8	5	-	-	-
F1A	20210127	Cloudy	Moderate	Mid-Flood	Middle	4.1	16:27	8.9	8.2	30.6	19.5	2.7	7	-	-	-
F1A	20210127	Cloudy	Moderate	Mid-Flood	Middle	4.1	16:27	9.4	8.2	30.4	19.4	3.0	6	-	-	-
F1A	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	16:28	8.9	8.3	30.6	19.4	2.7	6	-	-	-
F1A	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	16:28	9.9	8.3	29.9	19.5	2.7	7	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
H1	20210127	Cloudy	Moderate	Mid-Flood	Bottom	7.4	15:59	9.0	8.2	30.1	19.9	3.5	6	-	-	-
H1	20210127	Cloudy	Moderate	Mid-Flood	Bottom	7.4	15:59	9.0	8.2	30.6	20.0	3.3	7	-	-	-
H1	20210127	Cloudy	Moderate	Mid-Flood	Middle	4.2	16:00	8.7	8.2	30.7	19.6	2.5	5	-	-	-
H1	20210127	Cloudy	Moderate	Mid-Flood	Middle	4.2	16:00	9.3	8.2	30.7	19.5	2.5	4	-	-	-
H1	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	16:01	8.4	8.2	30.2	19.6	2.6	4	-	-	-
H1	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	16:01	9.3	8.3	30.6	19.7	2.2	5	-	-	-
M1	20210127	Cloudy	Moderate	Mid-Flood	Bottom	7.6	16:08	9.2	8.3	30.3	19.4	3.0	5	-	-	-
M1	20210127	Cloudy	Moderate	Mid-Flood	Bottom	7.6	16:08	9.3	8.4	29.9	19.5	3.2	6	-	-	-
M1	20210127	Cloudy	Moderate	Mid-Flood	Middle	4.3	16:09	9.3	8.3	30.2	19.8	2.9	7	-	-	-
M1	20210127	Cloudy	Moderate	Mid-Flood	Middle	4.3	16:09	9.7	8.2	29.9	19.7	3.1	8	-	-	-
M1	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	16:10	9.5	8.5	30.5	19.8	2.1	8	-	-	-
M1	20210127	Cloudy	Moderate	Mid-Flood	Surface	1.0	16:10	8.5	8.5	30.7	19.7	2.3	9	-	-	-
B1	20210129	Sunny	Moderate	Mid-Ebb	Bottom	3.6	13:04	8.3	8.4	31.1	19.7	3.5	5	-	-	-
B1	20210129	Sunny	Moderate	Mid-Ebb	Bottom	3.6	13:04	10.2	8.3	30.8	19.8	3.5	4	-	-	-
B1	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:05	8.2	8.4	31.1	19.6	3.2	3	-	-	-
B1	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:05	8.7	8.2	30.1	19.7	3.1	2	-	-	-
B2	20210129	Sunny	Moderate	Mid-Ebb	Bottom	4.0	12:51	8.6	8.2	30.3	19.7	3.5	2	-	-	-
B2	20210129	Sunny	Moderate	Mid-Ebb	Bottom	4.0	12:51	8.6	8.3	31.1	19.5	3.5	2	-	-	-
B2	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:52	9.7	8.4	30.9	19.8	2.9	<2	-	-	-
B2	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:52	8.6	8.3	30.4	19.8	3.2	<2	-	-	-
B3	20210129	Sunny	Moderate	Mid-Ebb	Bottom	3.7	12:32	9.0	8.3	31.0	19.7	2.9	2	-	-	-
B3	20210129	Sunny	Moderate	Mid-Ebb	Bottom	3.7	12:32	10.2	8.3	30.7	19.7	3.4	2	-	-	-
B3	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:33	8.8	8.4	30.9	19.9	2.8	2	-	-	-
B3	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:33	8.7	8.2	30.6	19.7	3.2	3	-	-	-
B4	20210129	Sunny	Moderate	Mid-Ebb	Bottom	3.1	12:23	9.4	8.2	31.1	19.9	3.1	3	-	-	-
B4	20210129	Sunny	Moderate	Mid-Ebb	Bottom	3.1	12:23	9.0	8.4	30.6	19.5	3.6	2	-	-	-
B4	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:24	9.8	8.3	30.9	19.6	2.8	2	-	-	-
B4	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:24	10.2	8.3	30.8	19.6	3.1	2	-	-	-
C1A	20210129	Sunny	Moderate	Mid-Ebb	Bottom	8.6	11:15	8.2	8.2	31.0	19.6	2.9	2	-	-	-
C1A	20210129	Sunny	Moderate	Mid-Ebb	Bottom	8.6	11:15	8.9	8.3	31.0	19.5	2.9	3	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
C1A	20210129	Sunny	Moderate	Mid-Ebb	Middle	4.8	11:16	9.2	8.3	30.7	19.5	3.3	2	-	-	-
C1A	20210129	Sunny	Moderate	Mid-Ebb	Middle	4.8	11:16	8.5	8.5	30.5	19.7	3.3	3	-	-	-
C1A	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:17	8.7	8.4	30.3	19.5	2.8	4	-	-	-
C1A	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:17	9.3	8.2	30.3	19.6	2.9	5	-	-	-
C2A	20210129	Sunny	Moderate	Mid-Ebb	Bottom	11.0	12:33	8.1	8.4	30.4	19.8	3.2	5	-	-	-
C2A	20210129	Sunny	Moderate	Mid-Ebb	Bottom	11.0	12:33	8.8	8.2	30.5	19.7	3.8	4	-	-	-
C2A	20210129	Sunny	Moderate	Mid-Ebb	Middle	6.0	12:34	8.2	8.3	30.8	19.8	2.6	3	-	-	-
C2A	20210129	Sunny	Moderate	Mid-Ebb	Middle	6.0	12:34	9.1	8.3	30.8	19.6	2.5	3	-	-	-
C2A	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:35	10.2	8.4	30.8	19.7	3.4	2	-	-	-
C2A	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:35	9.2	8.2	30.9	19.7	3.2	2	-	-	-
CR1	20210129	Sunny	Moderate	Mid-Ebb	Bottom	11.3	12:10	9.7	8.5	30.7	19.6	3.9	2	-	-	-
CR1	20210129	Sunny	Moderate	Mid-Ebb	Bottom	11.3	12:10	8.2	8.4	30.4	19.6	3.3	2	-	-	-
CR1	20210129	Sunny	Moderate	Mid-Ebb	Middle	6.2	12:11	9.7	8.5	30.9	19.8	3.0	2	-	-	-
CR1	20210129	Sunny	Moderate	Mid-Ebb	Middle	6.2	12:11	9.6	8.3	30.6	19.6	2.5	2	-	-	-
CR1	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:12	10.3	8.2	31.0	19.6	3.3	3	-	-	-
CR1	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:12	9.3	8.3	31.1	19.7	2.9	3	-	-	-
CR2	20210129	Sunny	Moderate	Mid-Ebb	Bottom	11.0	11:54	9.5	8.2	31.0	19.6	3.7	3	-	-	-
CR2	20210129	Sunny	Moderate	Mid-Ebb	Bottom	11.0	11:54	9.4	8.3	30.8	19.8	3.5	3	-	-	-
CR2	20210129	Sunny	Moderate	Mid-Ebb	Middle	6.0	11:55	8.7	8.3	30.9	19.8	3.0	4	-	-	-
CR2	20210129	Sunny	Moderate	Mid-Ebb	Middle	6.0	11:55	9.2	8.2	30.1	19.6	3.4	3	-	-	-
CR2	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:56	9.2	8.2	31.0	19.7	2.8	4	-	-	-
CR2	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:56	8.4	8.4	30.8	19.6	2.9	5	-	-	-
F1A	20210129	Sunny	Moderate	Mid-Ebb	Bottom	8.0	12:00	10.1	8.2	30.9	19.6	2.7	3	-	-	-
F1A	20210129	Sunny	Moderate	Mid-Ebb	Bottom	8.0	12:00	9.9	8.5	30.9	19.6	3.0	4	-	-	-
F1A	20210129	Sunny	Moderate	Mid-Ebb	Middle	4.5	12:01	9.0	8.4	30.8	19.7	2.4	5	-	-	-
F1A	20210129	Sunny	Moderate	Mid-Ebb	Middle	4.5	12:01	9.3	8.4	30.1	19.8	2.5	4	-	-	-
F1A	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:02	8.7	8.3	30.9	19.7	3.1	5	-	-	-
F1A	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:02	9.4	8.5	30.8	19.7	2.8	6	-	-	-
H1	20210129	Sunny	Moderate	Mid-Ebb	Bottom	8.0	11:40	9.1	8.5	30.5	19.7	3.1	3	-	-	-
H1	20210129	Sunny	Moderate	Mid-Ebb	Bottom	8.0	11:40	10.1	8.4	30.7	19.6	2.8	2	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
H1	20210129	Sunny	Moderate	Mid-Ebb	Middle	4.5	11:41	8.4	8.2	31.1	19.7	3.2	3	-	-	-
H1	20210129	Sunny	Moderate	Mid-Ebb	Middle	4.5	11:41	10.0	8.2	31.0	19.5	2.9	4	-	-	-
H1	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:42	9.9	8.3	30.4	19.7	2.4	3	-	-	-
H1	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:42	9.1	8.3	30.2	19.8	2.4	4	-	-	-
M1	20210129	Sunny	Moderate	Mid-Ebb	Bottom	8.9	11:36	10.1	8.4	30.6	19.6	3.6	4	-	-	-
M1	20210129	Sunny	Moderate	Mid-Ebb	Bottom	8.9	11:36	8.5	8.3	30.6	19.5	3.2	3	-	-	-
M1	20210129	Sunny	Moderate	Mid-Ebb	Middle	5.0	11:37	9.7	8.3	31.1	19.5	2.3	3	-	-	-
M1	20210129	Sunny	Moderate	Mid-Ebb	Middle	5.0	11:37	10.0	8.3	30.3	19.6	2.5	4	-	-	-
M1	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:38	9.3	8.4	31.0	19.6	2.8	3	-	-	-
M1	20210129	Sunny	Moderate	Mid-Ebb	Surface	1.0	11:38	8.6	8.4	30.6	19.6	2.4	3	-	-	-
B1	20210129	Sunny	Moderate	Mid-Flood	Bottom	4.0	15:33	8.0	8.5	30.6	19.4	4.0	4	-	-	-
B1	20210129	Sunny	Moderate	Mid-Flood	Bottom	4.0	15:33	8.9	8.3	30.2	19.4	3.5	5	-	-	-
B1	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	15:34	8.4	8.3	31.0	19.5	2.9	3	-	-	-
B1	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	15:34	8.6	8.5	31.0	19.2	3.3	3	-	-	-
B2	20210129	Sunny	Moderate	Mid-Flood	Bottom	3.4	15:45	8.1	8.2	30.8	19.4	3.0	3	-	-	-
B2	20210129	Sunny	Moderate	Mid-Flood	Bottom	3.4	15:45	8.6	8.1	31.2	19.5	3.2	3	-	-	-
B2	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	15:46	8.7	8.3	31.1	19.2	2.7	2	-	-	-
B2	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	15:46	7.9	8.4	30.7	19.2	2.3	2	-	-	-
B3	20210129	Sunny	Moderate	Mid-Flood	Bottom	3.9	16:04	8.8	8.5	31.2	19.3	3.6	3	-	-	-
B3	20210129	Sunny	Moderate	Mid-Flood	Bottom	3.9	16:04	8.2	8.4	30.8	19.5	3.1	3	-	-	-
B3	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	16:05	8.9	8.5	30.8	19.5	2.9	3	-	-	-
B3	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	16:05	8.2	8.4	31.0	19.5	3.1	4	-	-	-
B4	20210129	Sunny	Moderate	Mid-Flood	Bottom	4.6	16:12	8.7	8.5	30.5	19.5	3.1	3	-	-	-
B4	20210129	Sunny	Moderate	Mid-Flood	Bottom	4.6	16:12	8.9	8.2	30.9	19.2	3.2	2	-	-	-
B4	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	16:13	8.3	8.1	30.8	19.1	2.2	4	-	-	-
B4	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	16:13	8.7	8.4	30.2	19.5	2.6	3	-	-	-
C1A	20210129	Sunny	Moderate	Mid-Flood	Bottom	10.0	16:23	7.7	8.4	30.5	19.1	3.5	2	-	-	-
C1A	20210129	Sunny	Moderate	Mid-Flood	Bottom	10.0	16:23	8.0	8.2	30.3	19.5	3.7	2	-	-	-
C1A	20210129	Sunny	Moderate	Mid-Flood	Middle	5.5	16:24	8.3	8.3	30.5	19.5	2.9	2	-	-	-
C1A	20210129	Sunny	Moderate	Mid-Flood	Middle	5.5	16:24	8.3	8.5	30.3	19.1	3.2	2	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
C1A	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	16:25	8.0	8.4	30.5	19.2	2.9	<2	-	-	-
C1A	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	16:25	8.9	8.3	30.5	19.2	3.0	<2	-	-	-
C2A	20210129	Sunny	Moderate	Mid-Flood	Bottom	10.7	15:30	8.9	8.4	30.5	19.6	2.9	<2	-	-	-
C2A	20210129	Sunny	Moderate	Mid-Flood	Bottom	10.7	15:30	8.5	8.4	30.8	19.4	3.1	<2	-	-	-
C2A	20210129	Sunny	Moderate	Mid-Flood	Middle	5.9	15:31	8.2	8.2	30.1	19.6	3.2	2	-	-	-
C2A	20210129	Sunny	Moderate	Mid-Flood	Middle	5.9	15:31	7.8	8.2	30.9	19.3	2.7	2	-	-	-
C2A	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	15:32	8.6	8.5	30.6	19.4	2.6	3	-	-	-
C2A	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	15:32	8.6	8.3	30.7	19.4	2.9	4	-	-	-
CR1	20210129	Sunny	Moderate	Mid-Flood	Bottom	11.9	15:52	8.6	8.3	30.4	19.2	4.0	4	-	-	-
CR1	20210129	Sunny	Moderate	Mid-Flood	Bottom	11.9	15:52	8.3	8.3	30.1	19.6	3.9	5	-	-	-
CR1	20210129	Sunny	Moderate	Mid-Flood	Middle	6.5	15:53	7.9	8.3	31.2	19.3	3.3	3	-	-	-
CR1	20210129	Sunny	Moderate	Mid-Flood	Middle	6.5	15:53	7.7	8.4	30.7	19.4	3.1	2	-	-	-
CR1	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	15:54	8.7	8.4	30.5	19.3	3.1	2	-	-	-
CR1	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	15:54	8.6	8.3	31.1	19.1	3.4	2	-	-	-
CR2	20210129	Sunny	Moderate	Mid-Flood	Bottom	10.9	16:05	8.6	8.3	30.2	19.6	3.5	5	-	-	-
CR2	20210129	Sunny	Moderate	Mid-Flood	Bottom	10.9	16:05	8.0	8.3	30.8	19.1	3.8	4	-	-	-
CR2	20210129	Sunny	Moderate	Mid-Flood	Middle	6.0	16:06	8.8	8.4	30.6	19.5	2.9	2	-	-	-
CR2	20210129	Sunny	Moderate	Mid-Flood	Middle	6.0	16:06	7.7	8.2	30.8	19.3	2.7	2	-	-	-
CR2	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	16:07	7.7	8.5	30.9	19.3	3.4	3	-	-	-
CR2	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	16:07	8.9	8.1	31.1	19.4	2.9	3	-	-	-
F1A	20210129	Sunny	Moderate	Mid-Flood	Bottom	7.5	17:00	8.3	8.5	30.2	19.4	3.0	3	-	-	-
F1A	20210129	Sunny	Moderate	Mid-Flood	Bottom	7.5	17:00	9.0	8.2	30.3	19.5	3.2	2	-	-	-
F1A	20210129	Sunny	Moderate	Mid-Flood	Middle	4.3	17:01	8.9	8.4	30.3	19.4	2.6	3	-	-	-
F1A	20210129	Sunny	Moderate	Mid-Flood	Middle	4.3	17:01	7.9	8.2	30.1	19.2	2.5	4	-	-	-
F1A	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	17:02	7.8	8.2	31.2	19.4	2.9	4	-	-	-
F1A	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	17:02	9.0	8.2	30.8	19.2	3.2	4	-	-	-
H1	20210129	Sunny	Moderate	Mid-Flood	Bottom	6.5	16:46	7.8	8.3	30.8	19.2	3.0	5	-	-	-
H1	20210129	Sunny	Moderate	Mid-Flood	Bottom	6.5	16:46	8.6	8.5	30.7	19.2	3.3	4	-	-	-
H1	20210129	Sunny	Moderate	Mid-Flood	Middle	3.8	16:47	7.9	8.4	30.5	19.1	3.5	3	-	-	-
H1	20210129	Sunny	Moderate	Mid-Flood	Middle	3.8	16:47	8.6	8.5	30.7	19.1	3.1	2	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
H1	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	16:48	7.9	8.3	31.1	19.3	2.9	2	-	-	-
H1	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	16:48	8.4	8.5	30.9	19.2	2.5	2	-	-	-
M1	20210129	Sunny	Moderate	Mid-Flood	Bottom	7.1	16:39	8.0	8.3	30.6	19.2	3.1	3	-	-	-
M1	20210129	Sunny	Moderate	Mid-Flood	Bottom	7.1	16:39	8.2	8.2	31.2	19.3	3.6	3	-	-	-
M1	20210129	Sunny	Moderate	Mid-Flood	Middle	4.1	16:40	8.1	8.4	30.4	19.0	2.9	2	-	-	-
M1	20210129	Sunny	Moderate	Mid-Flood	Middle	4.1	16:40	8.3	8.3	30.5	19.3	3.4	3	-	-	-
M1	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	16:41	8.6	8.5	30.6	19.1	3.1	2	-	-	-
M1	20210129	Sunny	Moderate	Mid-Flood	Surface	1.0	16:41	8.7	8.2	30.9	19.5	2.7	2	-	-	-
B1	20210131	Sunny	Moderate	Mid-Flood	Bottom	3.9	11:02	8.4	8.4	30.9	19.1	2.8	8	-	-	-
B1	20210131	Sunny	Moderate	Mid-Flood	Bottom	3.9	11:02	8.6	8.4	30.8	19.2	3.1	8	-	-	-
B1	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	11:03	8.0	8.4	30.5	19.3	2.3	10	-	-	-
B1	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	11:03	8.9	8.3	30.9	19.2	2.4	10	-	-	-
B2	20210131	Sunny	Moderate	Mid-Flood	Bottom	3.7	10:47	8.6	8.4	30.3	19.1	3.6	7	-	-	-
B2	20210131	Sunny	Moderate	Mid-Flood	Bottom	3.7	10:47	9.3	8.4	30.7	19.2	3.3	7	-	-	-
B2	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	10:48	8.9	8.3	30.6	19.0	3.3	9	-	-	-
B2	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	10:48	8.1	8.1	30.3	19.1	3.2	9	-	-	-
B3	20210131	Sunny	Moderate	Mid-Flood	Bottom	4.0	10:25	8.2	8.3	30.2	18.8	3.8	10	-	-	-
B3	20210131	Sunny	Moderate	Mid-Flood	Bottom	4.0	10:25	8.1	8.1	30.4	19.2	3.4	9	-	-	-
B3	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	10:26	9.9	8.4	30.9	18.7	3.0	8	-	-	-
B3	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	10:26	9.5	8.1	30.9	19.1	3.3	7	-	-	-
B4	20210131	Sunny	Moderate	Mid-Flood	Bottom	4.0	10:16	9.1	8.5	30.6	18.7	3.6	11	-	-	-
B4	20210131	Sunny	Moderate	Mid-Flood	Bottom	4.0	10:16	9.4	8.1	30.3	19.1	3.1	10	-	-	-
B4	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	10:17	9.7	8.1	30.4	18.7	3.3	13	-	-	-
B4	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	10:17	9.3	8.3	30.4	19.1	3.3	12	-	-	-
C1A	20210131	Sunny	Moderate	Mid-Flood	Bottom	10.0	8:57	7.9	8.3	30.8	18.7	2.9	10	-	-	-
C1A	20210131	Sunny	Moderate	Mid-Flood	Bottom	10.0	8:57	8.0	8.1	30.8	18.6	3.3	9	-	-	-
C1A	20210131	Sunny	Moderate	Mid-Flood	Middle	5.5	8:58	9.0	8.1	30.6	18.7	2.8	7	-	-	-
C1A	20210131	Sunny	Moderate	Mid-Flood	Middle	5.5	8:58	9.6	8.3	30.5	18.6	2.7	8	-	-	-
C1A	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	8:59	9.4	8.2	30.6	18.5	3.0	6	-	-	-
C1A	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	8:59	9.1	8.3	30.9	18.9	3.3	6	-	-	-

Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
C2A	20210131	Sunny	Moderate	Mid-Flood	Bottom	10.1	8:00	8.0	8.4	30.7	18.6	3.7	6	-	-	-
C2A	20210131	Sunny	Moderate	Mid-Flood	Bottom	10.1	8:00	7.9	8.3	30.5	18.5	3.8	7	-	-	-
C2A	20210131	Sunny	Moderate	Mid-Flood	Middle	5.6	8:01	9.3	8.2	30.4	18.6	2.6	7	-	-	-
C2A	20210131	Sunny	Moderate	Mid-Flood	Middle	5.6	8:01	9.6	8.2	30.3	18.6	3.0	8	-	-	-
C2A	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	8:02	9.3	8.2	31.0	18.4	2.5	9	-	-	-
C2A	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	8:02	8.4	8.3	30.8	18.6	2.5	8	-	-	-
CR1	20210131	Sunny	Moderate	Mid-Flood	Bottom	11.4	8:21	9.9	8.3	30.8	18.6	3.5	8	-	-	-
CR1	20210131	Sunny	Moderate	Mid-Flood	Bottom	11.4	8:21	9.6	8.4	30.2	18.5	3.4	8	-	-	-
CR1	20210131	Sunny	Moderate	Mid-Flood	Middle	6.2	8:22	8.9	8.4	30.5	18.8	2.6	8	-	-	-
CR1	20210131	Sunny	Moderate	Mid-Flood	Middle	6.2	8:22	9.0	8.4	30.6	18.5	2.7	8	-	-	-
CR1	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	8:23	9.8	8.3	30.5	18.3	2.2	8	-	-	-
CR1	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	8:23	9.0	8.3	30.9	18.5	2.2	9	-	-	-
CR2	20210131	Sunny	Moderate	Mid-Flood	Bottom	10.8	8:37	9.5	8.2	30.3	18.8	3.6	8	-	-	-
CR2	20210131	Sunny	Moderate	Mid-Flood	Bottom	10.8	8:37	9.5	8.3	30.9	18.7	3.6	8	-	-	-
CR2	20210131	Sunny	Moderate	Mid-Flood	Middle	5.9	8:38	8.9	8.2	30.9	18.7	3.5	8	-	-	-
CR2	20210131	Sunny	Moderate	Mid-Flood	Middle	5.9	8:38	7.9	8.4	30.5	18.6	3.1	8	-	-	-
CR2	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	8:39	9.2	8.2	30.4	18.5	2.5	9	-	-	-
CR2	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	8:39	9.1	8.1	30.8	18.7	2.2	9	-	-	-
F1A	20210131	Sunny	Moderate	Mid-Flood	Bottom	7.5	9:07	7.9	8.2	30.8	18.6	2.8	9	-	-	-
F1A	20210131	Sunny	Moderate	Mid-Flood	Bottom	7.5	9:07	9.1	8.2	30.4	18.6	3.2	8	-	-	-
F1A	20210131	Sunny	Moderate	Mid-Flood	Middle	4.3	9:08	9.1	8.3	30.5	18.8	3.1	9	-	-	-
F1A	20210131	Sunny	Moderate	Mid-Flood	Middle	4.3	9:08	8.0	8.1	30.2	18.6	2.6	11	-	-	-
F1A	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	9:09	8.5	8.1	30.5	18.7	2.7	11	-	-	-
F1A	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	9:09	8.2	8.3	30.5	18.6	2.6	10	-	-	-
H1	20210131	Sunny	Moderate	Mid-Flood	Bottom	6.8	9:25	9.0	8.2	30.3	19.0	3.6	6	-	-	-
H1	20210131	Sunny	Moderate	Mid-Flood	Bottom	6.8	9:25	9.3	8.5	30.4	18.6	3.1	5	-	-	-
H1	20210131	Sunny	Moderate	Mid-Flood	Middle	3.9	9:26	8.8	8.1	30.3	19.0	3.0	7	-	-	-
H1	20210131	Sunny	Moderate	Mid-Flood	Middle	3.9	9:26	9.2	8.3	30.6	18.8	2.7	7	-	-	-
H1	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	9:27	8.3	8.4	30.4	19.0	2.7	8	-	-	-
H1	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	9:27	9.3	8.4	31.0	18.7	2.4	8	-	-	-


Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
M1	20210131	Sunny	Moderate	Mid-Flood	Bottom	7.2	9:30	8.9	8.2	30.9	18.9	3.0	8	-	-	-
M1	20210131	Sunny	Moderate	Mid-Flood	Bottom	7.2	9:30	7.9	8.2	30.5	19.0	2.7	7	-	-	-
M1	20210131	Sunny	Moderate	Mid-Flood	Middle	4.1	9:31	9.0	8.2	30.2	18.6	2.9	6	-	-	-
M1	20210131	Sunny	Moderate	Mid-Flood	Middle	4.1	9:31	8.9	8.4	30.7	18.8	2.6	6	-	-	-
M1	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	9:32	9.6	8.1	30.3	18.9	3.0	6	-	-	-
M1	20210131	Sunny	Moderate	Mid-Flood	Surface	1.0	9:32	8.0	8.3	30.3	18.6	3.0	5	-	-	-
B1	20210131	Sunny	Moderate	Mid-Ebb	Bottom	3.9	12:31	9.6	8.5	30.5	19.3	3.6	9	-	-	-
B1	20210131	Sunny	Moderate	Mid-Ebb	Bottom	3.9	12:31	9.0	8.3	30.4	18.9	3.6	9	-	-	-
B1	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:32	8.6	8.3	30.5	19.0	2.7	8	-	-	-
B1	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:32	9.4	8.2	31.0	19.2	2.5	8	-	-	-
B2	20210131	Sunny	Moderate	Mid-Ebb	Bottom	4.9	12:46	8.4	8.1	31.0	19.3	3.0	6	-	-	-
B2	20210131	Sunny	Moderate	Mid-Ebb	Bottom	4.9	12:46	9.0	8.5	30.9	19.1	3.1	6	-	-	-
B2	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:47	8.4	8.3	30.6	19.2	2.9	7	-	-	-
B2	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:47	8.3	8.4	30.4	19.5	2.7	7	-	-	-
B3	20210131	Sunny	Moderate	Mid-Ebb	Bottom	3.4	13:12	8.0	8.5	30.5	19.2	3.1	8	-	-	-
B3	20210131	Sunny	Moderate	Mid-Ebb	Bottom	3.4	13:12	8.8	8.2	30.6	19.5	3.2	8	-	-	-
B3	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:13	9.6	8.4	30.9	19.2	2.8	9	-	-	-
B3	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:13	8.0	8.4	31.1	19.2	3.3	10	-	-	-
B4	20210131	Sunny	Moderate	Mid-Ebb	Bottom	3.7	13:21	8.4	8.1	30.9	18.9	3.7	7	-	-	-
B4	20210131	Sunny	Moderate	Mid-Ebb	Bottom	3.7	13:21	8.0	8.3	30.4	19.0	3.2	7	-	-	-
B4	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:22	9.2	8.3	30.5	19.6	2.9	5	-	-	-
B4	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:22	9.0	8.2	30.2	19.3	2.6	5	-	-	-
C1A	20210131	Sunny	Moderate	Mid-Ebb	Bottom	8.4	12:31	9.0	8.2	30.3	19.1	3.7	7	-	-	-
C1A	20210131	Sunny	Moderate	Mid-Ebb	Bottom	8.4	12:31	9.4	8.1	30.8	19.4	3.2	6	-	-	-
C1A	20210131	Sunny	Moderate	Mid-Ebb	Middle	4.7	12:32	9.2	8.4	30.7	19.4	2.9	7	-	-	-
C1A	20210131	Sunny	Moderate	Mid-Ebb	Middle	4.7	12:32	9.7	8.5	30.7	19.1	3.3	7	-	-	-
C1A	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:33	9.3	8.2	31.0	18.7	2.2	9	-	-	-
C1A	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:33	9.5	8.1	30.9	19.1	2.6	8	-	-	-
C2A	20210131	Sunny	Moderate	Mid-Ebb	Bottom	10.9	13:42	9.4	8.3	31.1	18.9	3.0	8	-	-	-
C2A	20210131	Sunny	Moderate	Mid-Ebb	Bottom	10.9	13:42	8.9	8.4	31.1	18.9	2.9	8	-	-	-


Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
C2A	20210131	Sunny	Moderate	Mid-Ebb	Middle	6.0	13:43	9.6	8.2	30.8	18.8	2.6	5	-	-	-
C2A	20210131	Sunny	Moderate	Mid-Ebb	Middle	6.0	13:43	8.6	8.2	30.7	19.0	2.8	6	-	-	-
C2A	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:44	8.9	8.4	30.7	18.8	3.3	6	-	-	-
C2A	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:44	9.9	8.4	31.0	18.7	2.9	6	-	-	-
CR1	20210131	Sunny	Moderate	Mid-Ebb	Bottom	12.6	13:20	9.5	8.2	30.5	18.9	2.8	6	-	-	-
CR1	20210131	Sunny	Moderate	Mid-Ebb	Bottom	12.6	13:20	8.5	8.4	30.3	19.2	3.3	7	-	-	-
CR1	20210131	Sunny	Moderate	Mid-Ebb	Middle	6.8	13:21	9.4	8.5	30.6	19.2	3.4	6	-	-	-
CR1	20210131	Sunny	Moderate	Mid-Ebb	Middle	6.8	13:21	9.7	8.4	31.0	19.5	3.3	7	-	-	-
CR1	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:22	8.1	8.5	31.1	18.9	3.2	8	-	-	-
CR1	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:22	8.4	8.2	30.4	19.5	2.9	9	-	-	-
CR2	20210131	Sunny	Moderate	Mid-Ebb	Bottom	10.9	13:06	8.7	8.3	31.0	19.3	3.0	8	-	-	-
CR2	20210131	Sunny	Moderate	Mid-Ebb	Bottom	10.9	13:06	9.9	8.2	31.1	19.1	3.4	8	-	-	-
CR2	20210131	Sunny	Moderate	Mid-Ebb	Middle	6.0	13:07	8.5	8.2	31.1	18.8	3.0	7	-	-	-
CR2	20210131	Sunny	Moderate	Mid-Ebb	Middle	6.0	13:07	8.7	8.2	31.1	18.9	3.4	7	-	-	-
CR2	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:08	9.1	8.3	30.6	19.4	2.4	6	-	-	-
CR2	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:08	8.5	8.3	30.2	19.4	2.8	5	-	-	-
F1A	20210131	Sunny	Moderate	Mid-Ebb	Bottom	7.6	14:08	9.8	8.3	31.0	19.4	3.0	8	-	-	-
F1A	20210131	Sunny	Moderate	Mid-Ebb	Bottom	7.6	14:08	8.5	8.4	31.0	19.2	2.8	8	-	-	-
F1A	20210131	Sunny	Moderate	Mid-Ebb	Middle	4.3	14:09	8.9	8.4	30.2	18.9	2.9	7	-	-	-
F1A	20210131	Sunny	Moderate	Mid-Ebb	Middle	4.3	14:09	8.5	8.2	30.6	19.4	2.9	7	-	-	-
F1A	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:10	8.3	8.3	30.5	18.7	2.6	6	-	-	-
F1A	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	14:10	9.4	8.4	31.2	18.9	2.6	6	-	-	-
H1	20210131	Sunny	Moderate	Mid-Ebb	Bottom	7.1	12:51	8.2	8.2	30.3	19.3	3.5	7	-	-	-
H1	20210131	Sunny	Moderate	Mid-Ebb	Bottom	7.1	12:51	9.3	8.4	30.8	19.3	3.4	8	-	-	-
H1	20210131	Sunny	Moderate	Mid-Ebb	Middle	4.1	12:52	9.3	8.1	30.2	19.2	3.3	7	-	-	-
H1	20210131	Sunny	Moderate	Mid-Ebb	Middle	4.1	12:52	9.4	8.3	30.3	19.0	3.2	7	-	-	-
H1	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:53	9.4	8.5	31.2	19.6	2.2	6	-	-	-
H1	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	12:53	8.3	8.3	31.1	18.9	2.5	6	-	-	-
M1	20210131	Sunny	Moderate	Mid-Ebb	Bottom	8.2	13:46	8.7	8.1	31.1	19.3	3.1	6	-	-	-
M1	20210131	Sunny	Moderate	Mid-Ebb	Bottom	8.2	13:46	8.4	8.2	30.5	18.8	3.4	6	-	-	-


Location	Date (YYYYMMDD)	Weather	Sea Condition	Tidal	Water Level	Depth (m)	Time (hh:mm)	DO (mg/L)	pH	Sal (ppt)	Temp (° C)	Turbidty (NTU) note 1	SS (mg/L)	Total Alkalinity (mg/L)	Current Velocity (m/s)	Direction in NESW
M1	20210131	Sunny	Moderate	Mid-Ebb	Middle	4.6	13:47	8.7	8.5	30.2	19.1	3.2	8	-	-	-
M1	20210131	Sunny	Moderate	Mid-Ebb	Middle	4.6	13:47	8.3	8.3	31.0	19.1	2.9	8	-	-	-
M1	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:48	8.5	8.3	30.9	19.5	3.0	8	-	-	-
M1	20210131	Sunny	Moderate	Mid-Ebb	Surface	1.0	13:48	8.8	8.2	31.2	19.0	3.2	9	-	-	-

Remark


Note 1: Measurements of turbidity would be rounding to 0.1 NTU for proven accuracy as per the equipment specs during utilization of data.

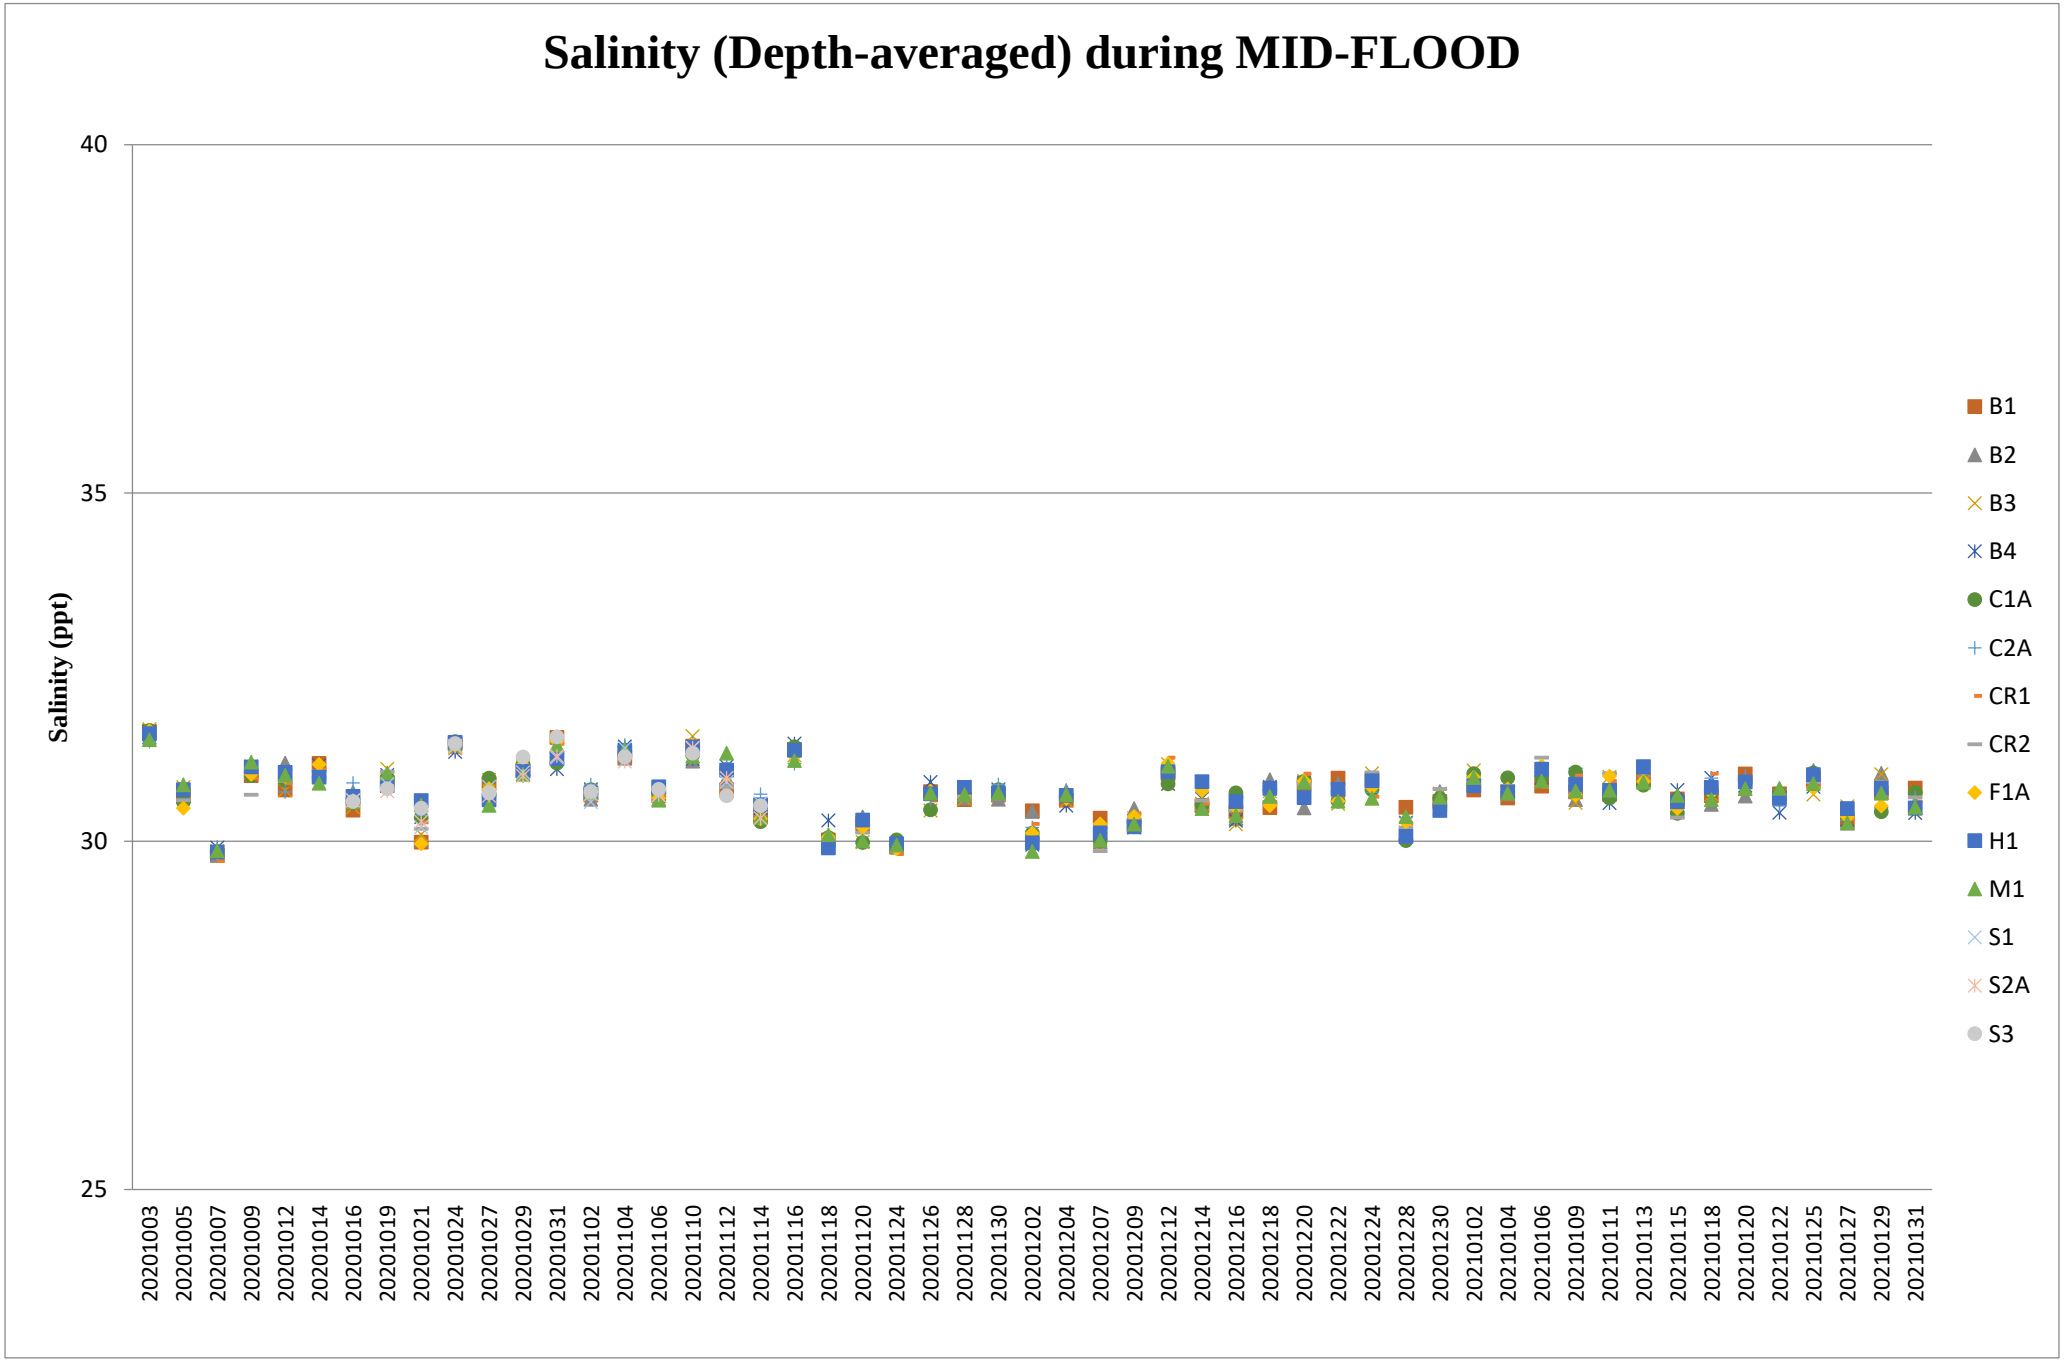
Salinity (Depth-averaged) during MID-FLOOD
Salinity (ppt)
40
35
30
25
20201003
20201005
20201007
20201009
20201012
20201014
20201016
20201019
20201021
20201024
20201027
20201029
20201031
20201102
20201104
20201106
20201110
20201112
20201114
20201116
20201118
20201120
20201124
20201126
20201128
20201130
20201202
20201204
20201207
20201209
20201212
20201214
20201216
20201218
20201220
20201222
20201224
20201228
20201230
20210102
20210104
20210106
20210109
20210111
20210113
20210115
20210118
20210120
20210122
20210125
20210127
20210129
20210131
B1
B2
B3
B4
C1A
C2A
CR1
CR2
F1A
H1
M1
S1
S2A
S3

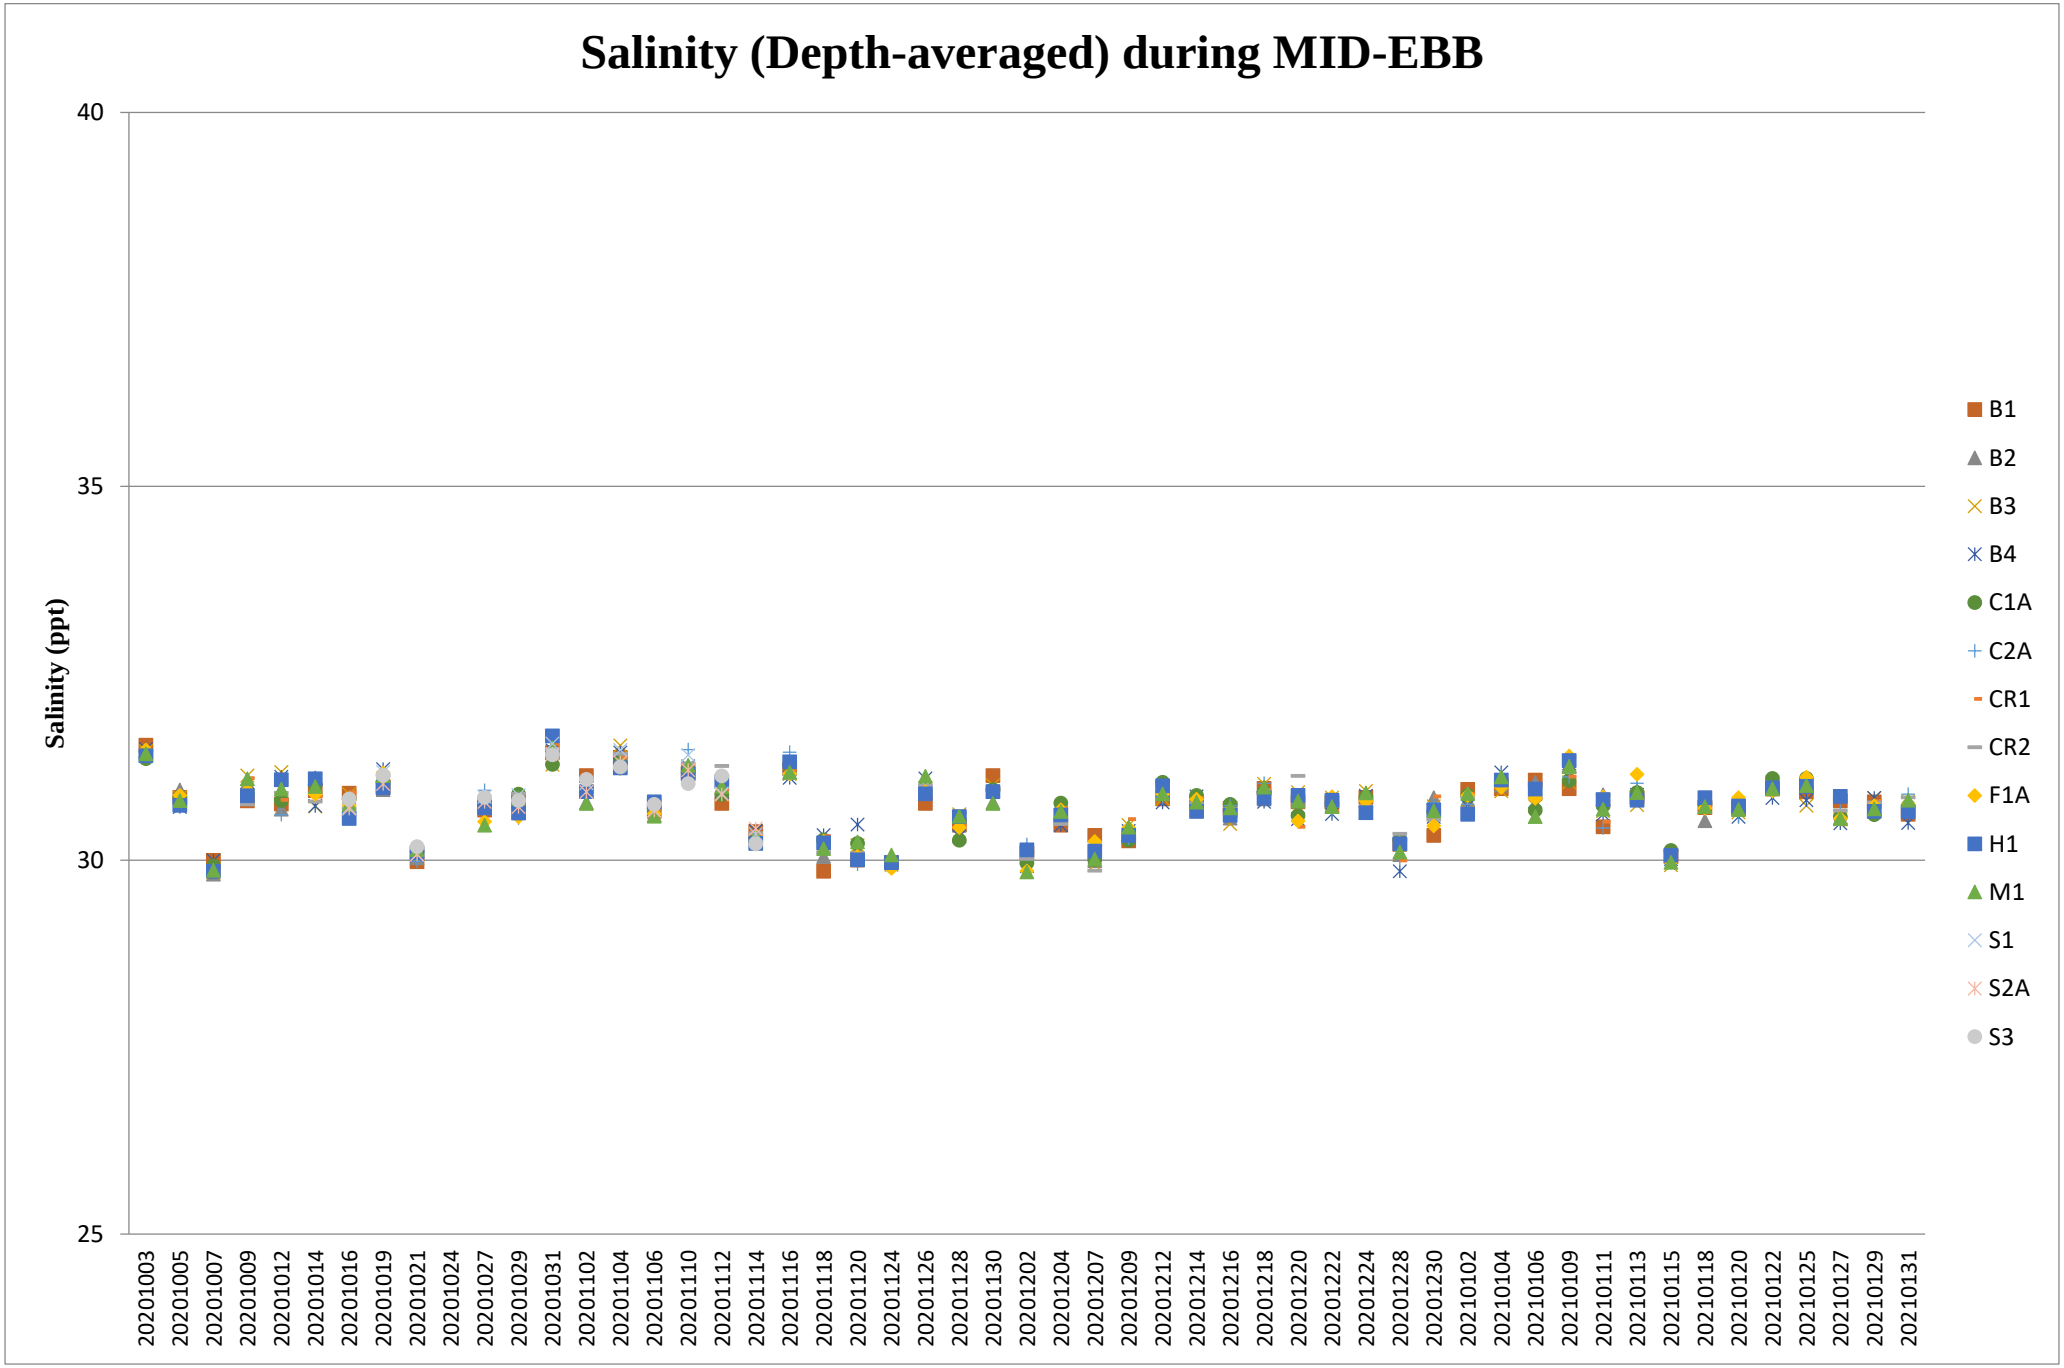

Salinity (Depth-averaged) during MID-EBB
Salinity (ppt)
40
35
30
25
20201003
20201005
20201007
20201009
20201012
20201014
20201016
20201019
20201021
20201024
20201027
20201029
20201031
20201102
20201104
20201106
20201110
20201112
20201114
20201116
20201118
20201120
20201124
20201126
20201128
20201130
20201202
20201204
20201207
20201209
20201212
20201214
20201216
20201218
20201220
20201222
20201224
20201228
20201230
20210102
20210104
20210106
20210109
20210111
20210113
20210115
20210118
20210120
20210122
20210125
20210127
20210129
20210131
B1
B2
B3
B4
C1A
C2A
CR1
CR2
F1A
H1
M1
S1
S2A
S3

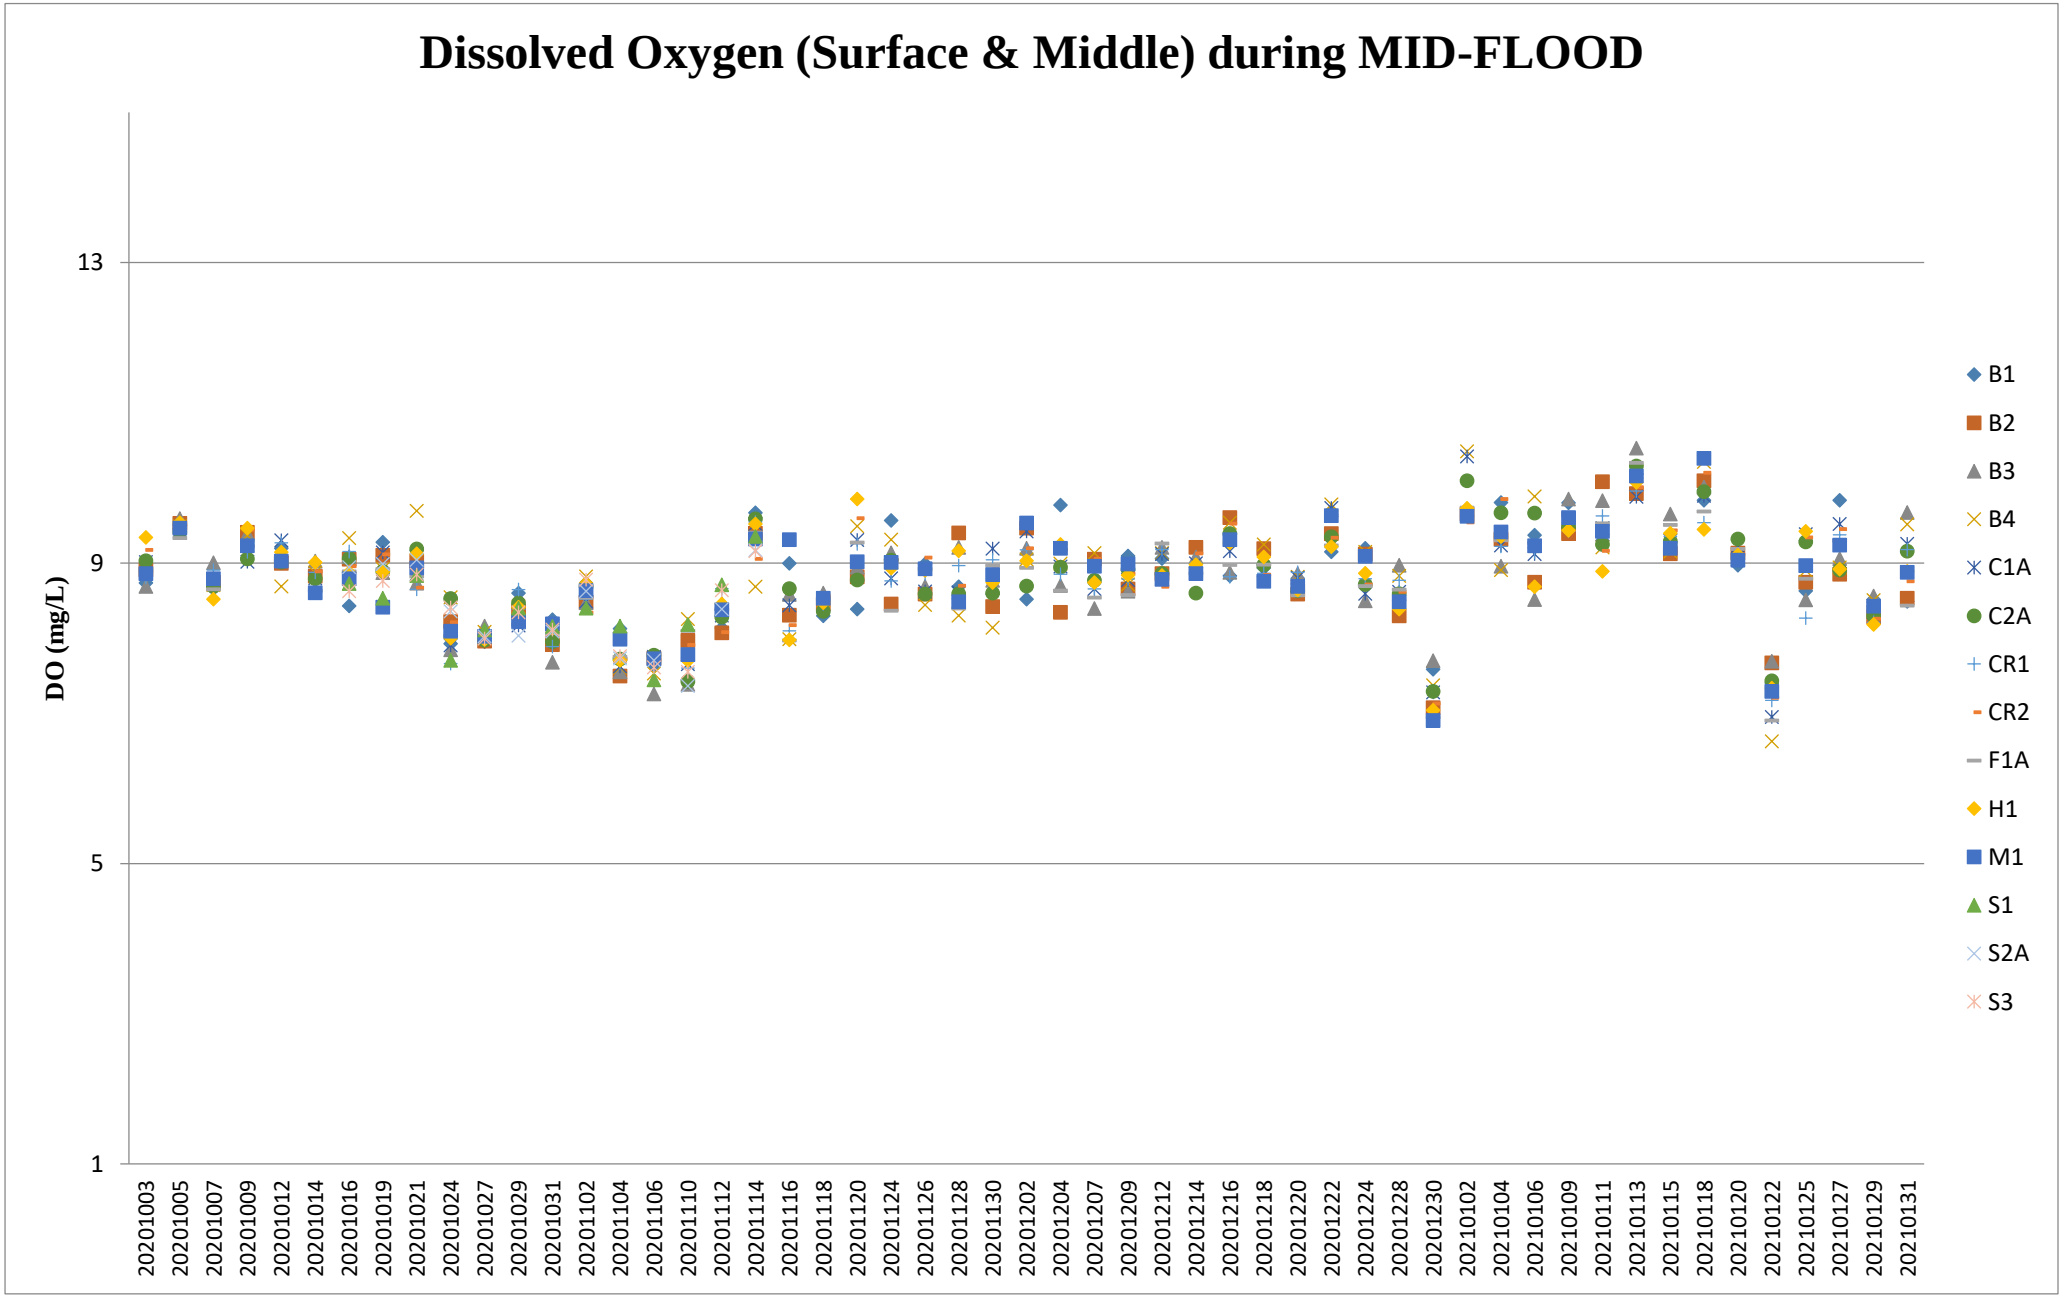


Note: The Action and Limit Level of dissolved oxygen can be referred to **Table 2.7** of the monthly EM&A report.

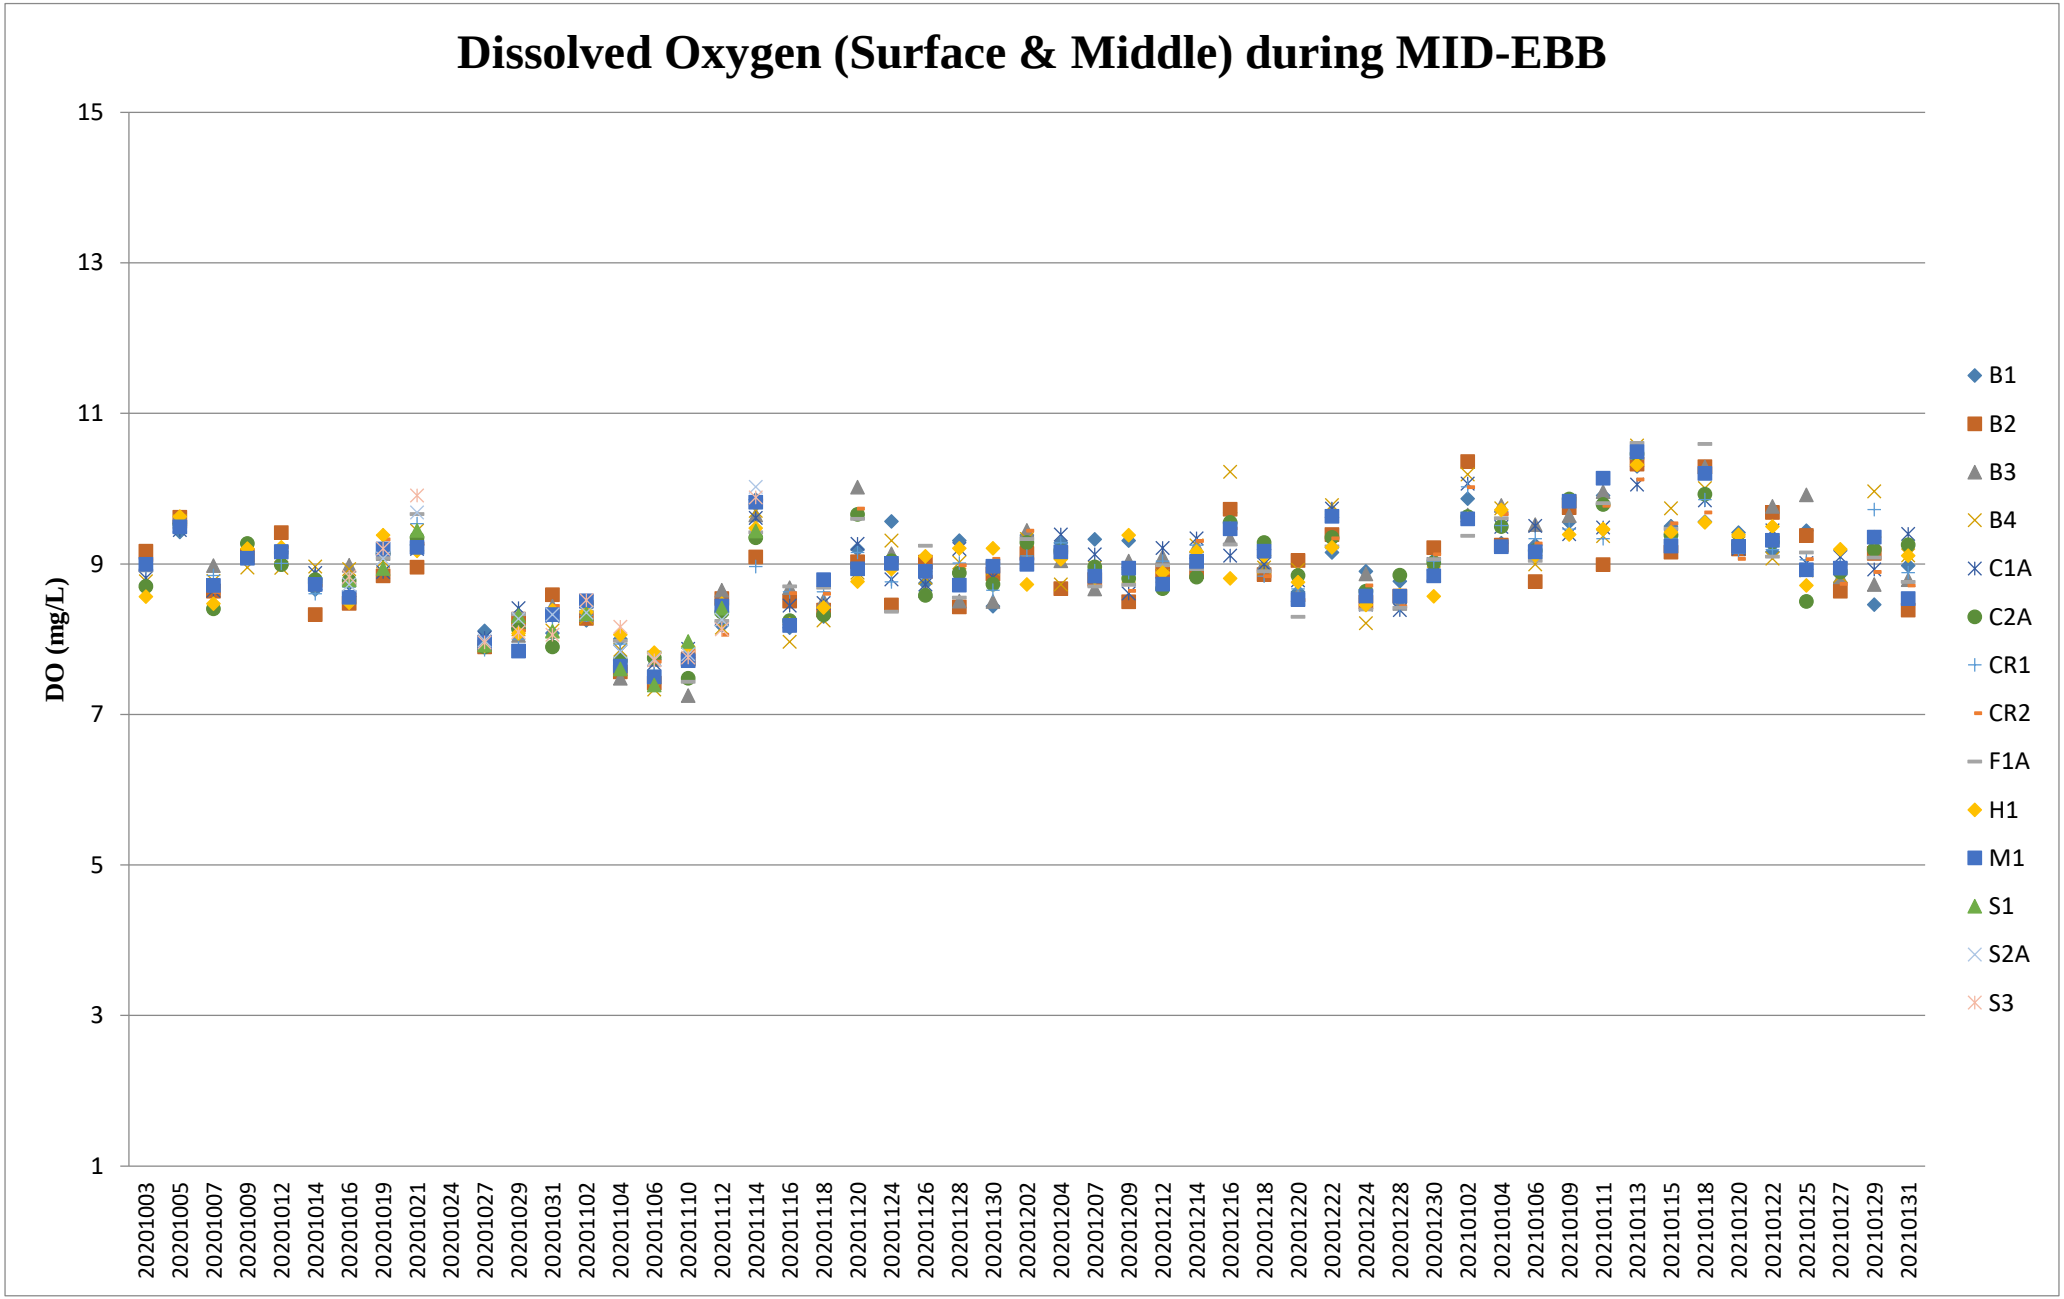

Note: The Action and Limit Level of dissolved oxygen can be referred to **Table 2.7** of the monthly EM&A report.

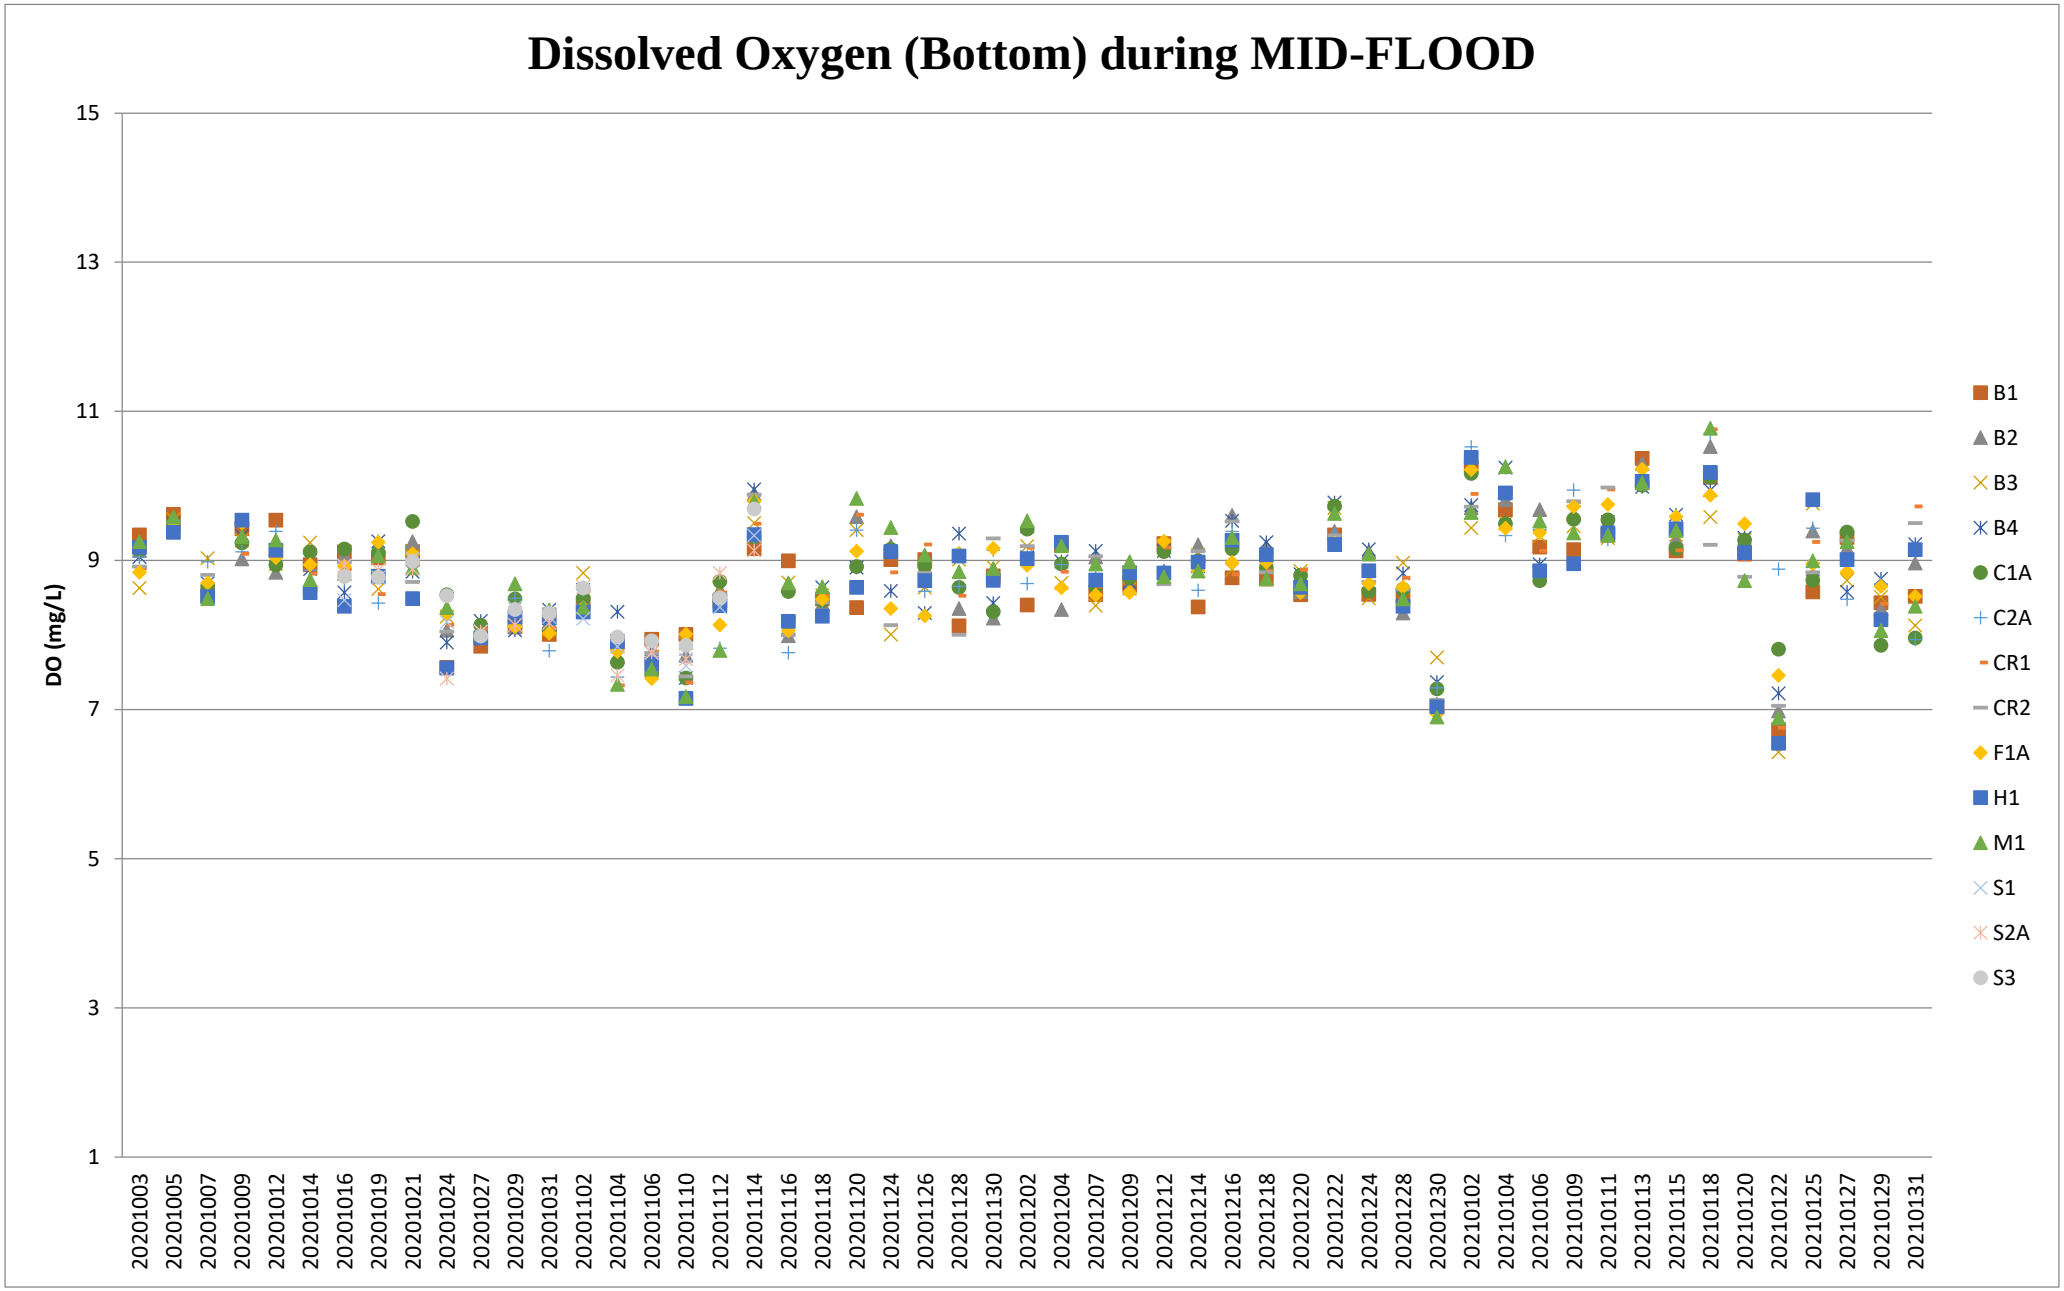



Note: The Action and Limit Level of dissolved oxygen can be referred to **Table 2.7** of the monthly EM&A report.

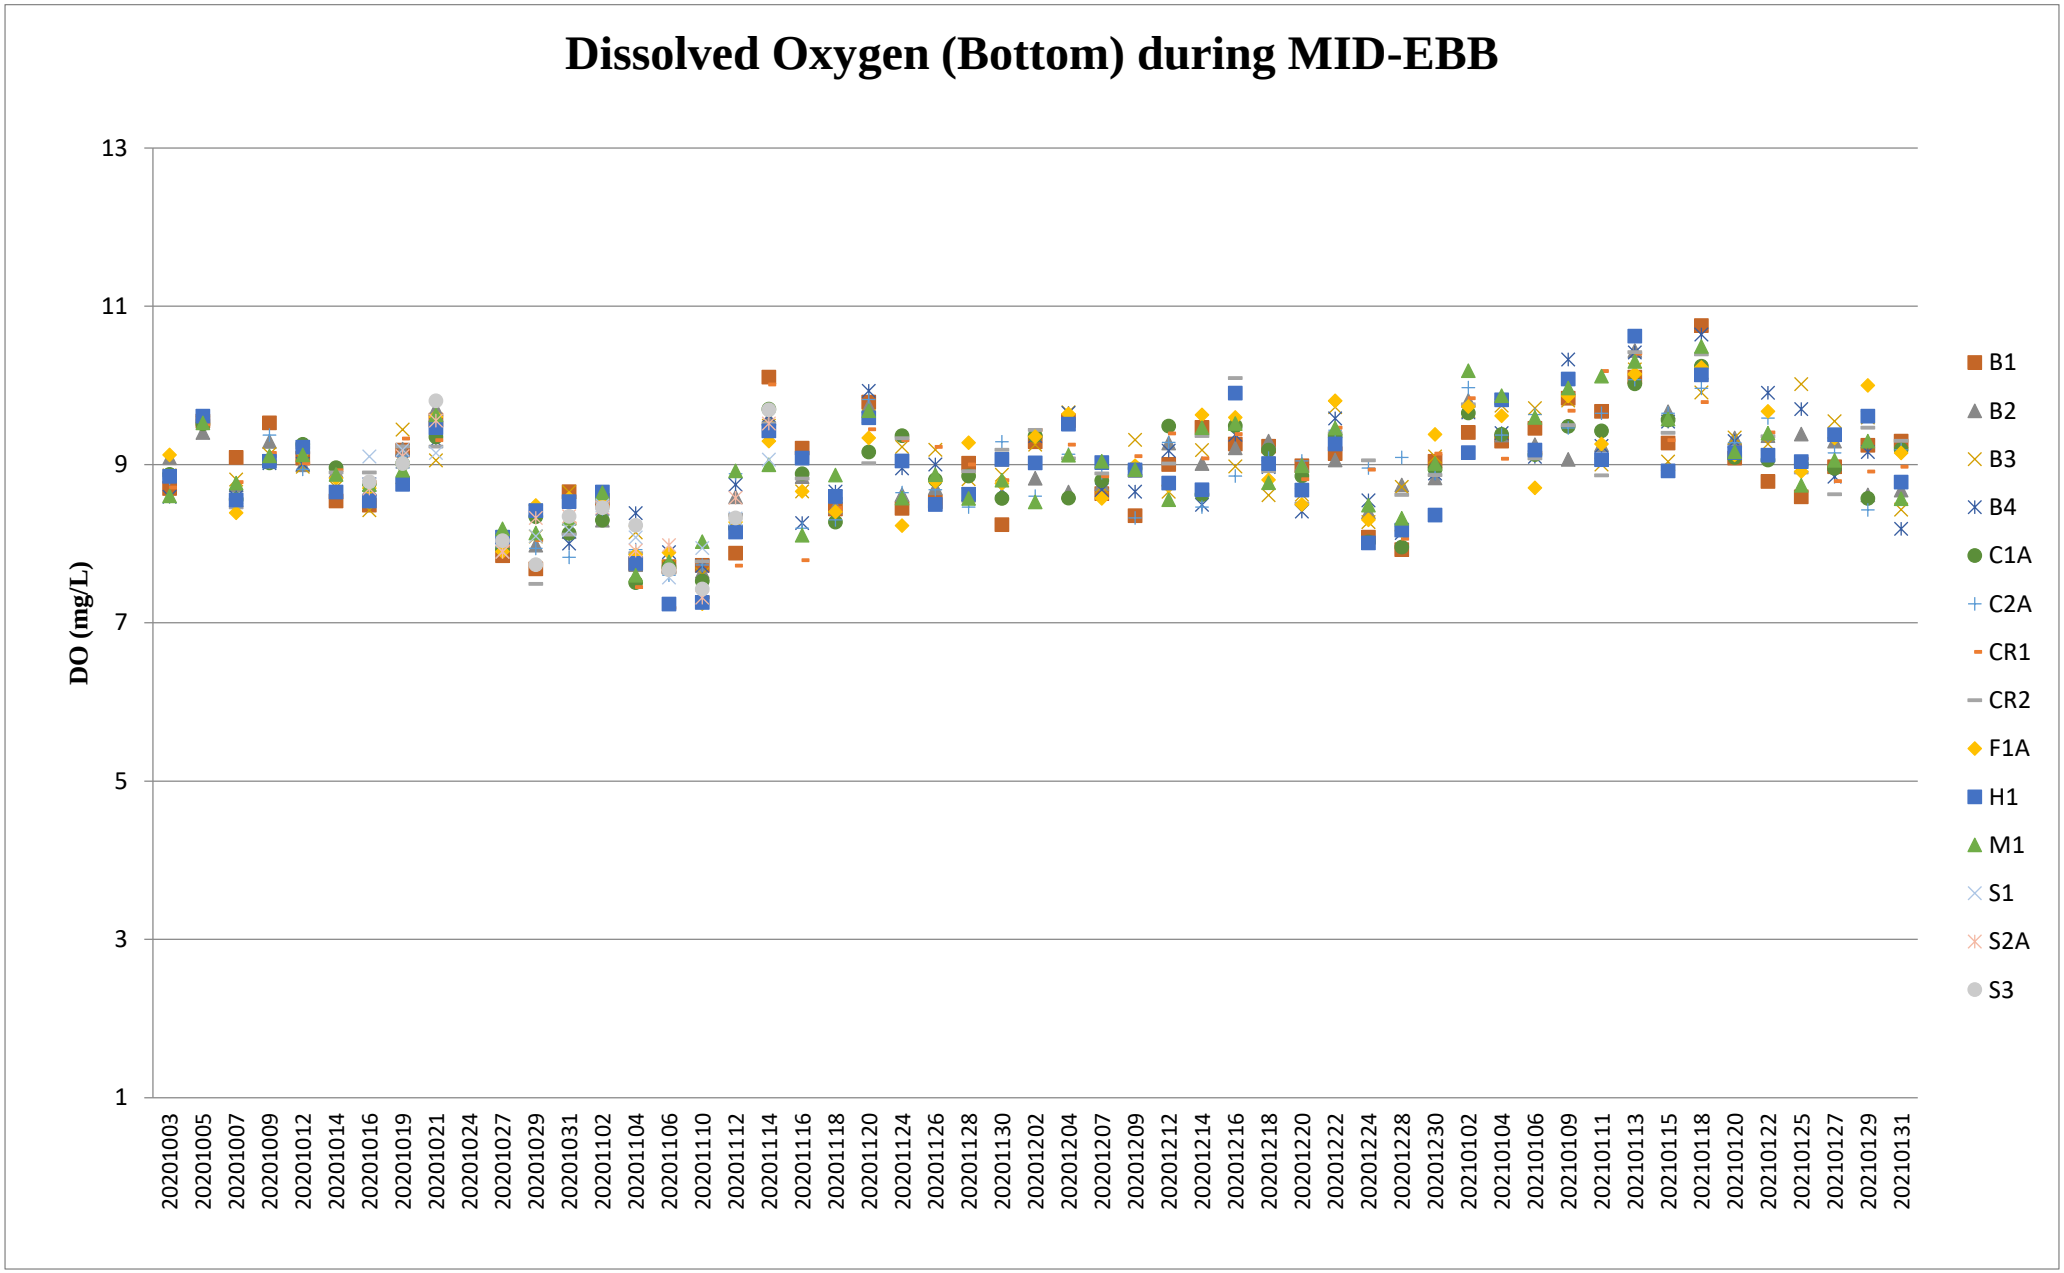


Note: The Action and Limit Level of dissolved oxygen can be referred to **Table 2.7** of the monthly EM&A report.


pH (Depth-averaged) during MID-FLOOD

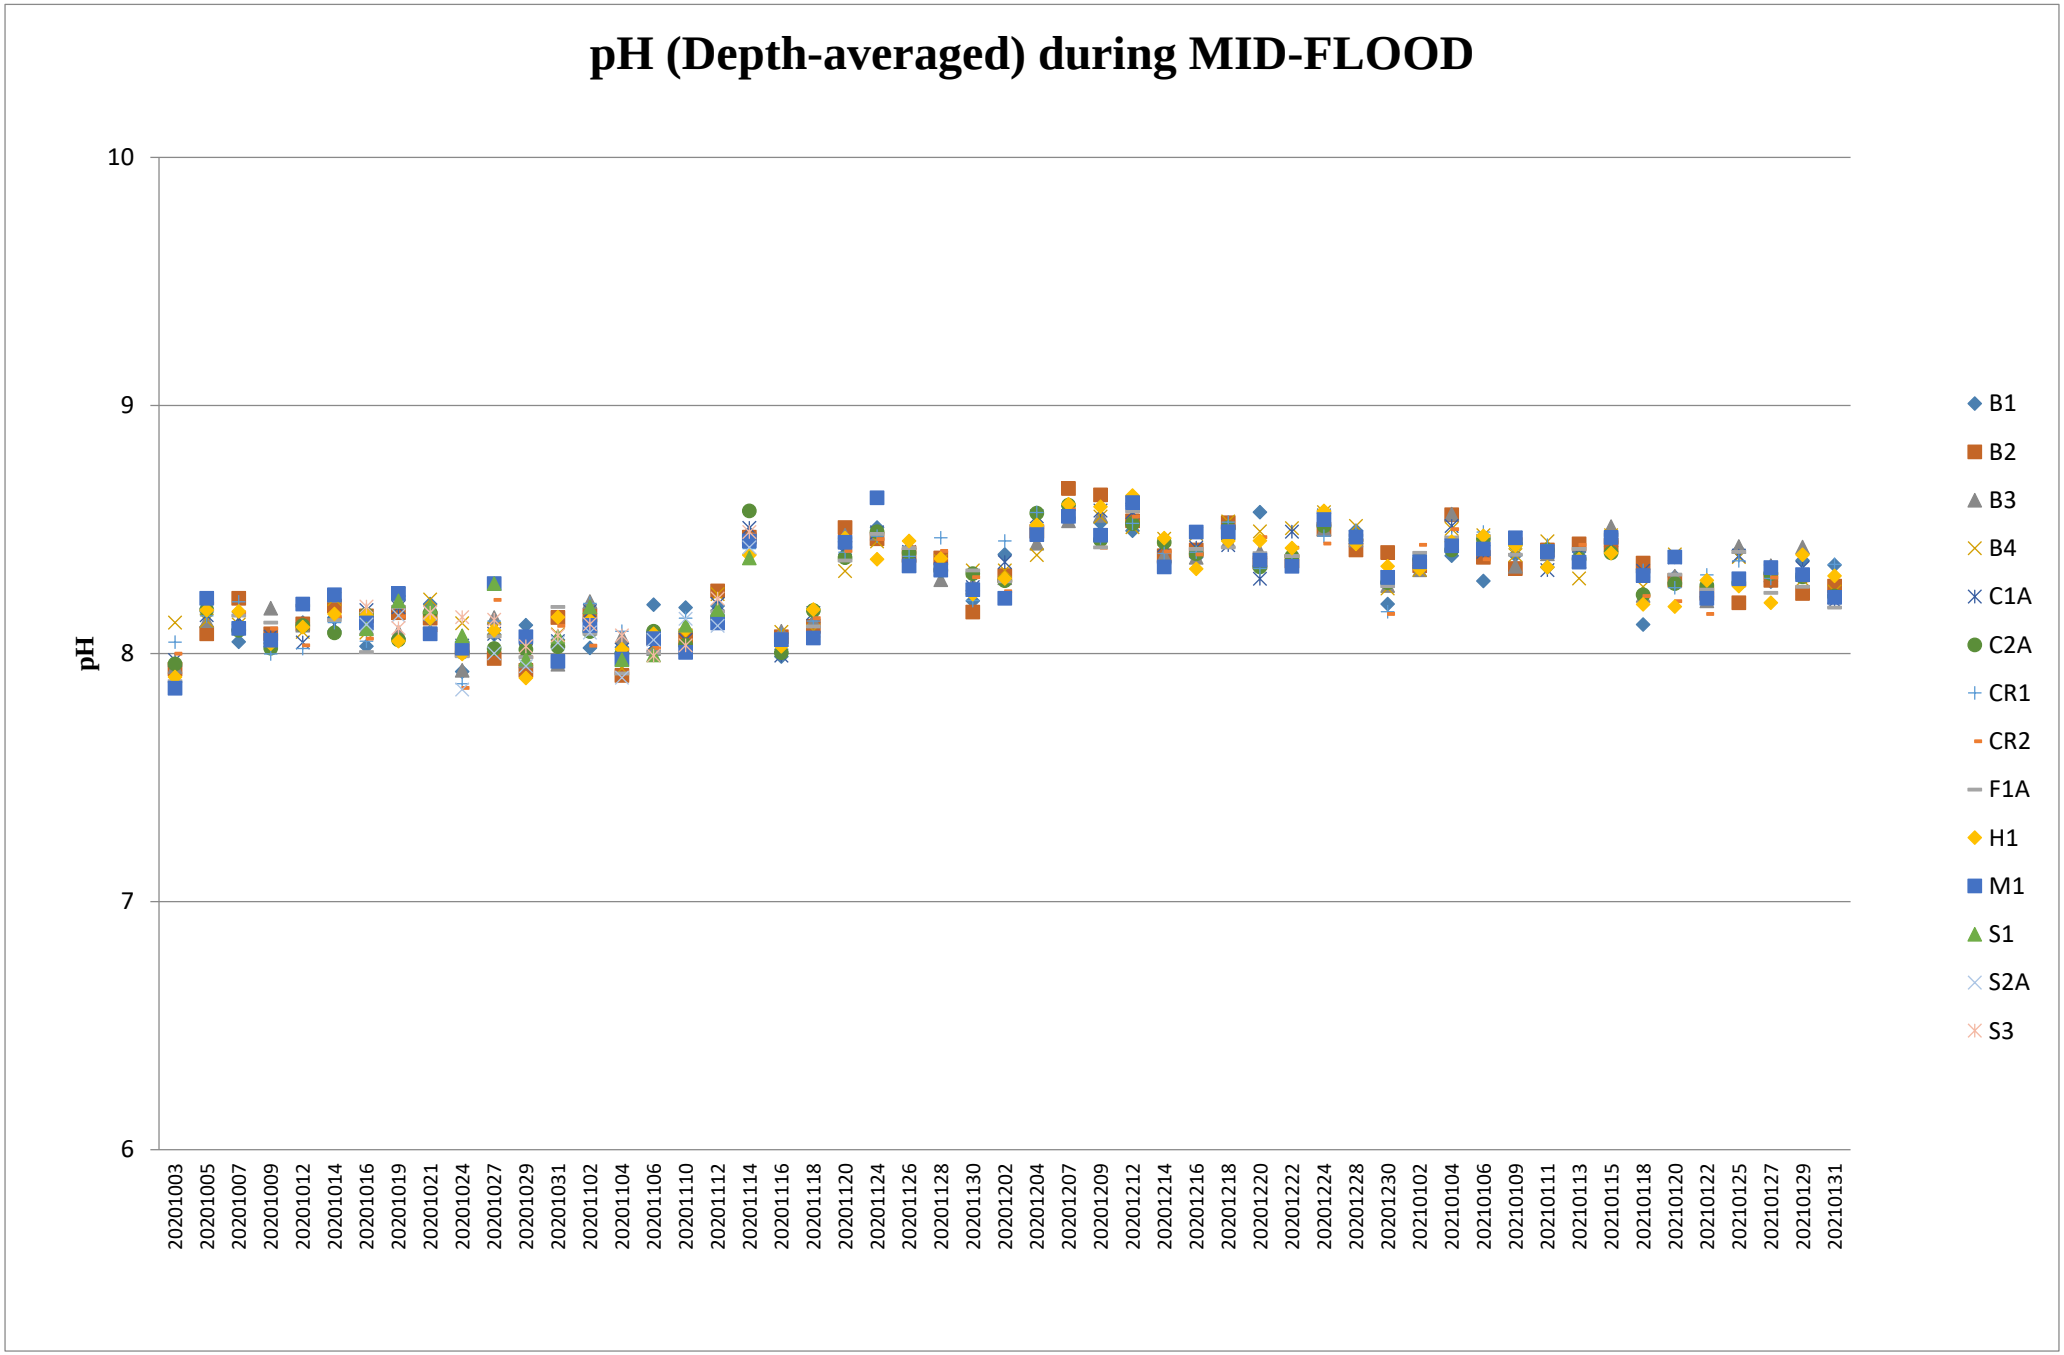

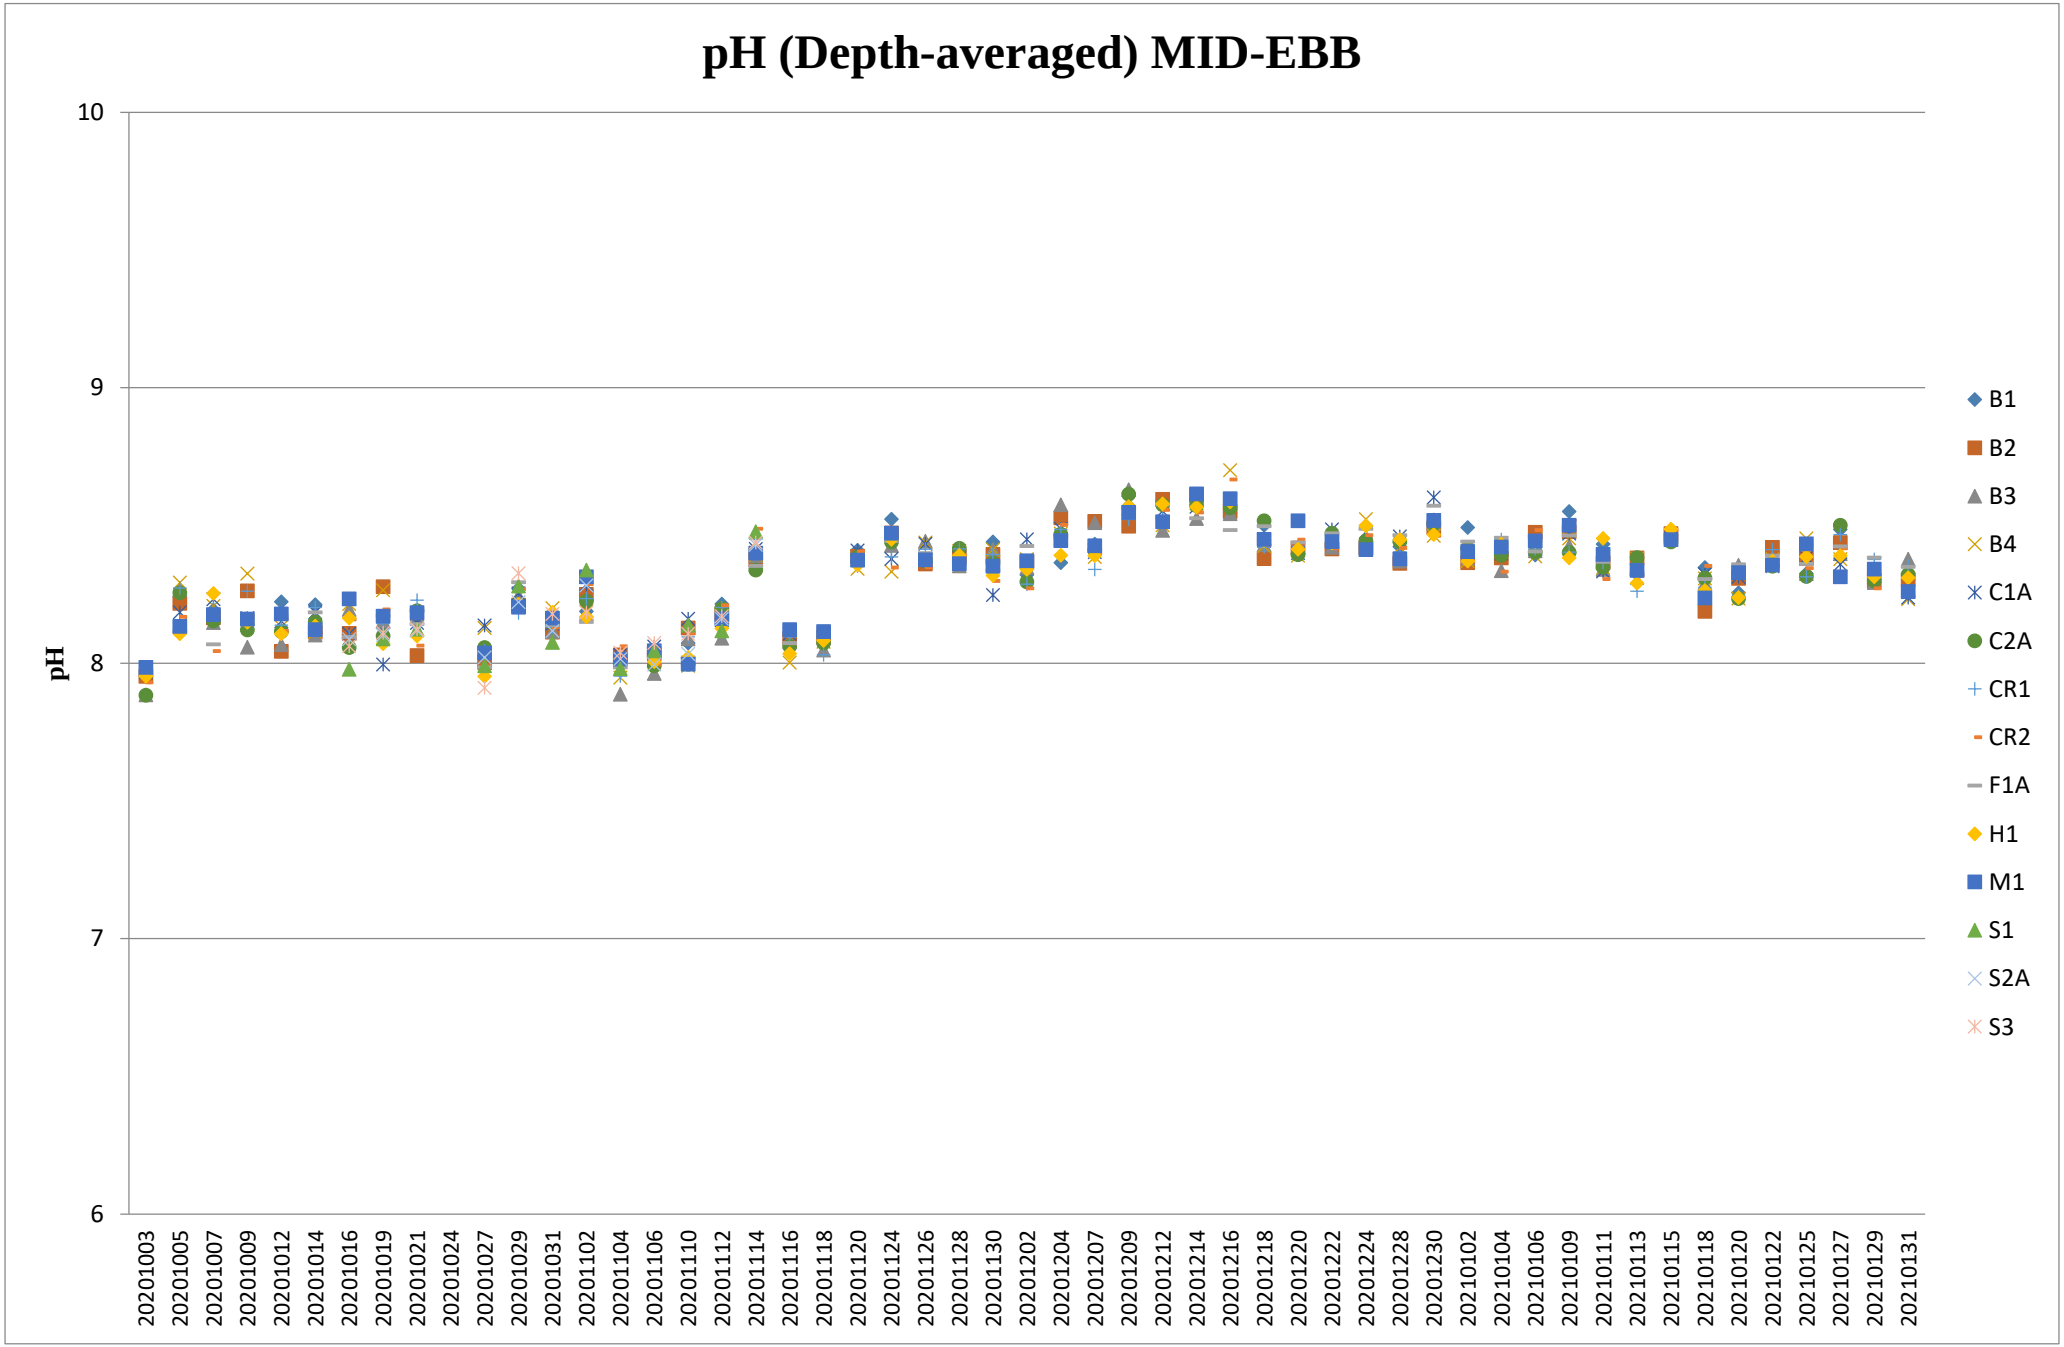

pH (Depth-averaged) MID-EBB
pH
10
9
8
7
6
20201003
20201005
20201007
20201009
20201012
20201014
20201016
20201019
20201021
20201024
20201027
20201029
20201031
20201102
20201104
20201106
20201110
20201112
20201114
20201116
20201118
20201120
20201124
20201126
20201128
20201130
20201202
20201204
20201207
20201209
20201212
20201214
20201216
20201218
20201220
20201222
20201224
20201228
20201230
20210102
20210104
20210106
20210109
20210111
20210113
20210115
20210118
20210120
20210122
20210125
20210127
20210129
20210131
B1
B2
B3
B4
C1A
C2A
CR1
CR2
F1A
H1
M1
S1
S2A
S3

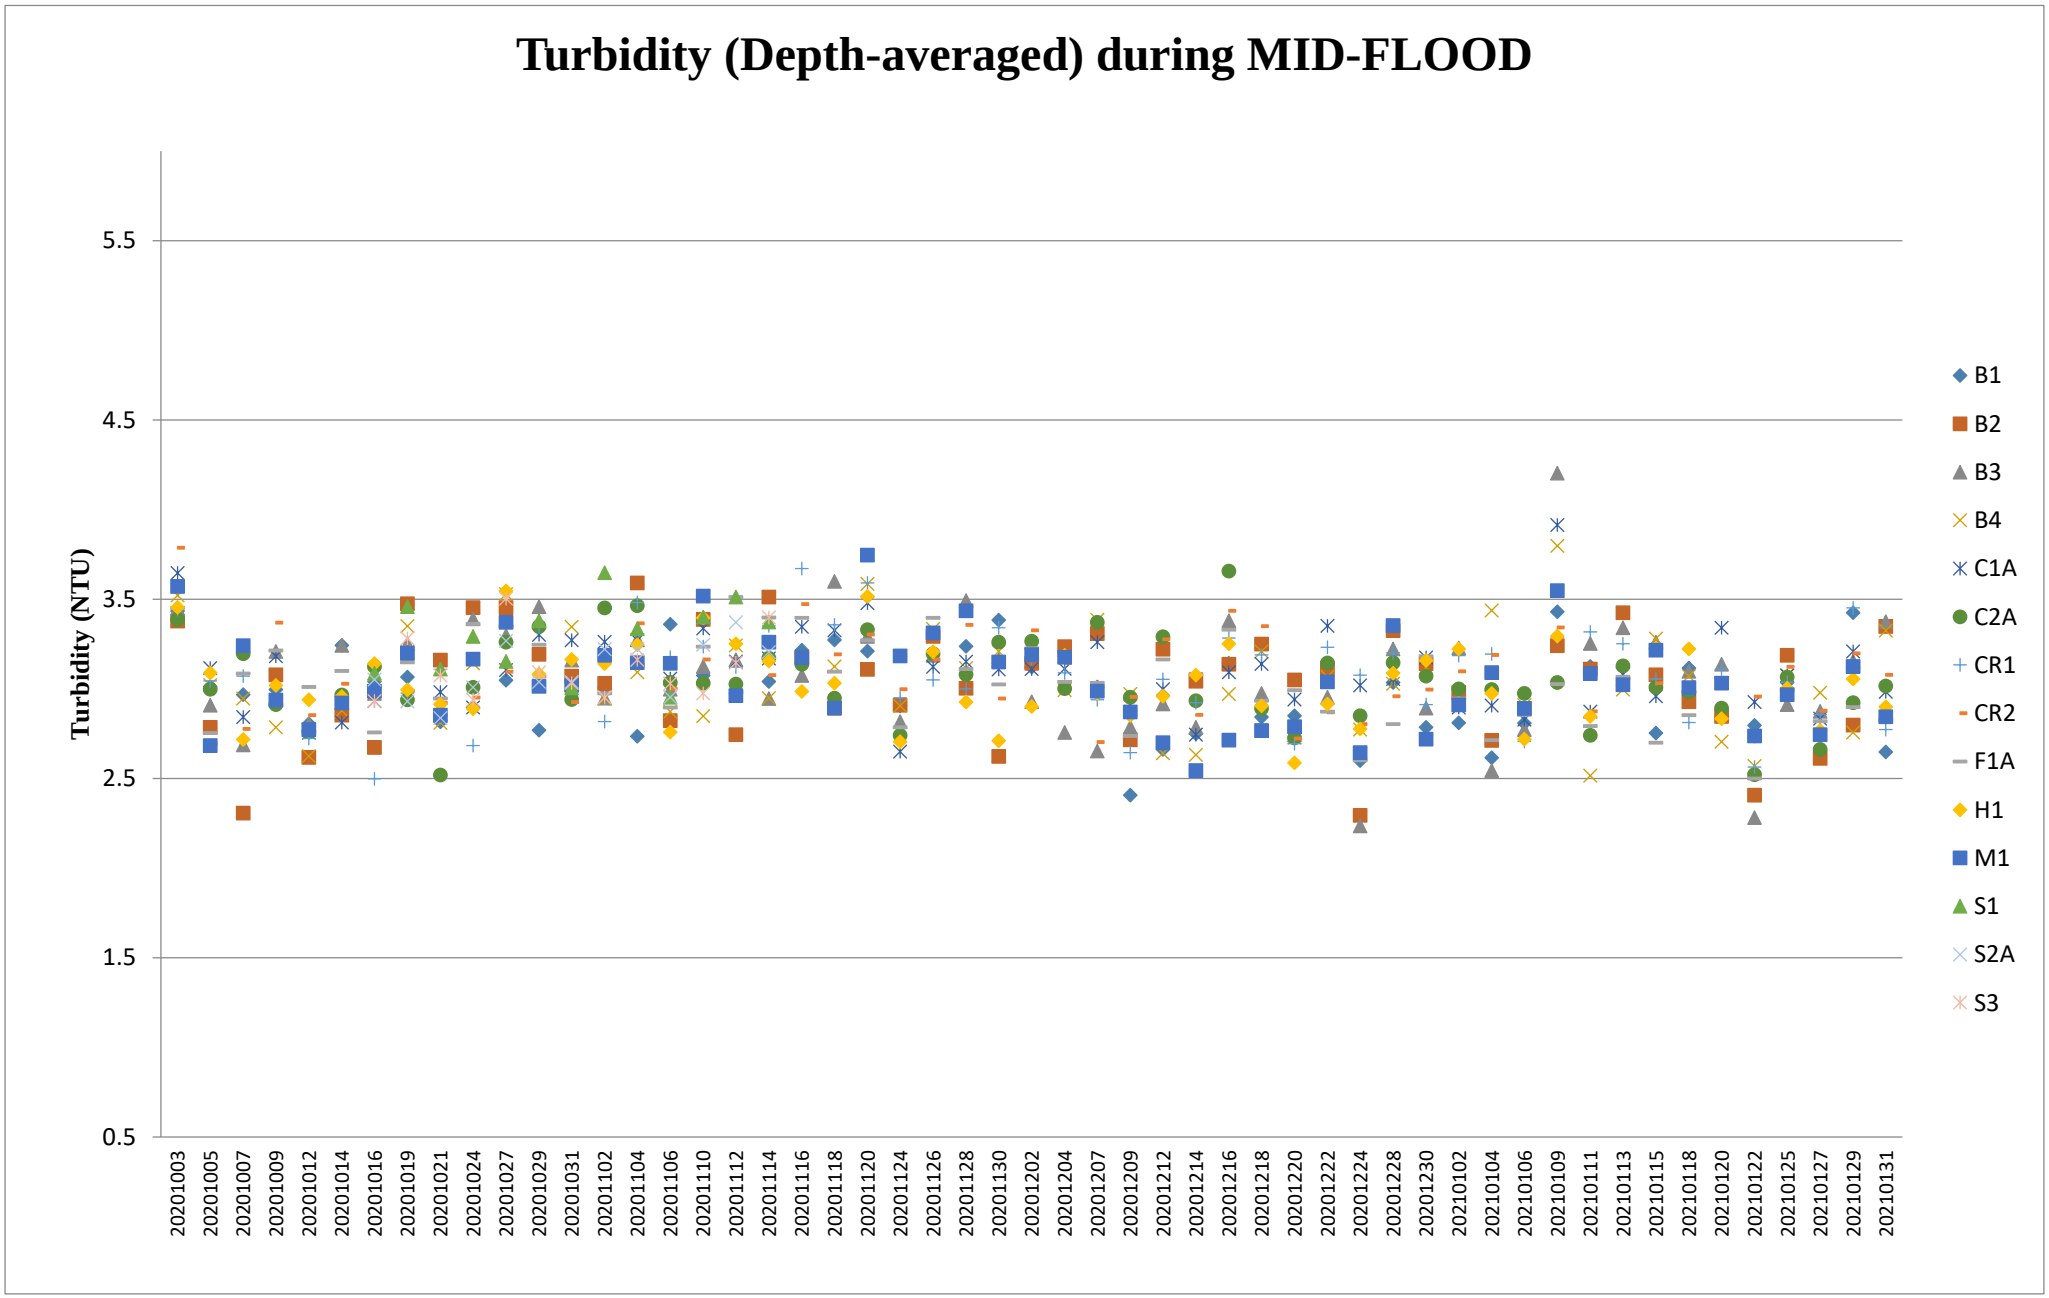


Note: The Action and Limit Level of turbidity can be referred to **Table 2.7** of the monthly EM&A report.

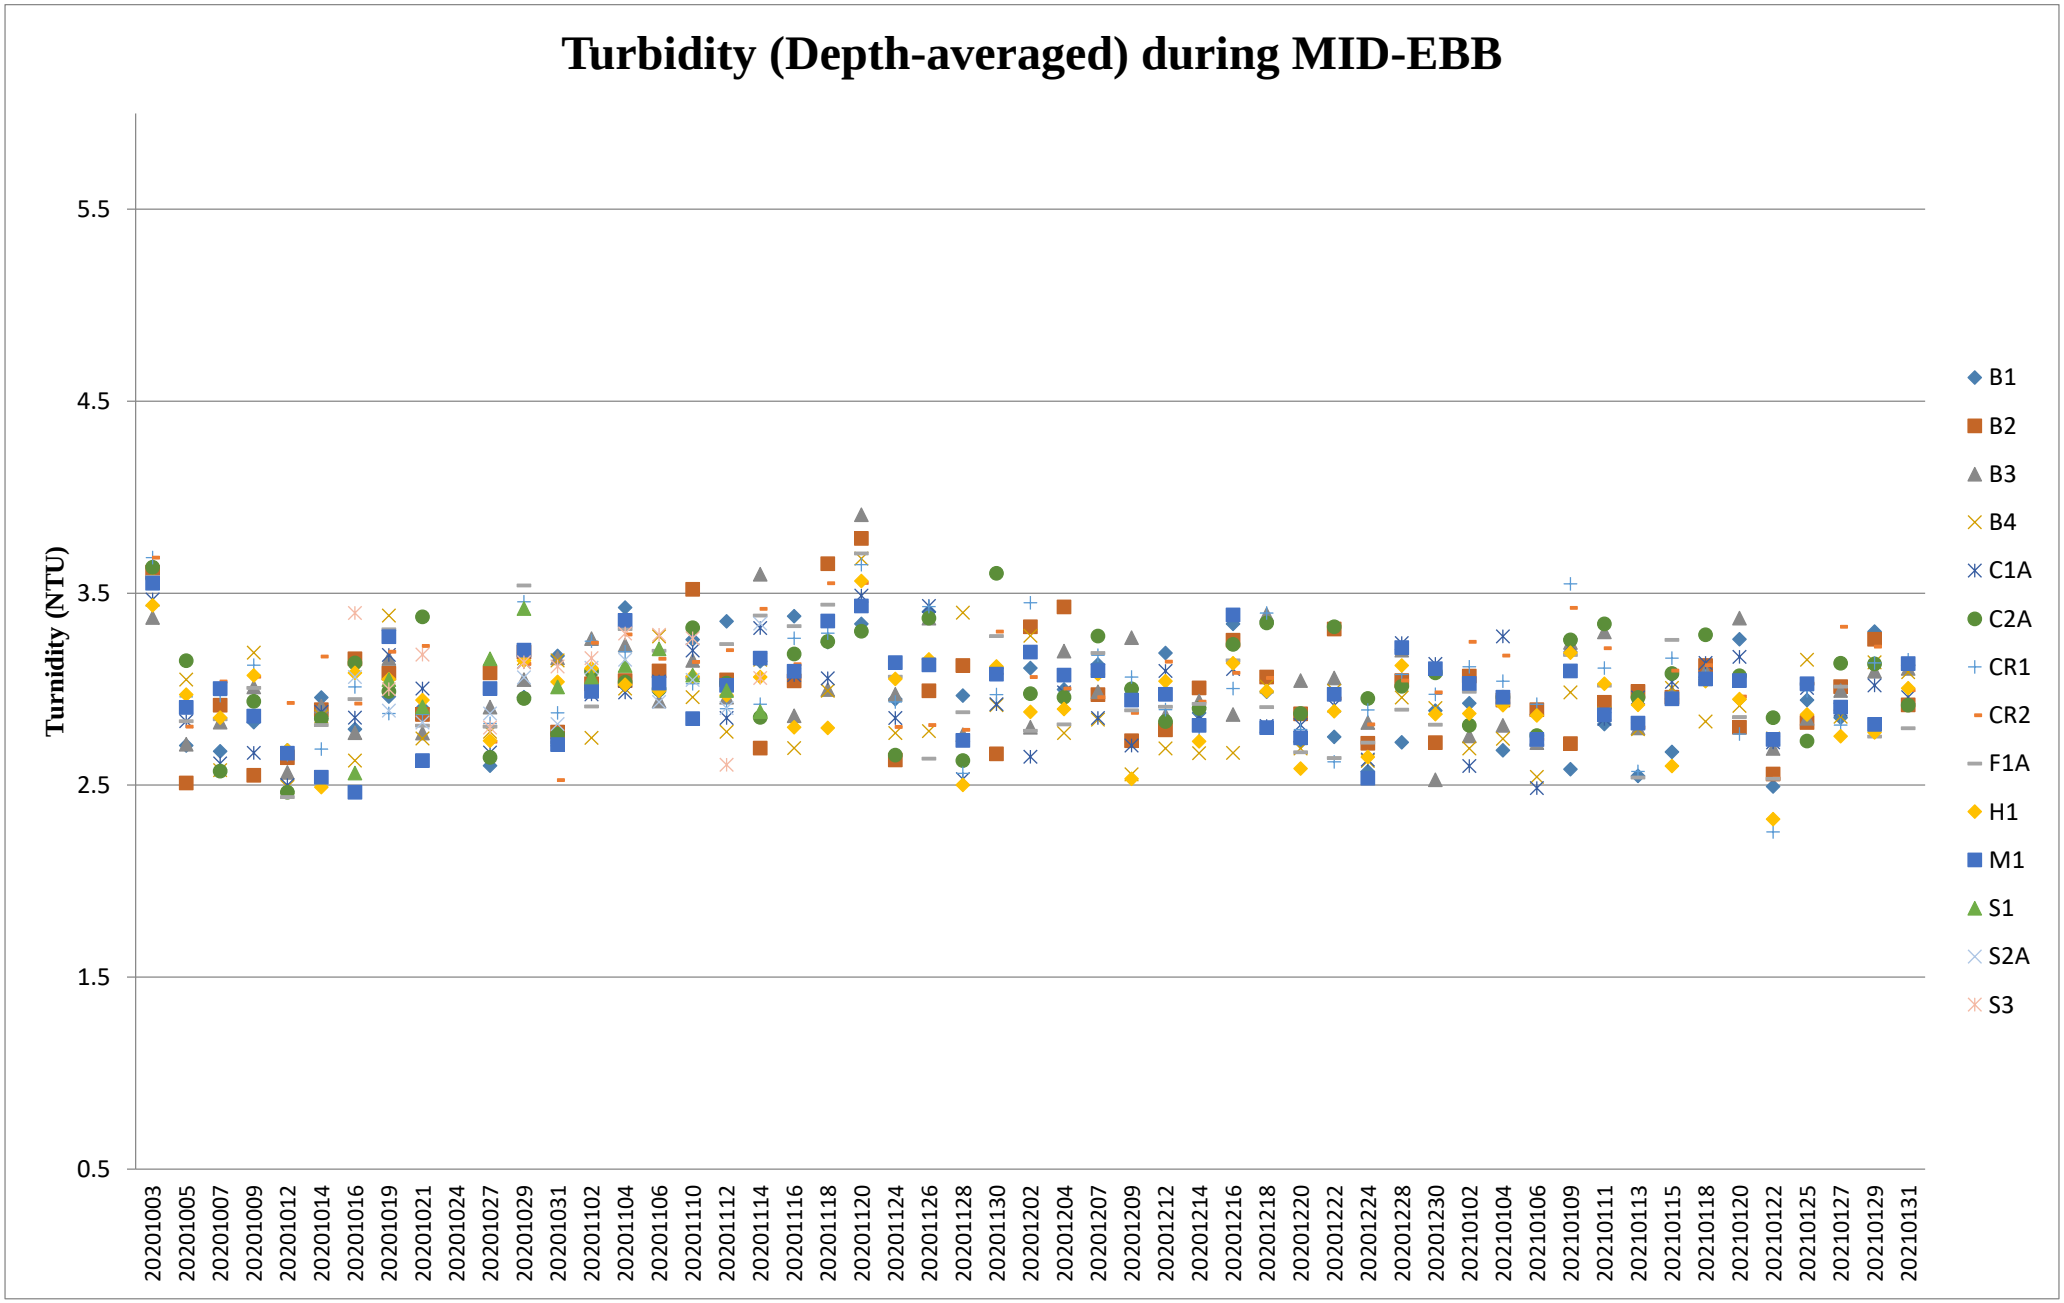


Note: The Action and Limit Level of turbidity can be referred to **Table 2.7** of the monthly EM&A report.

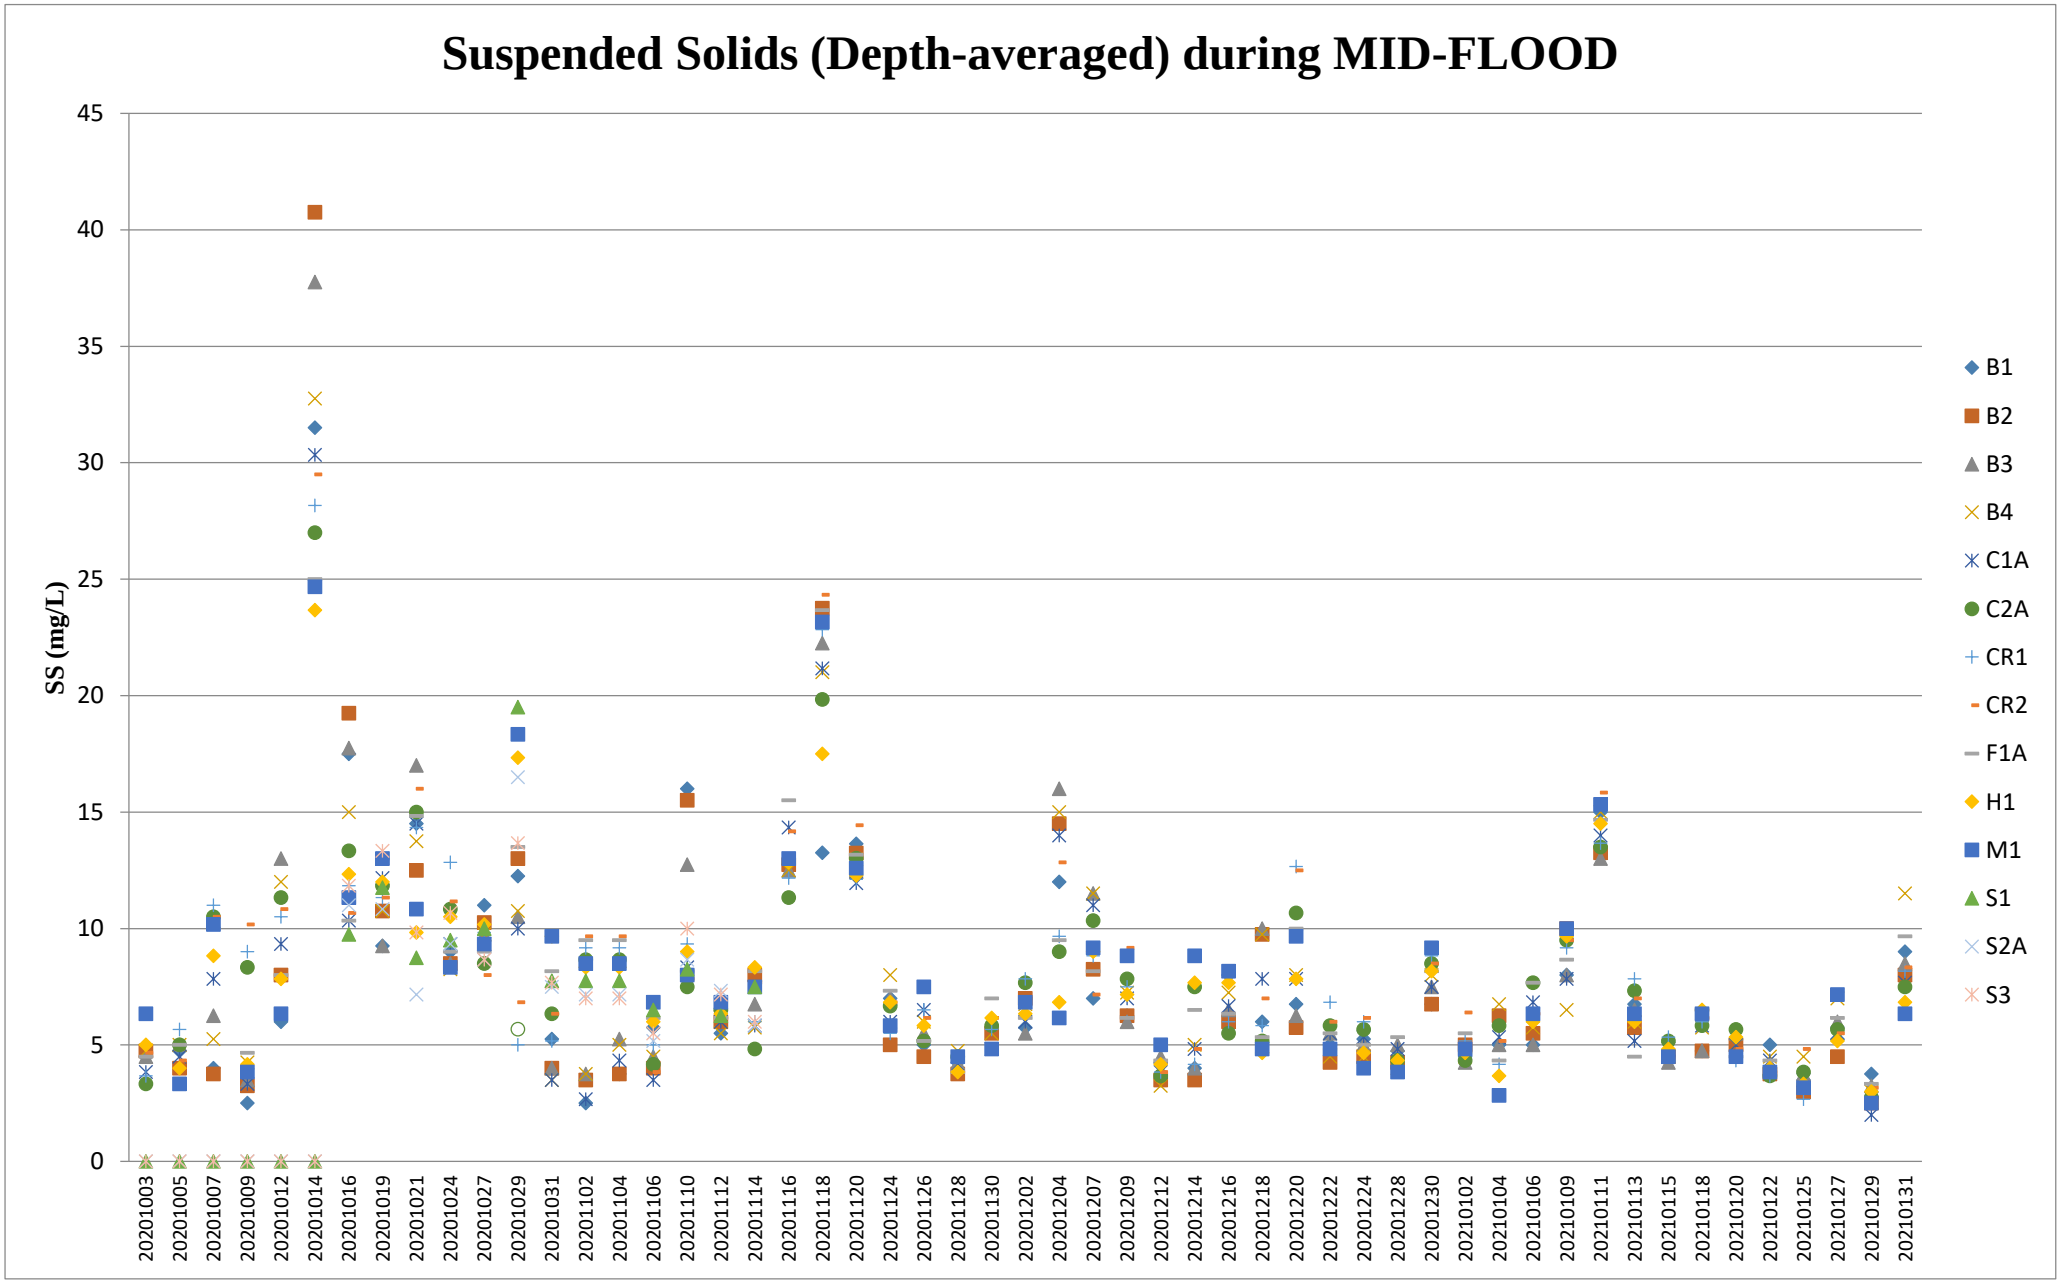


Note: The Action and Limit Level of suspended solids can be referred to **Table 2.7** of the monthly EM&A report.

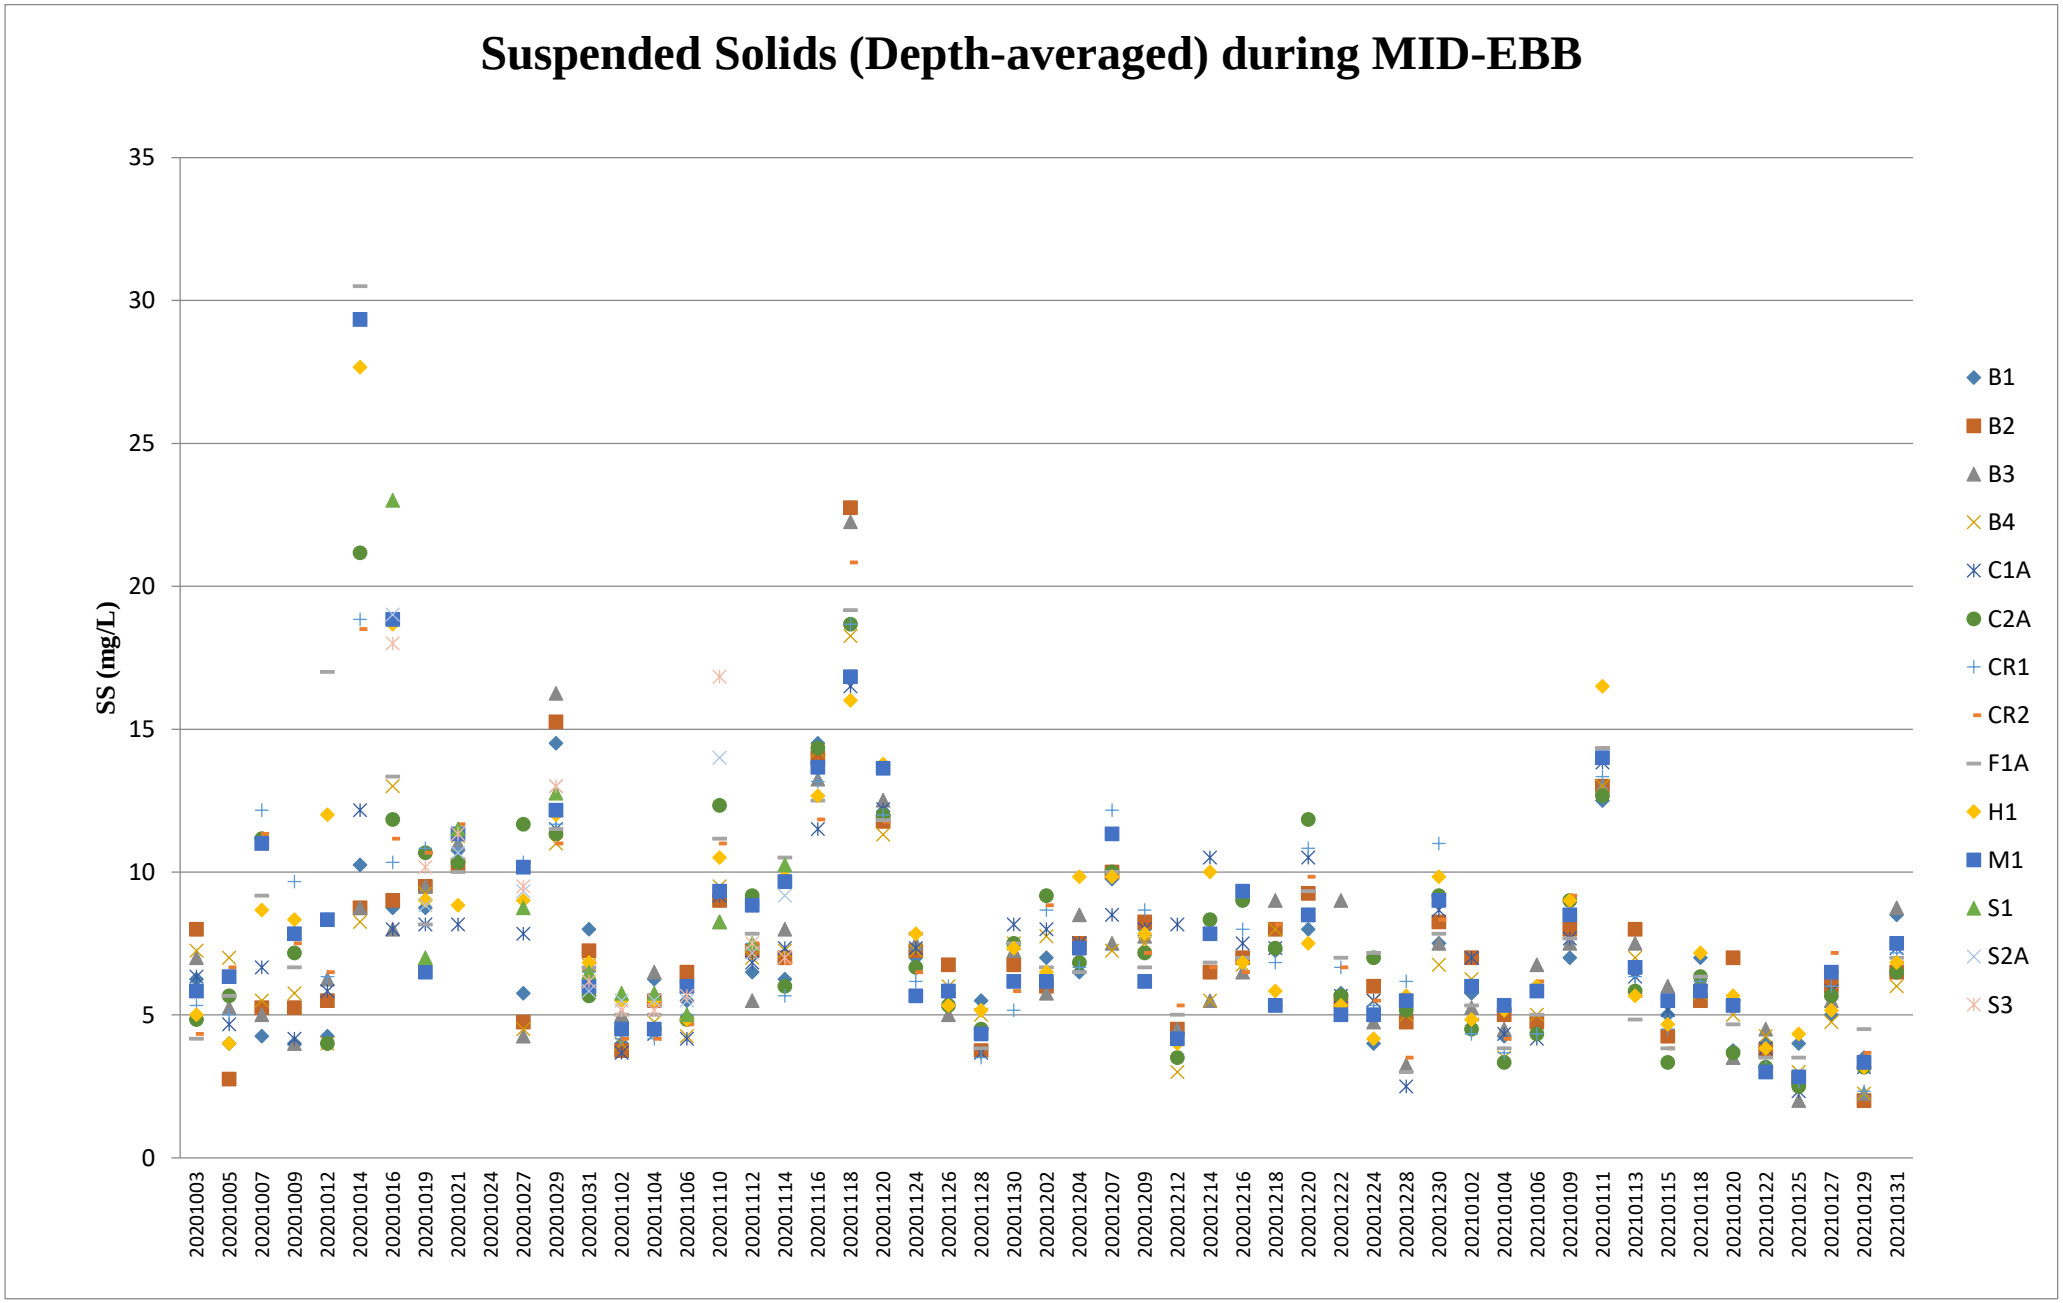

Note: The Action and Limit Level of suspended solids can be referred to **Table 2.7** of the monthly EM&A report.

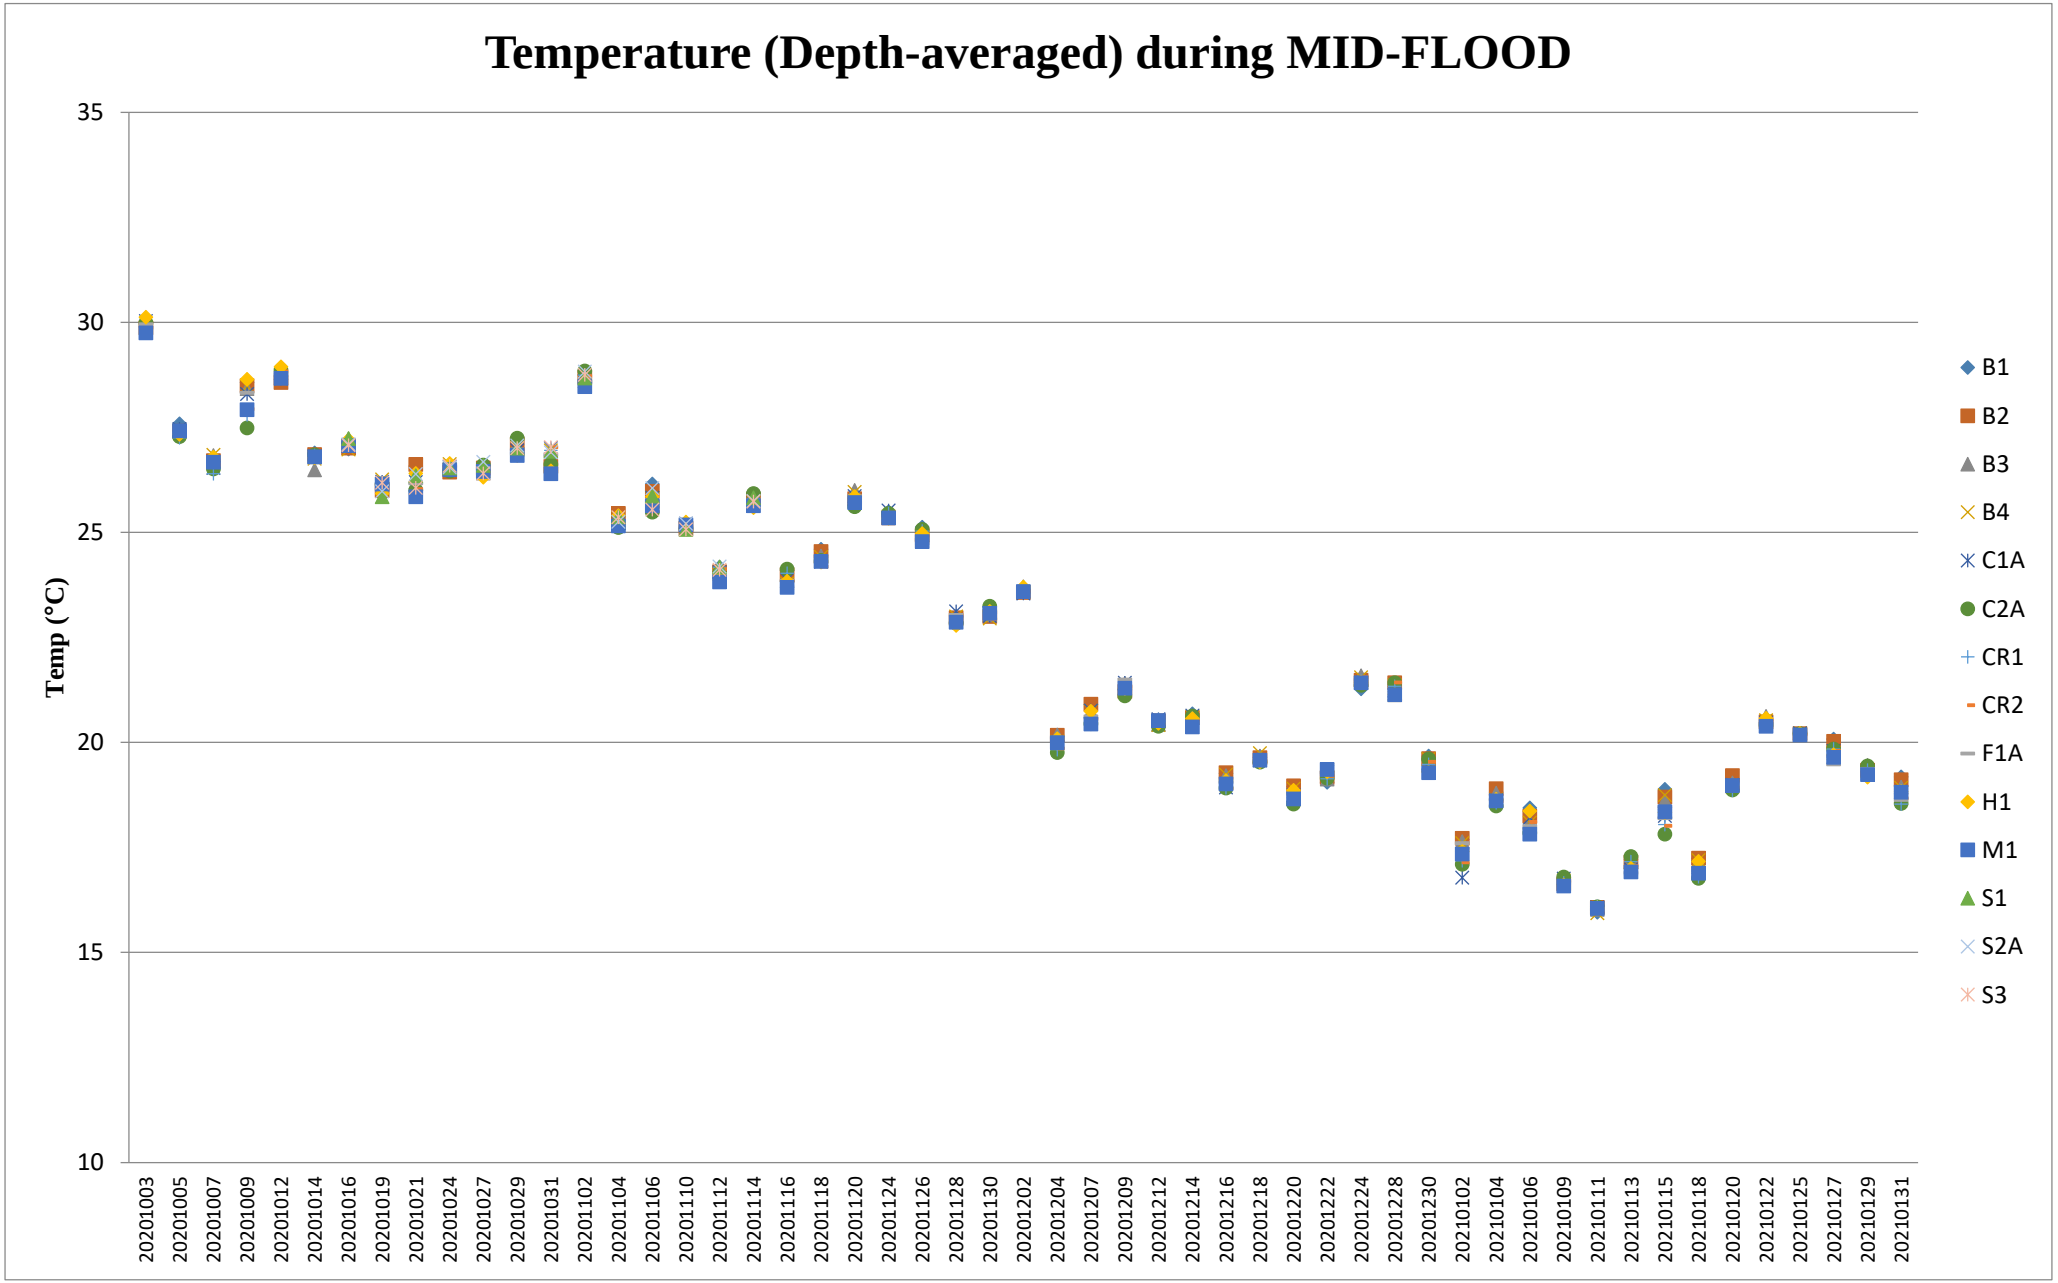

Note: The Action and Limit Level of temperature can be referred to **Table 2.7** of the monthly EM&A report.

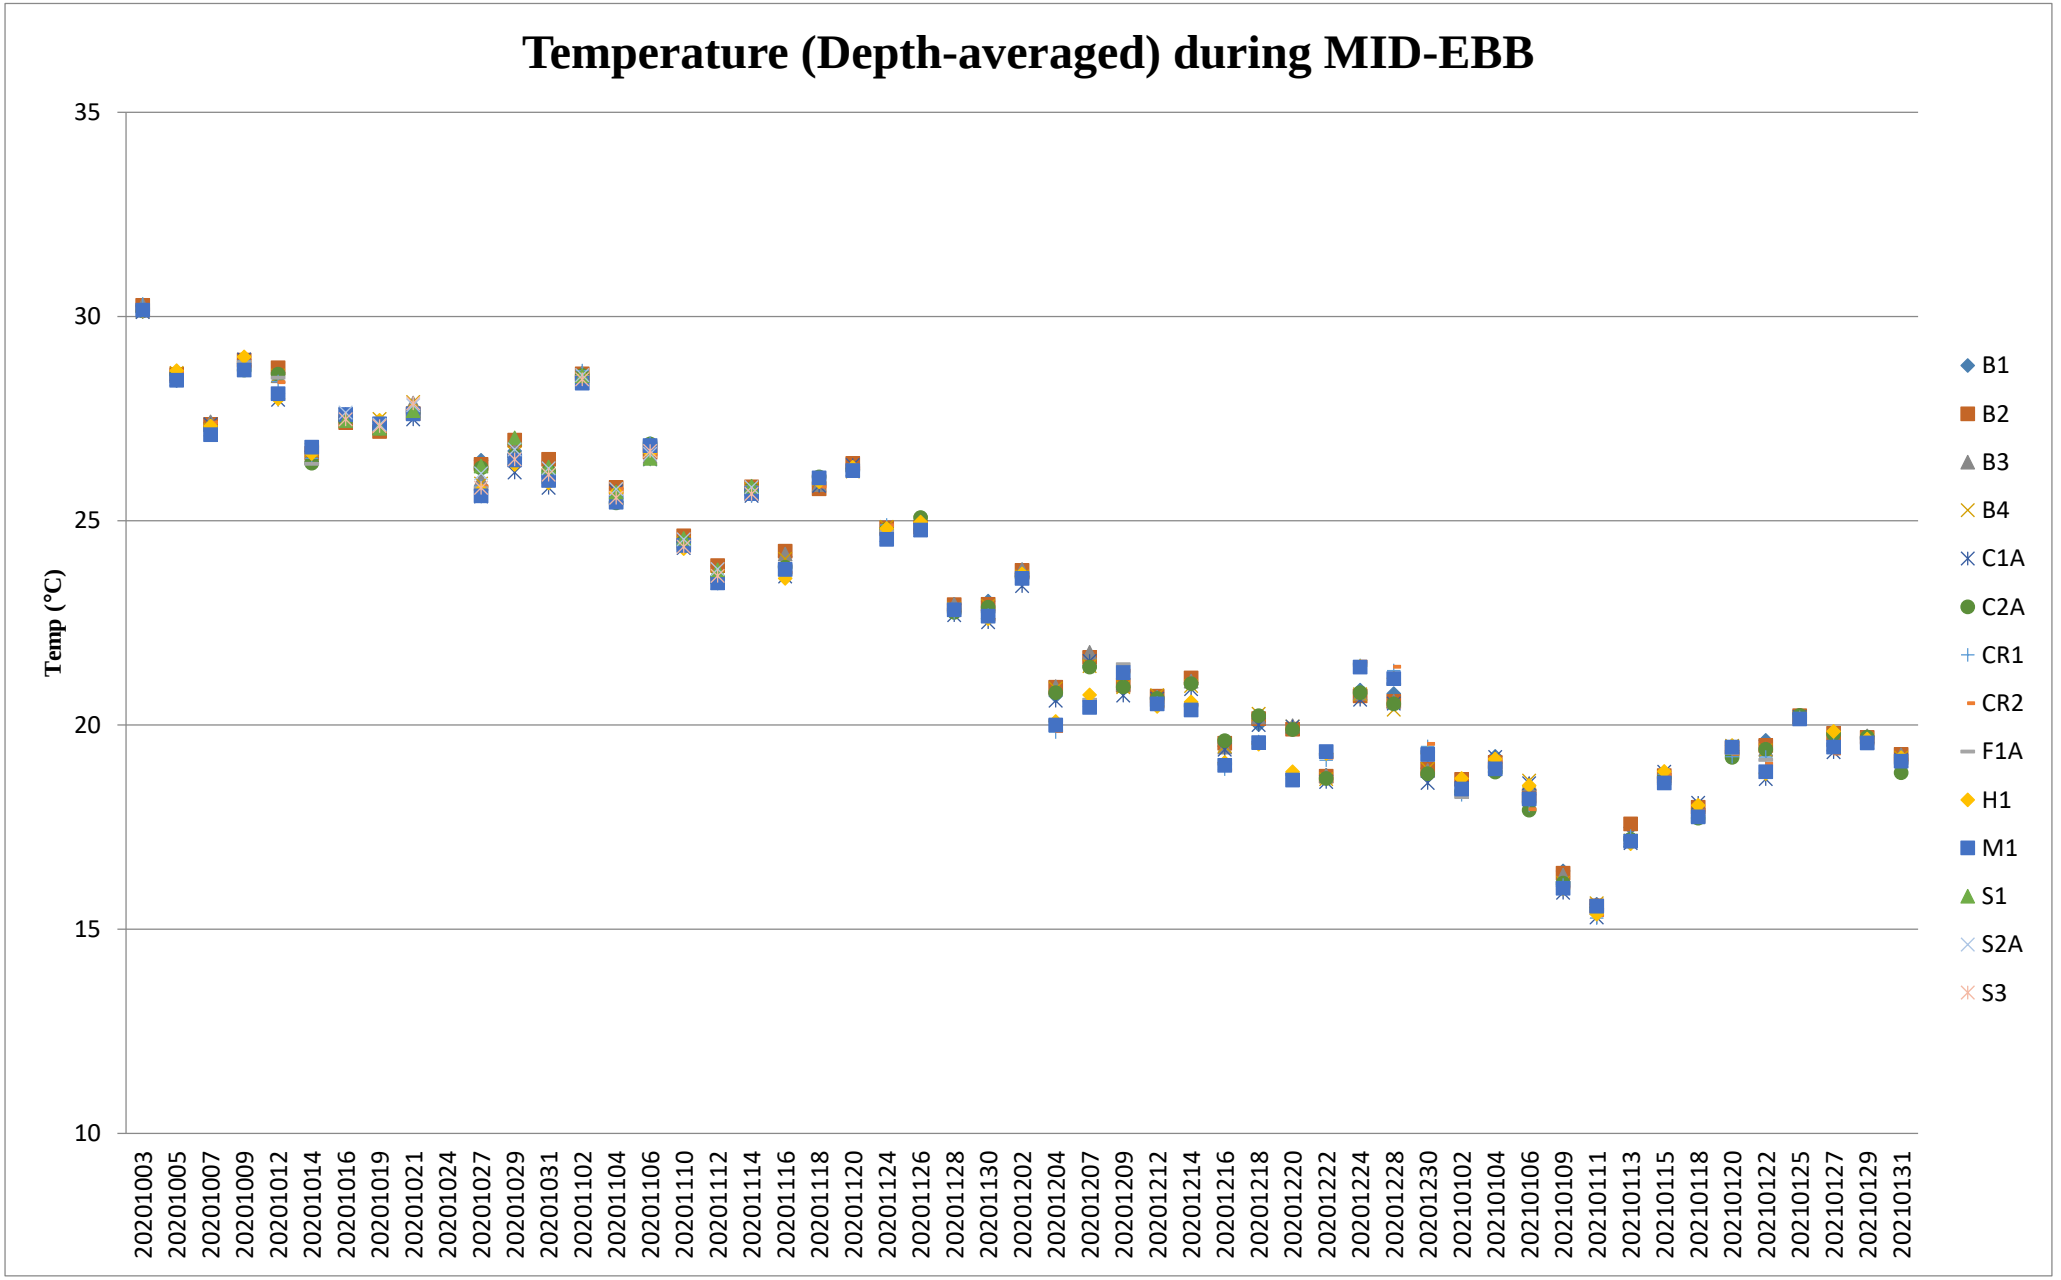

Note: The Action and Limit Level of temperature can be referred to **Table 2.7** of the monthly EM&A report.

Appendix E HOKLAS Laboratory Certificate

Hong Kong Accreditation Service
香港認可處

Certificate of Accreditation
認可證書

This is to certify that
特此證明

ALS TECHNICHEM (HK) PTY LIMITED

11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, New Territories, Hong Kong
香港新界葵涌永業街1-3號忠信針織中心11樓

has been accepted by the HKAS Executive, on the recommendation of the Accreditation Advisory Board, as a
為香港認可處執行機關根據認可諮詢委員會建議而接受的

HOKLAS Accredited Laboratory
「香港實驗所認可計劃」認可實驗所

This laboratory meets the requirements of ISO / IEC 17025 : 2005 – General requirements for the competence
此實驗所符合ISO / IEC 17025 : 2005 –《測試及校正實驗所能力的通用規定》所訂的要求，
of testing and calibration laboratories and it has been accredited for performing specific tests or calibrations as
獲認可進行載於香港實驗所認可計劃《認可實驗所名冊》內下述測試類別中的指定
listed in the HOKLAS Directory of Accredited Laboratories within the test category of
測試或校正工作

Environmental Testing
環境測試

This laboratory is accredited in accordance with the recognised international Standard ISO / IEC 17025 : 2005.
本實驗所乃根據公認的國際標準 ISO / IEC 17025 : 2005 獲得認可。
This accreditation demonstrates technical competence for a defined scope and the operation of a laboratory
這項認可資格顯示在指定範疇所需的技術能力及實驗所質量管理體系的運作
quality management system (see joint IAF-ILAC-ISO Communiqué).
(見國際認可論壇、國際實驗所認可合作組織及國際標準化組織的聯合公報)。

The common seal of the Hong Kong Accreditation Service is affixed hereto by the authority of the HKAS Executive
香港認可處根據認可處執行機關的權限在此蓋上通用印章

CHAN Sing Sing, Terence, Executive Administrator
執行幹事 陳成城
Issue Date : 5 May 2009
簽發日期：二零零九年五月五日

Registration Number : HOKLAS 066
註冊號碼：

Date of First Registration : 15 September 1995
首次註冊日期：一九九五年九月十五日

This certificate is issued subject to the terms and conditions laid down by HKAS
本證書按照香港認可處訂立的條款及條件發出

L 000552

Invalid if unsigned

Hong Kong Accreditation Service
香港認可處

Certificate of Accreditation
認可證書

This is to certify that
特此證明

ACUMEN LABORATORY AND TESTING LIMITED
浩科檢測中心有限公司

Lot 12, Tam Kon Shan Road, North Tsing Yi, New Territories, Hong Kong
香港新界青衣北担杆山路12路段

has been accepted by the HKAS Executive, on the recommendation of the Accreditation Advisory Board, as a
在認可諮詢委員會的建議下獲香港認可處執行機關接受為

HOKLAS Accredited Laboratory
「香港實驗所認可計劃」認可實驗所

This laboratory meets the requirements of ISO/IEC 17025:2005 and it has been accredited for performing specific tests or calibrations as listed in the scope of accreditation within the test category of

Environmental Testing

此實驗所符合ISO/IEC 17025:2005所訂的要求
並獲認可進行載於認可範圍內下述測試類別中的指定測試或校正工作

環境測試

This accreditation to ISO/IEC 17025:2005 demonstrates technical competence for a defined scope and the operation of a laboratory quality management system (see joint IAF-ILAC-ISO Communiqué).
此項 ISO/IEC 17025:2005 的認可資格證明此實驗所具備指定範疇內所須的技術能力並實施一套實驗所質量管理體系(見國際認可論壇、國際實驗所認可合作組織及國際標準化組織的聯合公報)。

The common seal of the Hong Kong Accreditation Service is affixed hereto by the authority of the HKAS Executive
現經香港認可處執行機關授權在此蓋上香港認可處的印章

WONG Wang-wah, Executive Administrator
執行幹事 黃宏華
Issue Date : 16 July 2014
簽發日期：二零一四年七月十六日

Registration Number : HOKLAS 241
註冊號碼：

Date of First Registration : 16 July 2014
首次註冊日期：二零一四年七月十六日

This certificate is issued subject to the terms and conditions laid down by HKAS
本證書按照香港認可處訂立的條款及條件發出

L 001195

Invalid if not printed

Appendix F Water Quality Equipment Calibration Certificate

專業化驗有限公司
QUALITY PRO TEST-CONSULT LIMITED
Unit 10, 14/F, Wah Wai Centre, 38-40 Au Pui Wan St., Fotan, Hong Kong
Email: info@qualityprotest.com; Website: www.qualityprotest.com
Tel: (852) 3956 8717; Fax: (852) 3956 3928

REPORT OF EQUIPMENT PERFORMANCE CHECK/ CALIBRATION

Report No. : AJ110068
Date of Issue : 27 November 2020

PART A – CUSTOMER INFORMATION

Acuity Sustainability Consulting Limited
Unit C, 11/F, Ford Glory Plaza
37-39 Wing Hong Street
Cheung Sha Wan, Kowloon, Hong Kong
Attn: Mr. Nelson TSUI

PART B – DESCRIPTION

Name of Equipment	:	Multi Water Quality Checker U-53
Manufacturer	:	Horiba
Serial Number	:	A55XB7UP
Date of Received	:	Nov 16, 2020
Date of Calibration	:	Nov 27, 2020
Date of Next Calibration[a]	:	Feb 26, 2021

PART C – REFERENCE METHODS/ DOCUMENTS FOR THE CALIBRATION

Parameter	Reference Method
pH at 25°C	APHA 21e 4500-H^+ B
Dissolved Oxygen	APHA 21e 4500-O G
Salinity	APHA 21e 2520 B
Turbidity	APHA 21e 2130 B
Temperature	Section 6 of international Accreditation New Zealand Technical Guide no. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

PART D – CALIBRATION RESULTS[b,c]

(1) pH at 25°C

Target (pH unit)	Displayed Reading[d] (pH Unit)	Tolerance[e](pH Unit)	Results
4.00	4.18	0.18	Satisfactory
7.42	7.27	-0.15	Satisfactory
10.01	9.88	-0.13	Satisfactory

Tolerance of pH should be less than ±0.20 (pH unit)

(2) Temperature

Reading of Ref. thermometer (°C)	Displayed Reading (°C)	Tolerance (°C)	Results
15	15.4	0.40	Satisfactory
23	23.8	0.80	Satisfactory
35	34.6	-0.40	Satisfactory

Tolerance limit of temperature should be less than ±2.0 (°C)

~ CONTINUED ON NEXT PAGE ~

Remark(s): -

[a] *The "Date of Next Calibration" is recommended according to best practice principals as practiced by QPT or quoted form relevant international standards.*
[b] *The results relate only to the calibrated equipment as received*
[c] *The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.*
[d] *"Displayed Reading" denotes the figure shown on item under calibration/ checking regardless of equipment precision or significant figures.*
[e] *The "Tolerance Limit" mentioned is the acceptance criteria applicable for similar equipment used by Quality Pro Test-Consult Ltd. or quoted form relevant international standards.*

LEE Chun-ning, Desmond
Senior Chemist

This report shall not be reproduced unless with prior written approval from this laboratory.

專業化驗有限公司
QUALITY PRO TEST-CONSULT LIMITED
Unit 10, 14/F, Wah Wai Centre, 38-40 Au Pui Wan St., Fotan, Hong Kong
Email: info@qualityprotest.com; Website: www.qualityprotest.com
Tel: (852) 3956 8717; Fax: (852) 3956 3928

REPORT OF EQUIPMENT PERFORMANCE CHECK/ CALIBRATION

Report No. : AJ110068
Date of Issue : 27 November 2020

PART D – CALIBRATION RESULTS (Cont'd)

(3) Dissolved Oxygen

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)	Results
0.10	0.00	-0.10	Satisfactory
3.59	3.84	0.25	Satisfactory
5.01	4.99	-0.02	Satisfactory
7.83	7.57	-0.26	Satisfactory

Tolerance limit of dissolved oxygen should be less than ±0.50 (mg/L)

(4) Salinity

Expected Reading (g/L)	Displayed Reading (g/L)	Tolerance (%)	Results
10	9.95	-0.50	Satisfactory
20	19.02	-4.90	Satisfactory
30	29.03	-3.23	Satisfactory

Tolerance limit of salinity should be less than ±10.0 (%)

(5) Turbidity

Expected Reading (NTU)	Displayed Reading[f] (NTU)	Tolerance[g] (%)	Results
0	0.61	--	Satisfactory
10	10.08	0.8	Satisfactory
20	19.50	-2.5	Satisfactory
100	99.10	-0.9	Satisfactory
800	777.00	-2.9	Satisfactory

Tolerance limit of turbidity should be less than ±10.0 (%)

~ END OF REPORT ~

Remark(s): -

(f) "Displayed Reading" presents the figures shown on item under calibration/ checking regardless of equipment precision or significant figures.

(g) The "Tolerance Limit" mentioned is the acceptance criteria applicable for similar equipment used by Quality Pro Test-Consult Ltd. or quoted form relevant international standards.

This report shall not be reproduced unless with prior written approval from this laboratory.

專業化驗有限公司
QUALITY PRO TEST-CONSULT LIMITED
Unit 10, 14/F, Wah Wai Centre, 38-40 Au Pui Wan St., Fotan, Hong Kong
Email: info@qualityprotest.com; Website: www.qualityprotest.com
Tel: (852) 3956 8717; Fax: (852) 3956 3928

REPORT OF EQUIPMENT PERFORMANCE CHECK/ CALIBRATION

Report No. : AJ120034
Date of Issue : 11 December 2020

PART A – CUSTOMER INFORMATION

Acuity Sustainability Consulting Limited
Unit C, 11/F, Ford Glory Plaza
37-39 Wing Hong Street
Cheung Sha Wan, Kowloon, Hong Kong
Attn: Mr. Nelson TSUI

PART B – DESCRIPTION

Name of Equipment	:	Multi Water Quality Checker U-53
Manufacturer	:	Horiba
Serial Number	:	L20550GA
Date of Received	:	Dec 08, 2020
Date of Calibration	:	Dec 10, 2020
Date of Next Calibration[a]	:	Mar 09, 2021

PART C – REFERENCE METHODS/ DOCUMENTS FOR THE CALIBRATION

Parameter	Reference Method
pH at 25°C	APHA 21e 4500-H^+ B
Dissolved Oxygen	APHA 21e 4500-O G
Salinity	APHA 21e 2520 B
Turbidity	APHA 21e 2130 B
Temperature	Section 6 of international Accreditation New Zealand Technical Guide no. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

PART D – CALIBRATION RESULTS[b,c]

(1) pH at 25°C

Target (pH unit)	Displayed Reading[d] (pH Unit)	Tolerance[e](pH Unit)	Results
4.00	4.12	0.12	Satisfactory
7.42	7.59	0.17	Satisfactory
10.01	10.19	0.18	Satisfactory

Tolerance of pH should be less than ±0.20 (pH unit)

(2) Temperature

Reading of Ref. thermometer (°C)	Displayed Reading (°C)	Tolerance (°C)	Results
16	17.15	1.15	Satisfactory
27	27.27	0.27	Satisfactory
33	32.26	-0.74	Satisfactory

Tolerance limit of temperature should be less than ±2.0 (°C)

~ CONTINUED ON NEXT PAGE ~

Remark(s): -

(a) The "Date of Next Calibration" is recommended according to best practice principals as practiced by QPT or quoted form relevant international standards.
(b) The results relate only to the calibrated equipment as received
(c) The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.
(d) "Displayed Reading" denotes the figure shown on item under calibration/ checking regardless of equipment precision or significant figures.
(e) The "Tolerance Limit" mentioned is the acceptance criteria applicable for similar equipment used by Quality Pro Test-Consult Ltd. or quoted form relevant international standards.

LEE Chun-ning, Desmond
Senior Chemist

This report shall not be reproduced unless with prior written approval from this laboratory.

專業化驗有限公司
QUALITY PRO TEST-CONSULT LIMITED
Unit 10, 14/F, Wah Wai Centre, 38-40 Au Pui Wan St., Fotan, Hong Kong
Email: info@qualityprotest.com; Website: www.qualityprotest.com
Tel: (852) 3956 8717; Fax: (852) 3956 3928

REPORT OF EQUIPMENT PERFORMANCE CHECK/ CALIBRATION

Report No. : AJ120034
Date of Issue : 11 December 2020

PART D – CALIBRATION RESULTS (Cont'd)

(3) Dissolved Oxygen

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)	Results
0.14	0.00	-0.14	Satisfactory
3.62	3.27	-0.35	Satisfactory
4.48	4.68	0.20	Satisfactory
8.26	8.57	0.31	Satisfactory

Tolerance limit of dissolved oxygen should be less than ±0.50 (mg/L)

(4) Salinity

Expected Reading (g/L)	Displayed Reading (g/L)	Tolerance (%)	Results
10	9.76	-2.40	Satisfactory
20	20.08	0.40	Satisfactory
30	31.08	3.60	Satisfactory

Tolerance limit of salinity should be less than ±10.0 (%)

(5) Turbidity

Expected Reading (NTU)	Displayed Reading[f] (NTU)	Tolerance[g] (%)	Results
0	0.62	--	Satisfactory
10	10.1	1.0	Satisfactory
20	19.0	-5.0	Satisfactory
100	98.0	-2.0	Satisfactory
800	779	-2.6	Satisfactory

Tolerance limit of turbidity should be less than ±10.0 (%)

~ END OF REPORT ~

Remark(s): -

(f) "Displayed Reading" presents the figures shown on item under calibration/ checking regardless of equipment precision or significant figures.

(g) The "Tolerance Limit" mentioned is the acceptance criteria applicable for similar equipment used by Quality Pro Test-Consult Ltd. or quoted form relevant international standards.

This report shall not be reproduced unless with prior written approval from this laboratory.

專業化驗有限公司
QUALITY PRO TEST-CONSULT LIMITED
Unit 10, 14/F, Wah Wai Centre, 38-40 Au Pui Wan St., Fotan, Hong Kong
Email: info@qualityprotest.com; Website: www.qualityprotest.com
Tel: (852) 3956 8717; Fax: (852) 3956 3928

REPORT OF EQUIPMENT PERFORMANCE CHECK/ CALIBRATION

Report No. : AJ110022
Date of Issue : 11 November 2020

PART A – CUSTOMER INFORMATION

Acuity Sustainability Consulting Limited
Unit C, 11/F, Ford Glory Plaza
37-39 Wing Hong Street
Cheung Sha Wan, Kowloon, Hong Kong
Attn: Mr. Nelson TSUI

PART B – DESCRIPTION

Name of Equipment	:	Multi Water Quality Checker U-53
Manufacturer	:	Horiba
Serial Number	:	UHB5F2BB
Date of Received	:	Nov 04, 2020
Date of Calibration	:	Nov 11, 2020
Date of Next Calibration[a]	:	Feb 10, 2021

PART C – REFERENCE METHODS/ DOCUMENTS FOR THE CALIBRATION

Parameter	Reference Method
pH at 25°C	APHA 21e 4500-H^+ B
Dissolved Oxygen	APHA 21e 4500-O G
Salinity	APHA 21e 2520 B
Turbidity	APHA 21e 2130 B
Temperature	Section 6 of international Accreditation New Zealand Technical Guide no. 3 Second edition March 2008: Working Thermometer Calibration Procedure.
Oxidation-Reduction Potential	APHA 22e 2580 B

PART D – CALIBRATION RESULTS[b,c]

(1) pH at 25°C

Target (pH unit)	Displayed Reading[d] (pH Unit)	Tolerance[e](pH Unit)	Results
4.00	4.10	0.10	Satisfactory
7.42	7.46	0.04	Satisfactory
10.01	10.02	0.01	Satisfactory

Tolerance of pH should be less than ±0.20 (pH unit)

(2) Temperature

Reading of Ref. thermometer (°C)	Displayed Reading (°C)	Tolerance (°C)	Results
12	12.38	0.38	Satisfactory
25	25.01	0.01	Satisfactory
35	35.75	0.75	Satisfactory

Tolerance limit of temperature should be less than ±2.0 (°C)

~ CONTINUED ON NEXT PAGE ~

Remark(s): -

[a] *The "Date of Next Calibration" is recommended according to best practice principals as practiced by QPT or quoted form relevant international standards.*
[b] *The results relate only to the calibrated equipment as received*
[c] *The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.*
[d] *"Displayed Reading" denotes the figure shown on item under calibration/ checking regardless of equipment precision or significant figures.*
[e] *The "Tolerance Limit" mentioned is the acceptance criteria applicable for similar equipment used by Quality Pro Test-Consult Ltd. or quoted form relevant international standards.*

LEE Chun-ning, Desmond
Senior Chemist

This report shall not be reproduced unless with prior written approval from this laboratory.

專業化驗有限公司
QUALITY PRO TEST-CONSULT LIMITED
Unit 10, 14/F, Wah Wai Centre, 38-40 Au Pui Wan St., Fotan, Hong Kong
Email: info@qualityprotest.com; Website: www.qualityprotest.com
Tel: (852) 3956 8717; Fax: (852) 3956 3928

REPORT OF EQUIPMENT PERFORMANCE CHECK/ CALIBRATION

Report No. : AJ110022
Date of Issue : 11 November 2020

PART D – CALIBRATION RESULTS (Cont'd)

(3) Dissolved Oxygen

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)	Results
0.07	0.00	-0.07	Satisfactory
4.60	4.27	-0.33	Satisfactory
6.32	6.11	-0.21	Satisfactory
7.98	8.00	0.02	Satisfactory

Tolerance limit of dissolved oxygen should be less than ±0.50 (mg/L)

(4) Salinity

Expected Reading (g/L)	Displayed Reading (g/L)	Tolerance (%)	Results
10	9.88	-1.20	Satisfactory
20	19.60	-2.00	Satisfactory
30	28.55	-4.83	Satisfactory

Tolerance limit of salinity should be less than ±10.0 (%)

(5) Turbidity

Expected Reading (NTU)	Displayed Reading[f] (NTU)	Tolerance[g] (%)	Results
0	0.46	--	Satisfactory
10	10.01	0.1	Satisfactory
20	20.11	0.5	Satisfactory
100	96.80	-3.2	Satisfactory
800	797.00	-0.4	Satisfactory

Tolerance limit of turbidity should be less than ±10.0 (%)

(6) Oxidation-Reduction Potential

Expected Reading (mV)	Displayed Reading (mV)	Tolerance (mV)[g]	Results
222	225	3	Satisfactory

Tolerance limit of Oxidation-Reduction Potential should be less than ±10 (mV)

~ END OF REPORT ~

Remark(s): -

[f] *"Displayed Reading" presents the figures shown on item under calibration/ checking regardless of equipment precision or significant figures.*

[g] *The "Tolerance Limit" mentioned is the acceptance criteria applicable for similar equipment used by Quality Pro Test-Consult Ltd. or quoted form relevant international standards.*

This report shall not be reproduced unless with prior written approval from this laboratory.

Appendix G Event / Action Plan for Water Quality Exceedance

Event	Action			
	ET	IEC	SO	Contractor
Action level being exceeded by one sampling day	Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Repeat measurement on next day of exceedance. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the SO accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the SO and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and SO within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)
Action level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; Repeat measurement on next working day of exceedance. (The above actions should be taken within 1 working day after Action Level being exceeded by two consecutive sampling days)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the SO accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after Action Level being exceeded by two consecutive sampling days)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented. Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after Action Level being exceeded by two consecutive sampling days)	Inform the SO and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and SO within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after Action Level being exceeded by two consecutive sampling days)

Event	Action			
	ET	IEC	SO	Contractor
Limit level being exceeded by one sampling day	Inform the SO and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with Contractor, IEC and SO and propose mitigation measures to IEC and SO within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the SO accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented. Assess the effectiveness of the implemented measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the SO and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and SO and propose mitigation measures to IEC and SO within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)

Event	Action			
	ET	IEC	SO	Contractor
Limit level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC, Contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods. Discuss mitigation measures with IEC, SO and Contractor. Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days. (The above actions should be taken within 1 working day after Limit Level being exceeded by two consecutive sampling days)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the SO accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after Limit Level being exceeded by two consecutive sampling days)	Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented. Assess the effectiveness of the implemented measures. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit level. (The above actions should be taken within 1 working day after Limit Level being exceeded by two consecutive sampling days)	Inform the SO and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and SO and propose mitigation measures to IEC and SO within 3 working days; Implement the agreed mitigation measures; As directed by the SOR, to slow down or to stop all or part of the marine work or construction activities. (The above actions should be taken within 1 working day after Limit Level being exceeded by two consecutive sampling days)

Appendix H Noise Monitoring Equipment Calibration Certificate

Certificate of Calibration

for

Description:	*Sound Level Meter*
Manufacturer:	*SVANTEK*
Type No.:	*971 (Serial No.: 77731)*
Microphone:	*ACO 7052E (Serial No.: 72681)*
Preamplifier:	*SV18 (Serial No.: 78763)*

Submitted by:

Customer:	*Acuity Sustainability Consulting Limited*
Address:	*Unit C, 11/F., Ford Glory Plaza, No. 37-39 Wing Hong Street, Cheung Sha Wan, Kowloon*

Upon receipt for calibration, the instrument was found to be:

☑ **Within**
☐ **Outside**

the allowable tolerance.

The test equipment used for calibration are traceable to National Standards via:
- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory

Date of receipt: 12 February 2020

Date of calibration: 13 February 2020

Calibrated by: _____
Calibration Technician

Certified by: _____
Mr. Ng Yan Wa
Laboratory Manager

Date of issue: **13 February 2020**

ACOUSTICS AND AIR TESTING LABORATORY CO LTD (A+A) *L

Certificate No.: APJ19-160-CC001

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong
Tel: (852) 2668 3423 Fax:(852) 2668 6946
Homepage: http://www.aa-lab.com E-mail : inquiry@aa-lab.com

1. *Calibration Precaution:*

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.

- The results presented are the mean of 3 measurements at each calibration point.

2. *Calibration Conditions:*

Air Temperature:	23.7 **°C**
Air Pressure:	1006 **hPa**
Relative Humidity:	66.2 **%**

3. *Calibration Equipment:*

	Type	Serial No.	Calibration Report Number	Traceable to
Multifunction Calibrator	B&K 4226	2288467	AV180064	HOKLAS

4. *Calibration Results*

Sound Pressure Level

Reference Sound Pressure Level

Setting of Unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672 Class 1 Specification, dB
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz		
34.2-136.2	dBA SPL	Fast	94	1000	94.0	±0.4

Linearity

Setting of Unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672 Class 1 Specification, dB
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz		
34.2-136.2	dBA SPL	Fast	94	1000	94.0	Ref
			104		104.0	±0.3
			114		114.0	±0.3

Time Weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672 Class 1 Specification, dB
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz		
34.2-136.2	dBA SPL	Fast	94	1000	94.0	Ref
		Slow			94.0	±0.3

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong
Tel: (852) 2668 3423 Fax:(852) 2668 6946
Homepage: http://www.aa-lab.com E-mail : inquiry@aa-lab.com

Frequency Response

Linear Response

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
34.2-136.2	dB SPL	Fast	94	31.5	94.1	±2.0
				63	94.0	±1.5
				125	93.9	±1.5
				250	93.9	±1.4
				500	93.9	±1.4
				1000	94.0	Ref
				2000	94.1	±1.6
				4000	93.9	±1.6
				8000	91.2	+2.1; -3.1

A-weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
34.2-136.2	dBA SPL	Fast	94	31.5	54.8	-39.4 ±2.0
				63	67.8	-26.2 ±1.5
				125	77.9	-16.1 ±1.5
				250	85.3	-8.6 ±1.4
				500	90.7	-3.2 ±1.4
				1000	94.0	Ref
				2000	95.3	+1.2 ±1.6
				4000	94.9	+1.0 ±1.6
				8000	90.1	-1.1+2.1; -3.1

C-weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
34.2-136.2	dBC SPL	Fast	94	31.5	91.1	-3.0 ±2.0
				63	93.2	-0.8 ±1.5
				125	93.7	-0.2 ±1.5
				250	93.9	-0.0 ±1.4
				500	93.9	-0.0 ±1.4
				1000	94.0	Ref
				2000	93.8	-0.2 ±1.6
				4000	93.1	-0.8 ±1.6
				8000	88.2	–3.0 +2.1: –3.1

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong
Tel: (852) 2668 3423 Fax:(852) 2668 6946
Homepage: http://www.aa-lab.com E-mail : inquiry@aa-lab.com

5. *Calibration Results Applied*

The results apply to the particular unit-under-test only. All calibration points are within manufacture's specification as IEC 61672 Class 1.

Uncertainties of Applied Value:

94 dB	31.5 Hz	± 0.15
	63 Hz	± 0.10
	125 Hz	± 0.10
	250 Hz	± 0.10
	500 Hz	± 0.10
	1000 Hz	± 0.05
	2000 Hz	± 0.05
	4000 Hz	± 0.05
	8000 Hz	± 0.15
104 dB	1000 Hz	± 0.05
114 dB	1000 Hz	± 0.05

The uncertainties are evaluated for a 95% confidence level.

Note:
The values given in this certification only related to the values measured at the time of the calibration and any uncertainties quoted will not allow for the equipment long-term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the calibration. (A+A)*L shall not be liable for any loss or damage resulting from the use of the equipment.

ACOUSTICS AND AIR TESTING LABORATORY CO. LTD. (A+A)*L

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong
Tel: (852) 2668 3423 Fax:(852) 2668 6946
Homepage: http://www.aa-lab.com E-mail : inquiry@aa-lab.com

Certificate of Calibration

for

Description:	***Sound Level Meter***
Manufacturer:	***NTi Audio***
Type No.:	***XL2 (Serial No.: A2A-13663-E0)***
Microphone:	***ACO 7052 (Serial No.: 73912)***
Preamplifier:	***NTi Audio MA220 (Serial No.: 5735)***

Submitted by:

Customer:	*Acuity Sustainability Consulting Limited*
Address:	*Unit C, 11/F, Ford Glory Plaza, No. 37-39 Wing Hong Street, Cheung Sha Wan, Kowloon, Hong Kong*

Upon receipt for calibration, the instrument was found to be:

☑ **Within**
☐ **Outside**

the allowable tolerance.

The test equipment used for calibration are traceable to National Standards via:
- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory

Date of receipt: ***08 September 2020***

Date of calibration: ***09 September 2020***

Calibrated by: _____
Calibration Technician

Certified by: _____
Mr. Ng Yan Wa
Laboratory Manager

Date of issue: 09 September 2020

ACOUSTICS AND AIR TESTING LABORATORY CO. LTD. (A+A)*L

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong
Tel: (852) 2668 3423 Fax:(852) 2668 6946
Homepage: http://www.aa-lab.com E-mail: inquiry@aa-lab.com

1. *Calibration Precaution:*

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.

2. *Calibration Conditions:*

Air Temperature:	23.8 °C
Air Pressure:	1008 hPa
Relative Humidity:	62.5 %

3. *Calibration Equipment:*

	Type	Serial No.	Calibration Report Number	Traceable to
Multifunction Calibrator	B&K 4226	2288467	AV200041	HOKLAS

4. *Calibration Results*

Sound Pressure Level

Reference Sound Pressure Level

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
30-130	dBA SPL	Fast	94	1000	94.0	±0.4

Linearity

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
30-130	dBA SPL	Fast	94	1000	94.0	Ref
			104		104.0	±0.3
			114		114.0	±0.3

Time Weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
30-130	dBA SPL	Fast	94	1000	94.0	Ref
		Slow			94.0	±0.3

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong
Tel: (852) 2668 3423 Fax:(852) 2668 6946
Homepage: http://www.aa-lab.com E-mail : inquiry@aa-lab.com

Frequency Response

Linear Response

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
30-130	dB SPL	Fast	94	31.5	94.3	±2.0
				63	94.3	±1.5
				125	94.3	±1.5
				250	94.2	±1.4
				500	94.1	±1.4
				1000	94.0	Ref
				2000	93.8	±1.6
				4000	93.6	±1.6
				8000	93.4	+2.1; -3.1

A-weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
30-130	dBA SPL	Fast	94	31.5	54.8	-39.4 ±2.0
				63	68.0	-26.2 ±1.5
				125	78.1	-16.1 ±1.5
				250	85.5	-8.6 ±1.4
				500	90.8	-3.2 ±1.4
				1000	94.0	Ref
				2000	95.0	+1.2 ±1.6
				4000	94.6	+1.0 ±1.6
				8000	92.3	-1.1 +2.1; -3.1

C-weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
30-130	dBC SPL	Fast	94	31.5	91.2	-3.0 ±2.0
				63	93.4	-0.8 ±1.5
				125	94.1	-0.2 ±1.5
				250	94.1	-0.0 ±1.4
				500	94.1	-0.0 ±1.4
				1000	94.0	Ref
				2000	93.6	-0.2 ±1.6
				4000	92.8	-0.8 ±1.6
				8000	90.4	-3.0 +2.1; -3.1

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong
Tel: (852) 2668 3423 Fax:(852) 2668 6946
Homepage: http://www.aa-lab.com E-mail: inquiry@aa-lab.com

5. *Calibration Results Applied*

The results apply to the particular unit-under-test only. All calibration points are within manufacture's specification as IEC 61672 Class 1.

Uncertainties of Applied Value:

94 dB	31.5 Hz	± 0.05
	63 Hz	± 0.05
	125 Hz	± 0.05
	250 Hz	± 0.05
	500 Hz	± 0.05
	1000 Hz	± 0.05
	2000 Hz	± 0.05
	4000 Hz	± 0.05
	8000 Hz	± 0.10
104 dB	1000 Hz	± 0.05
114 dB	1000 Hz	± 0.05

The uncertainties are evaluated for a 95% confidence level.

Note:
The values given in this certification only related to the values measured at the time of the calibration and any uncertainties quoted will not allow for the equipment long-term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the calibration. (A+A)*L shall not be liable for any loss or damage resulting from the use of the equipment.

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong
Tel: (852) 2668 3423 Fax:(852) 2668 6946

Certificate of Calibration

for

Description:	*Sound Level Meter*
Manufacturer:	*NTi Audio*
Type No.:	*XL2 (Serial No.: A2A-13548-E0)*
Microphone:	*ACO 7052 (Serial No.:73780)*
Preamplifier:	*NTi Audio M2211 MA220 (Serial No.:5235)*

Submitted by:

Customer:	*Acuity Sustainability Consulting Limited*
Address:	*Unit C, 11/F., Ford Glory Plaza, No. 37-39 Wing Hong Street, Cheung Sha Wan, Kowloon*

Upon receipt for calibration, the instrument was found to be:

☑ **Within**
☐ **Outside**

the allowable tolerance.

The test equipment used for calibration are traceable to National Standards via:
- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory

Date of receipt: 10 December 2020

Date of calibration: 12 December 2020

Calibrated by: _____
Calibration Technician

Certified by: _____
Mr. Ng Yan Wa
Laboratory Manager

Date of issue: 12 December 2020

Certificate No.: APJ20-144-CC001

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong
Tel: (852) 2668 3423 Fax:(852) 2668 6946
Homepage: http://www.aa-lab.com E-mail : inquiry@aa-lab.com

1. *Calibration Precaution:*

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.

2. *Calibration Conditions:*

Air Temperature:	23.7 °C
Air Pressure:	1006 hPa
Relative Humidity:	61.8 %

3. *Calibration Equipment:*

	Type	Serial No.	Calibration Report Number	Traceable to
Multifunction Calibrator	B&K 4226	2288467	AV200041	HOKLAS

4. *Calibration Results*

Sound Pressure Level

Reference Sound Pressure Level

Setting of Unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672 Class 1 Specification, dB
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz		
30-130	dBA SPL	Fast	94	1000	94.0	±0.4

Linearity

Setting of Unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672 Class 1 Specification, dB
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz		
30-130	dBA SPL	Fast	94	1000	94.0	Ref
			104		104.0	±0.3
			114		114.0	±0.3

Time Weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672 Class 1 Specification, dB
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz		
30-130	dBA SPL	Fast	94	1000	94.0	Ref
		Slow			94.0	±0.3

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong
Tel: (852) 2668 3423 Fax:(852) 2668 6946
Homepage: http://www.aa-lab.com E-mail : inquiry@aa-lab.com

Frequency Response

Linear Response

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
30-130	dB SPL	Fast	94	31.5	94.1	±2.0
				63	94.1	±1.5
				125	94.1	±1.5
				250	94.1	±1.4
				500	94.1	±1.4
				1000	94.0	Ref
				2000	93.8	±1.6
				4000	93.4	±1.6
				8000	92.7	+2.1; -3.1

A-weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
30-130	dBA SPL	Fast	94	31.5	54.7	-39.4 ±2.0
				63	68.0	-26.2 ±1.5
				125	78.0	-16.1 ±1.5
				250	85.4	-8.6 ±1.4
				500	90.8	-3.2 ±1.4
				1000	94.0	Ref
				2000	95.0	+1.2 ±1.6
				4000	94.4	+1.0 ±1.6
				8000	91.6	-1.1+2.1; -3.1

C-weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
30-130	dBC SPL	Fast	94	31.5	91.1	-3.0 ±2.0
				63	93.3	-0.8 ±1.5
				125	93.9	-0.2 ±1.5
				250	94.1	-0.0 ±1.4
				500	94.1	-0.0 ±1.4
				1000	94.0	Ref
				2000	93.7	-0.2 ±1.6
				4000	92.6	-0.8 ±1.6
				8000	89.7	–3.0 +2.1: –3.1

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong
Tel: (852) 2668 3423 Fax:(852) 2668 6946
Homepage: http://www.aa-lab.com E-mail : inquiry@aa-lab.com

5. *Calibration Results Applied*

The results apply to the particular unit-under-test only. All calibration points are within manufacture's specification as IEC 61672 Class 1.

Uncertainties of Applied Value:

94 dB	31.5 Hz	± 0.10
	63 Hz	± 0.15
	125 Hz	± 0.10
	250 Hz	± 0.10
	500 Hz	± 0.10
	1000 Hz	± 0.05
	2000 Hz	± 0.05
	4000 Hz	± 0.05
	8000 Hz	± 0.10
104 dB	1000 Hz	± 0.05
114 dB	1000 Hz	± 0.05

The uncertainties are evaluated for a 95% confidence level.

Note:
The values given in this certification only related to the values measured at the time of the calibration and any uncertainties quoted will not allow for the equipment long-term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the calibration. (A+A)*L shall not be liable for any loss or damage resulting from the use of the equipment.

ACOUSTICS AND AIR TESTING LABORATORY CO LTD. (A+A) *L

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong
Tel: (852) 2668 3423 Fax:(852) 2668 6946
Homepage: http://www.aa-lab.com E-mail : inquiry@aa-lab.com

綜合試驗有限公司
SOILS & MATERIALS ENGINEERING CO., LTD.
香港新界葵涌永基路22-24號椰林閣集團大廈全幢
The Whole Block of YLK Group Building, Nos. 22-24 Wing Kei Road, Kwai Chung, New Territories, Hong Kong.
Tel: (852) 2873 6860 Fax: (852) 2555 7533 E-mail: smec@cigismec.com Website: www.cigismec.com

HOKLAS 028 CAL

CERTIFICATE OF CALIBRATION

Certificate No.: 20CA0803 01 **Page:** 1 **of** 2

Item tested

Description:	Acoustical Calibrator (Class 1)
Manufacturer:	Pulsar Instruments Ltd.
Type/Model No.:	105
Serial/Equipment No.:	63705
Adaptors used:	-

Item submitted by

Curstomer:	Acuity Sustainability Consulting Limited.
Address of Customer:	-
Request No.:	-
Date of receipt:	03-Aug-2020

Date of test: 06-Aug-2020

Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Lab standard microphone	B&K 4180	2341427	11-May-2021	SCL
Preamplifier	B&K 2673	2743150	03-Jun-2021	CEPREI
Measuring amplifier	B&K 2610	2346941	03-Jun-2021	CEPREI
Signal generator	DS 360	33873	19-May-2021	CEPREI
Digital multi-meter	34401A	US36087050	19-May-2021	CEPREI
Audio analyzer	8903B	GB41300350	18-May-2021	CEPREI
Universal counter	53132A	MY40003662	18-May-2021	CEPREI

Ambient conditions

Temperature:	22 ± 1 °C
Relative humidity:	55 ± 10 %
Air pressure:	1005 ± 5 hPa

Test specifications

1, The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.

2, The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.

3, The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

Test results

This is to certify that the sound calibrator conforms to the requirements of annex B of IEC 60942: 1997 for the conditions under which the test was performed. This does not imply that the sound calibrator meets IEC 60942 under any other conditions.

Details of the performed measurements are presented on **page 2** of this certificate.

Approved Signatory: Feng Junqi **Date:** 07-Aug-2020 **Company Chop:** SOILS & MATERIALS ENGINEERING COMPANY LTD. 綜合試驗有限公司

Comments: The results reported in this certificate refer to the conditon of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

© Soils & Materials Engineering Co., Ltd.

HKAS has accredited this laboratory (Reg. No. HOKLAS 028) under HOKLAS for specific calibration activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this certificate are traceable to the International System of Units (SI) or recognised measurement standards. The results relate only to the item(s) calibrated. This certificate shall not be reproduced except in full without approval of the laboratory.

綜合試驗有限公司
SOILS & MATERIALS ENGINEERING CO., LTD.
香港新界葵涌永基路22-24號椰林閣集團大廈全幢
The Whole Block of YLK Group Building, Nos. 22-24 Wing Kei Road, Kwai Chung, New Territories, Hong Kong.
Tel: (852) 2873 6860 Fax: (852) 2555 7533 E-mail: smec@cigismec.com Website: www.cigismec.com

HOKLAS 028 CAL

CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.: 20CA0803 01 **Page:** 2 **of** 2

1, Measured Sound Pressure Level

The output Sound Pressure Level in the calibrator head was measured at the setting and frequency shown using a calibrated laboratory standard microphone and insert voltage technique. The results are given in below with the estimated uncertainties.

(Output level in dB re 20 μPa)

Frequency Shown Hz	Output Sound Pressure Level Setting dB	Measured Output Sound Pressure Level dB	Estimated Expanded Uncertainty dB
1000	94.00	93.78	0.10

2, Sound Pressure Level Stability - Short Term Fluctuations

The Short Term Fluctuations was determined by measuring the maximum and minimum of the fast weighted DC output of the B&K 2610 measuring amplifier over a 20 second time interval as required in the standard. The Short Term Fluctuation was found to be:

At 1000 Hz **STF = 0.027 dB**

Estimated expanded uncertainty 0.005 dB

3, Actual Output Frequency

The determination of actual output frequency was made using a B&K 4180 microphone together with a B&K 2673 preamplifier connected to a B&K 2610 measuring amplifier. The AC output of the B&K 2610 was taken to an universal counter which was used to determine the frequency averaged over 20 second of operation as required by the standard. The actual output frequency at 1 KHz was:

At 1000 Hz **Actual Frequency = 1000.3 Hz**

Estimated expanded uncertainty 0.1 Hz Coverage factor k = 2.2

4, Total Noise and Distortion

For the Total Noise and Distortion measurement, the unfiltered AC output of the B&K 2610 measuring amplifier was connected to an Agilent Type 8903 B distortion analyser. The TND result at 1 KHz was:

At 1000 Hz **TND = 0.6 %**

Estimated expanded uncertainty 0.7 %

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

- End -

Calibrated by: Fung Chi Yip **Date:** 06-Aug-2020

Checked by: Feng Junqi **Date:** 07-Aug-2020

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

© Soils & Materials Engineering Co., Ltd.

HKAS has accredited this laboratory (Reg. No. HOKLAS 028) under HOKLAS for specific calibration activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this certificate are traceable to the International System of Units (SI) or recognised measurement standards. The results relate only to the item(s) calibrated. This certificate shall not be reproduced except in full without approval of the laboratory.

Appendix I Event / Action Plan for Noise Exceedance

Event	Actions to be taken by Environmental Team as immediate as practicable	Actions to be taken by Independent Environmental Checker as immediate as practicable	Actions to be taken by Supervising Officer's Representative as immediate as practicable	Actions to be taken by Contractor as immediate as practicable
Action Level being exceeded	1. Notify IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, SO and Contractor; 4. Discuss with the IEC and Contractor on remedial measures 5. required; Increase monitoring frequency to check mitigation effectiveness. (The above actions should be taken within 2 working .days after the exceedance is identified)	1. Review the investigation results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the SO accordingly; 3. Advise the SO on the effectiveness of the proposed remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified).	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be 4. implemented; Supervise the implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified).	1. Submit noise mitigation proposals to IEC and SO; 2. Implement noise mitigation proposals. (The above actions should be taken within 2 working days after the exceedance is identified)
Limit Level being exceeded	1. Inform IEC, SO, Contractor and 2. EPD; Repeat measurements to confirm 3. findings; 4. Increase monitoring frequency; Identify source and investigate the 5. cause of exceedance; Carry out analysis of Contractor's 6. working procedures; Discuss with the IEC, Contractor 7. and SO on remedial measures required; Assess effectiveness of 8. Contractor's remedial actions and keep IEC, EPD and SO informed of the results; If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Discuss amongst SO, ET, and Contractor on the potential remedial actions; 2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the SO accordingly; (The above actions should be taken within 2 working days after the exceedance is identified)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be 4. implemented; Supervise the implementation of 5. remedial measures; If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC and SO within 3 working days 3. of notification; Implement the agreed 4. proposals; Submit further proposal if 5. problem still not under control; Stop the relevant portion of works as instructed by the SO until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)

Appendix J Noise Monitoring Data

Location:	Shek Kwu Chau Treatment & Rehabilitation Centre Hostel 1 (M1 / N_S1)
Monitoring date:	4, 11, 18, 25 January 2021 (Daytime)
	4&5, 11&12, 18&19, 25&26 January 2021 (Evening & Night time)
Parameter :	$L_{eq\ 30min}$ (Daytime), $L_{eq\ 5min}$ (Evening & Night time)
Noise source other than construction activities from the Project:	Nil

Noise Monitoring Data:

Date	Start time		End time	Weather	$L_{eq\ 30min}$ dB(A) / $L_{eq\ 5min}$ dB(A)	Sound Level Meter Used	Calibrator Used
4 Jan 2021	16:01	-	16:31	Sunny	57.2	XL2 (Serial No. A2A-13663-E0)	Pulsar 105 (No. 63705)
4 Jan 2021	19:01	-	19:06	Fine	57.1	XL2 (Serial No. A2A-13663-E0)	Pulsar 105 (No. 63705)
	20:01	-	20:06		58.3		
	21:01	-	21:06		57.0		
5 Jan 2021	01:01	-	01:06	Fine	55.6	XL2 (Serial No. A2A-13663-E0)	Pulsar 105 (No. 63705)
	03:01	-	03:06		56.8		
	05:01	-	05:06		56.2		
11 Jan 2021	16:02	-	16:32	Fine	56.7	XL2 (Serial No. A2A-13663-E0)	Pulsar 105 (No. 63705)
11 Jan 2021	19:02	-	19:07	Fine	58.1	XL2 (Serial No. A2A-13663-E0)	Pulsar 105 (No. 63705)
	20:02	-	20:07		57.3		
	21:02	-	21:07		55.1		
12 Jan 2021	01:02	-	01:07	Fine	60.3	XL2 (Serial No. A2A-13663-E0)	Pulsar 105 (No. 63705)
	03:02	-	03:07		57.3		
	05:02	-	05:07		52.3		
18 Jan 2021	16:03	-	16:33	Sunny	58.2	XL2 (Serial No. A2A-13663-E0)	Pulsar 105 (No. 63705)
18 Jan 2021	19:03	-	19:08	Fine	59.6	XL2 (Serial No. A2A-13663-E0)	Pulsar 105 (No. 63705)
	20:03	-	20:08		56.2		
	21:03	-	21:08		60.2		
19 Jan 2021	01:03	-	01:08	Fine	56.1	XL2 (Serial No. A2A-13663-E0)	Pulsar 105 (No. 63705)
	03:03	-	03:08		55.1		
	05:03	-	05:08		52.3		
25 Jan 2021	16:01	-	16:31	Sunny	59.6	XL2 (Serial No. A2A-13663-E0)	Pulsar 105 (No. 63705)

Date	Start time		End time	Weather	$L_{eq\ 30min}$ dB(A) / $L_{eq\ 5min}$ dB(A)	Sound Level Meter Used	Calibrator Used
25 Jan 2021	19:01	-	19:06	Fine	50.6	XL2 (Serial No. A2A-13663-E0)	Pulsar 105 (No. 63705)
	20:01	-	20:06		55.8		
	21:01	-	21:06		55.8		
26 Jan 2021	01:01	-	01:06	Fine	56.4	XL2 (Serial No. A2A-13663-E0)	Pulsar 105 (No. 63705)
	03:01	-	03 06		57.1		
	05:01	-	05:06		57.2		

Location:	Shek Kwu Chau Treatment & Rehabilitation Centre Hostel 2 (M2 / N_S2)
Monitoring date:	4, 11, 18, 25 January 2021 (Daytime)
	4&5, 11&12, 18&19, 25&26 January 2021 (Evening & Night time)
Parameter :	$L_{eq\ 30min}$ (Daytime), $L_{eq\ 5min}$ (Evening & Night time)
Noise source other than construction activities from the Project:	Nil

Noise Monitoring Data:

Date	Start time		End time	Weather	$L_{eq\ 30min}$ dB(A) / $L_{eq\ 5min}$ dB(A)	Sound Level Meter Used	Calibrator Used
4 Jan 2021	16:03	-	16:33	Sunny	61.2	XL2 (Serial No. A2A-13548-E0)	Pulsar 105 (No. 63705)
4 Jan 2021	19:03	-	19:08	Fine	54.6	XL2 (Serial No. A2A-13548-E0)	Pulsar 105 (No. 63705)
	20:03	-	20:08		56.4		
	21:03	-	21:08		60.3		
5 Jan 2021	01:03	-	01:08	Fine	59.3	XL2 (Serial No. A2A-13548-E0)	Pulsar 105 (No. 63705)
	03:03	-	03:08		54.5		
	05:03	-	05:08		53.2		
11 Jan 2021	16:05	-	16:35	Fine	59.0	XL2 (Serial No. A2A-13548-E0)	Pulsar 105 (No. 63705)
11 Jan 2021	19:05	-	19:10	Fine	55.3	XL2 (Serial No. A2A-13548-E0)	Pulsar 105 (No. 63705)
	20:05	-	20:10		56.7		
	21:05	-	21:10		54.7		
12 Jan 2021	01:05	-	01:10	Fine	55.1	XL2 (Serial No. A2A-13548-E0)	Pulsar 105 (No. 63705)
	03:05	-	03:10		50.1		
	05:05	-	05:10		54.9		
18 Jan 2021	16:05	-	16:35	Sunny	57.6	XL2 (Serial No. A2A-13548-E0)	Pulsar 105 (No. 63705)
18 Jan 2021	19:05	-	19:10	Fine	58.6	XL2 (Serial No. A2A-13548-E0)	Pulsar 105 (No. 63705)
	20:05	-	20:10		57.0		
	21:05	-	21:10		49.9		
19 Jan 2021	01:05	-	01:10	Fine	51.6	XL2 (Serial No. A2A-13548-E0)	Pulsar 105 (No. 63705)
	03:05	-	03:10		55.4		
	05:05	-	05:10		55.4		
25 Jan 2021	16:05	-	16:35	Sunny	57.4	XL2 (Serial No. A2A-13548-E0)	Pulsar 105 (No. 63705)


Date	Start time		End time	Weather	$L_{eq\ 30min}$ dB(A) / $L_{eq\ 5min}$ dB(A)	Sound Level Meter Used	Calibrator Used
25 Jan 2021	19:05	-	19:10	Fine	50.3	XL2 (Serial No. A2A-13548-E0)	Pulsar 105 (No. 63705)
	20:05	-	20:10		52.6		
	21:05	-	21:10		52.5		
26 Jan 2021	01:05	-	01:10	Fine	55.3	XL2 (Serial No. A2A-13548-E0)	Pulsar 105 (No. 63705)
	03:05	-	03:10		57.6		
	05:05	-	05:10		57.5		


Location:	Shek Kwu Chau Treatment & Rehabilitation Centre Hostel 3 (M3 / N_S3)
Monitoring date:	4, 11, 18, 25 January 2021 (Daytime)
	4&5, 11&12, 18&19, 25&26 January 2021 (Evening & Night time)
Parameter :	$L_{eq\ 30min}$ (Daytime), $L_{eq\ 5min}$ (Evening & Night time)
Noise source other than construction activities from the Project:	Nil


Noise Monitoring data:

Date	Start time		End time	Weather	$L_{eq\ 30min}$ dB(A) / $L_{eq\ 5min}$ dB(A)	Sound Level Meter Used	Calibrator Used
4 Jan 2021	16:04	-	16:34	Sunny	60.7	SVAN 971 (Serial No. 77731)	Pulsar 105 (No. 63705)
4 Jan 2021	19:04	-	19:09	Fine	47.9	SVAN 971 (Serial No. 77731)	Pulsar 105 (No. 63705)
	20:04	-	20:09		52.2		
	21:04	-	21:09		58.5		
5 Jan 2021	01:04	-	01:09	Fine	60.9	SVAN 971 (Serial No. 77731)	Pulsar 105 (No. 63705)
	03:04	-	03:09		54.5		
	05:04	-	05:09		52.2		
11 Jan 2021	16:04	-	16:34	Fine	62.1	SVAN 971 (Serial No. 77731)	Pulsar 105 (No. 63705)
11 Jan 2021	19:04	-	19:09	Fine	59.8	SVAN 971 (Serial No. 77731)	Pulsar 105 (No. 63705)
	20:04	-	20:09		59.9		
	21:04	-	21:09		60.0		
12 Jan 2021	01:04	-	01:09	Fine	62.1	SVAN 971 (Serial No. 77731)	Pulsar 105 (No. 63705)
	03:04	-	03:09		49.3		
	05:04	-	05:09		47.8		
18 Jan 2021	16:01	-	16:31	Sunny	57.9	SVAN 971 (Serial No. 77731)	Pulsar 105 (No. 63705)
18 Jan 2021	19:01	-	19:06	Fine	58.8	SVAN 971 (Serial No. 77731)	Pulsar 105 (No. 63705)
	20:01	-	20:06		48.7		
	21:01	-	21:06		43.0		
19 Jan 2021	01:01	-	01:06	Fine	55.6	SVAN 971 (Serial No. 77731)	Pulsar 105 (No. 63705)
	03:01	-	03:06		59.3		
	05:01	-	05:06		55.4		
25 Jan 2021	16:02	-	16:32	Sunny	55.7	SVAN 971 (Serial No. 77731)	Pulsar 105 (No. 63705)

Date	Start time		End time	Weather	$L_{eq\ 30min}$ dB(A) / $L_{eq\ 5min}$ dB(A)	Sound Level Meter Used	Calibrator Used
25 Jan 2021	19:02	-	19:07	Fine	54.7	SVAN 971 (Serial No. 77731)	Pulsar 105 (No. 63705)
	20:02	-	20:07		56.4		
	21:02	-	21:07		59.9		
26 Jan 2021	01:02	-	01:07	Fine	56.5	SVAN 971 (Serial No. 77731)	Pulsar 105 (No. 63705)
	03:02	-	03 07		56.5		
	05:02	-	05:07		48.3		

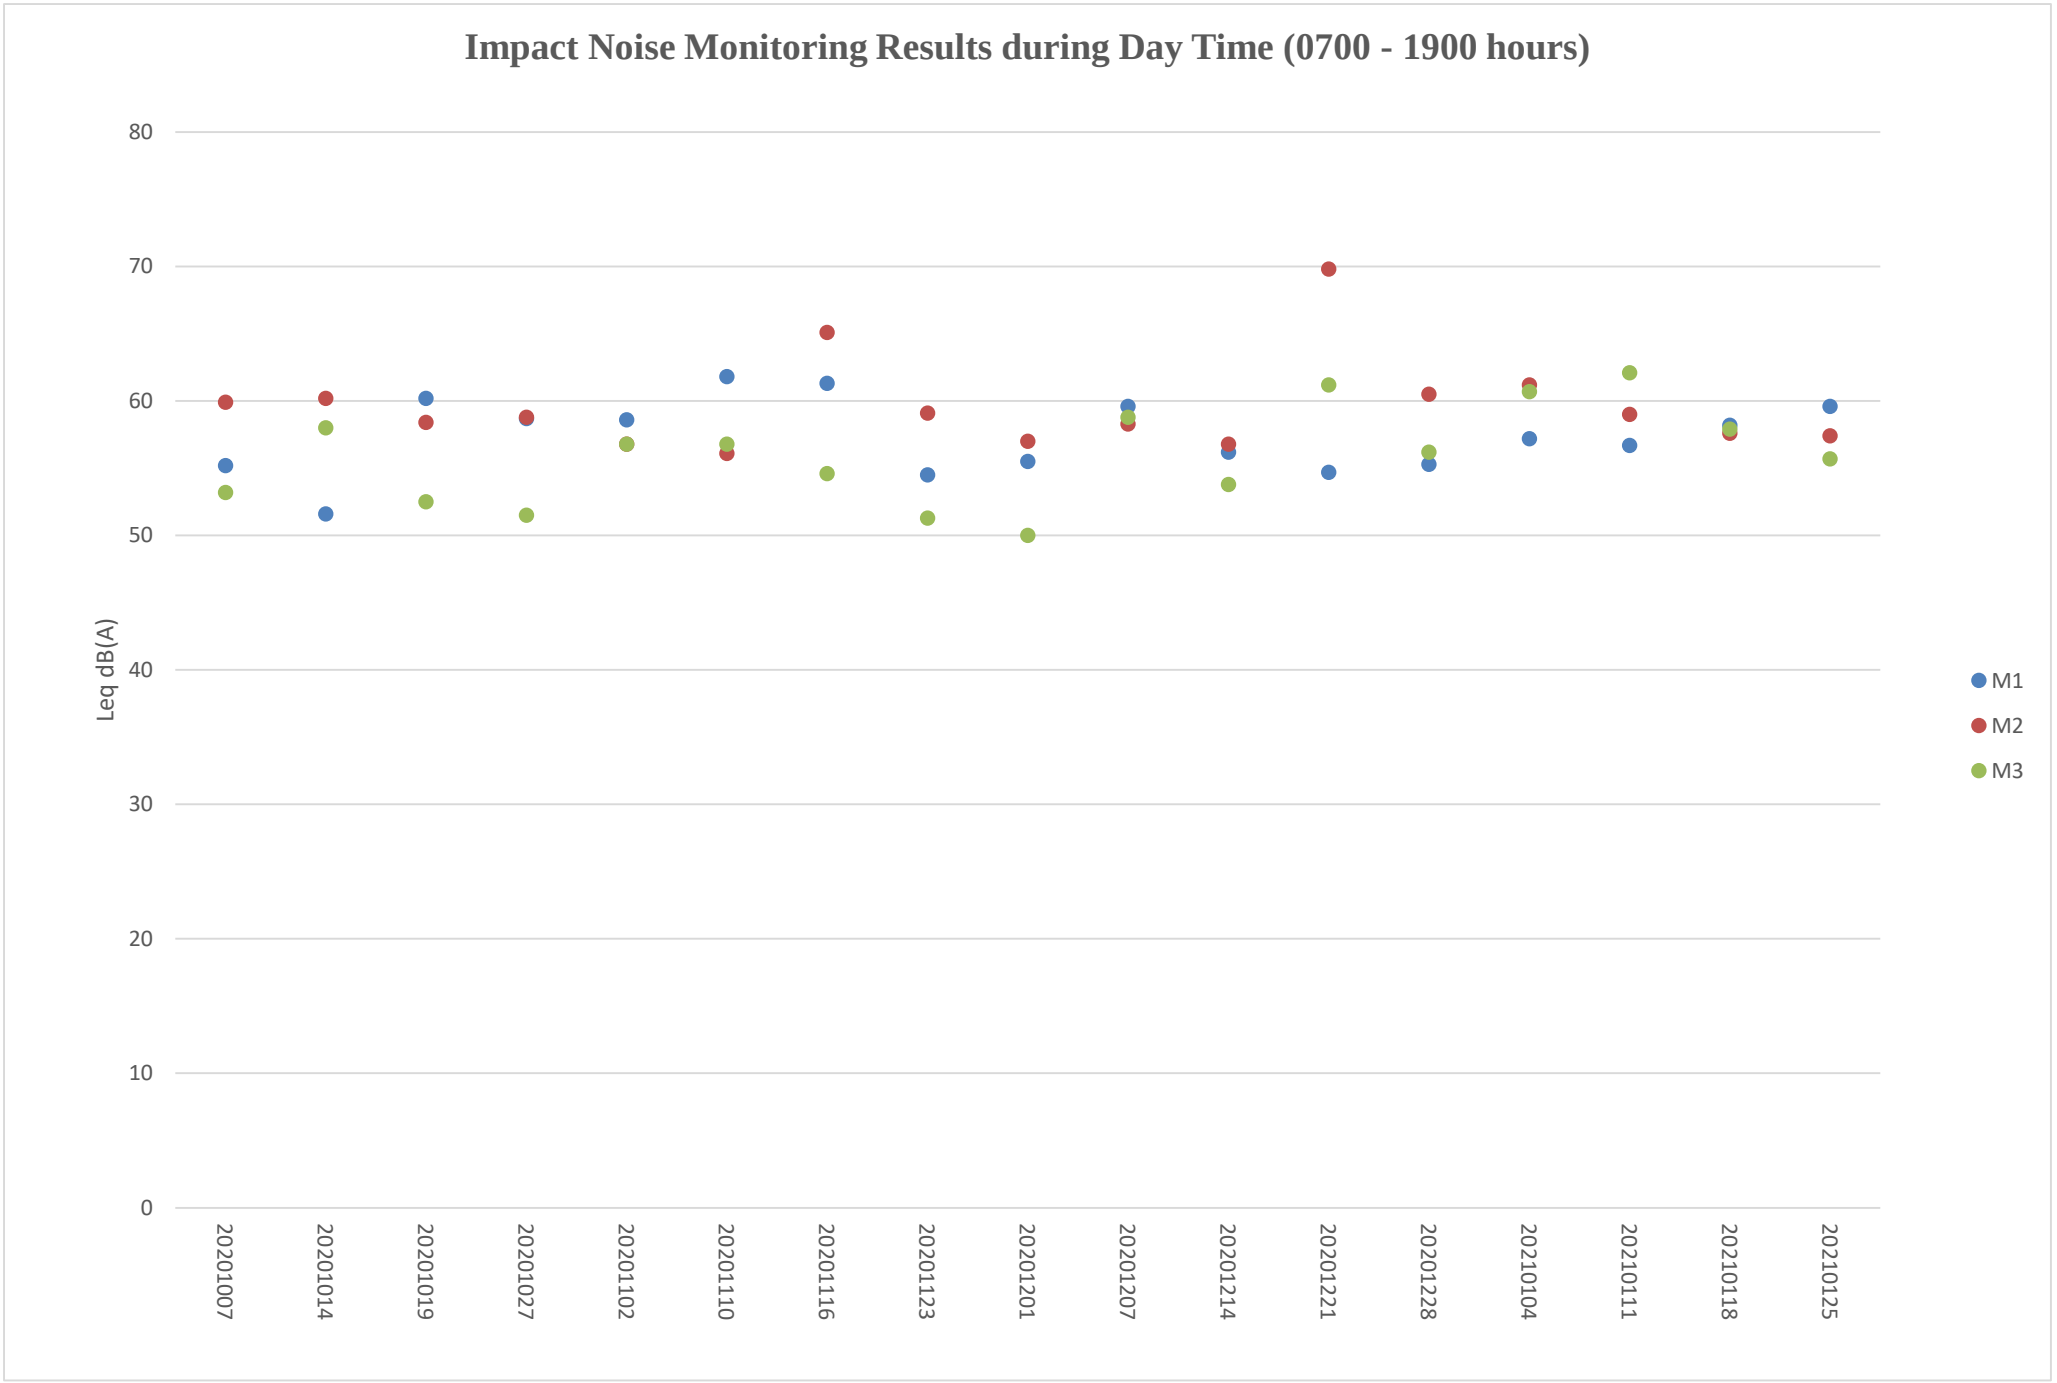
Impact Noise Monitoring Results during Day Time (0700 - 1900 hours)
Leq dB(A)
80
70
60
50
40
30
20
10
0
20201007
20201014
20201019
20201027
20201102
20201110
20201116
20201123
20201201
20201207
20201214
20201221
20201228
20210104
20210111
20210118
20210125
M1
M2
M3

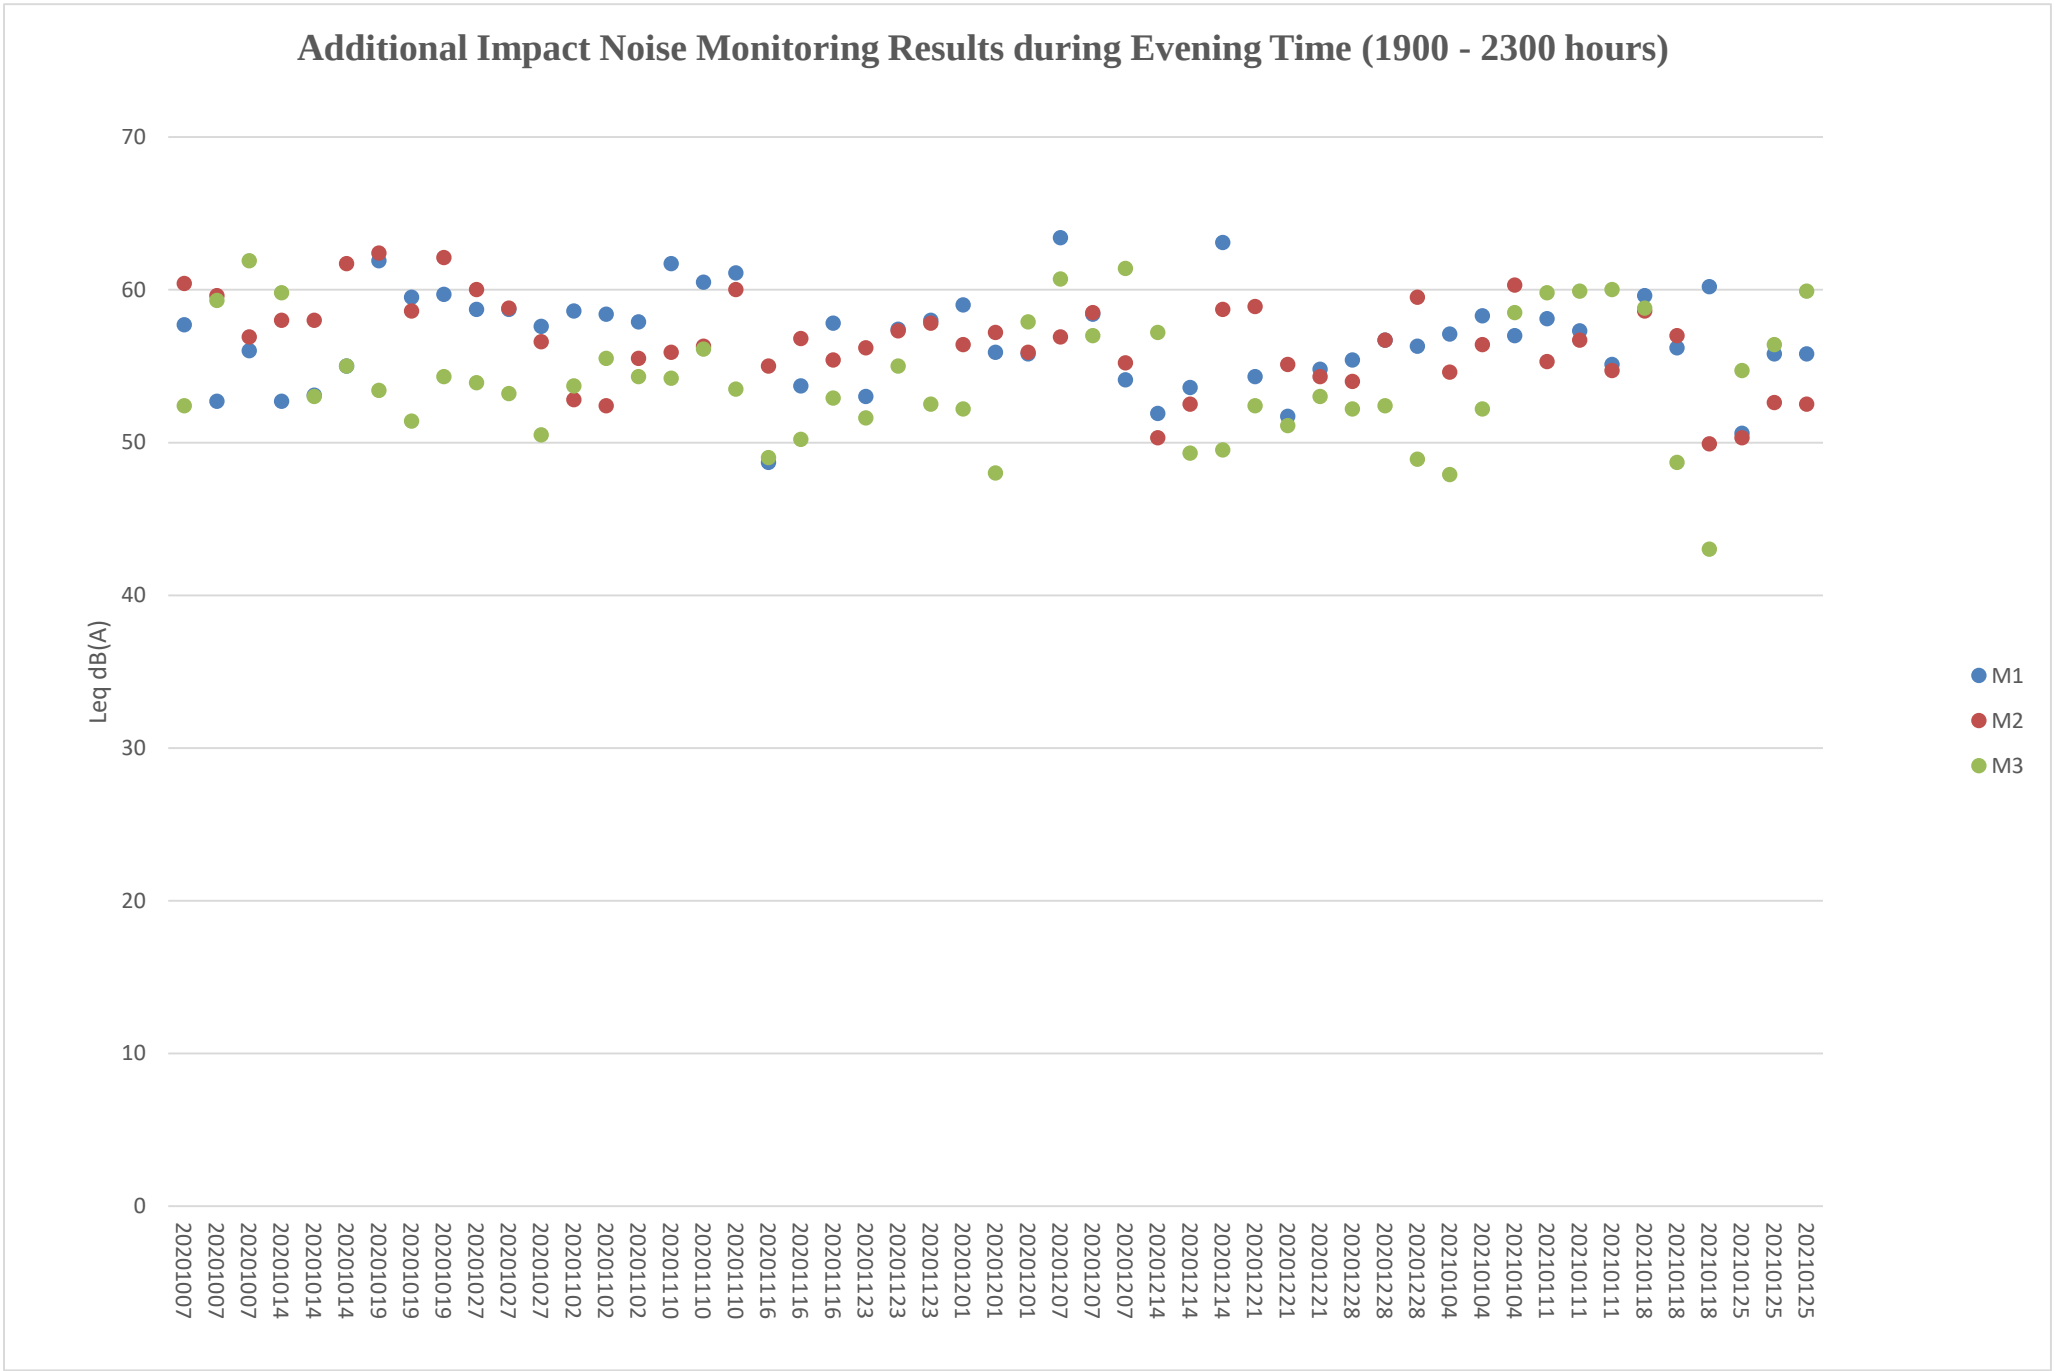
Additional Impact Noise Monitoring Results during Evening Time (1900 - 2300 hours)
Leq dB(A)
70
60
50
40
30
20
10
0
M1
M2
M3
20201007
20201007
20201007
20201014
20201014
20201014
20201019
20201019
20201019
20201027
20201027
20201027
20201102
20201102
20201102
20201110
20201110
20201110
20201116
20201116
20201116
20201123
20201123
20201123
20201201
20201201
20201201
20201207
20201207
20201207
20201214
20201214
20201214
20201221
20201221
20201221
20201228
20201228
20201228
20210104
20210104
20210104
20210111
20210111
20210111
20210118
20210118
20210118
20210125
20210125
20210125

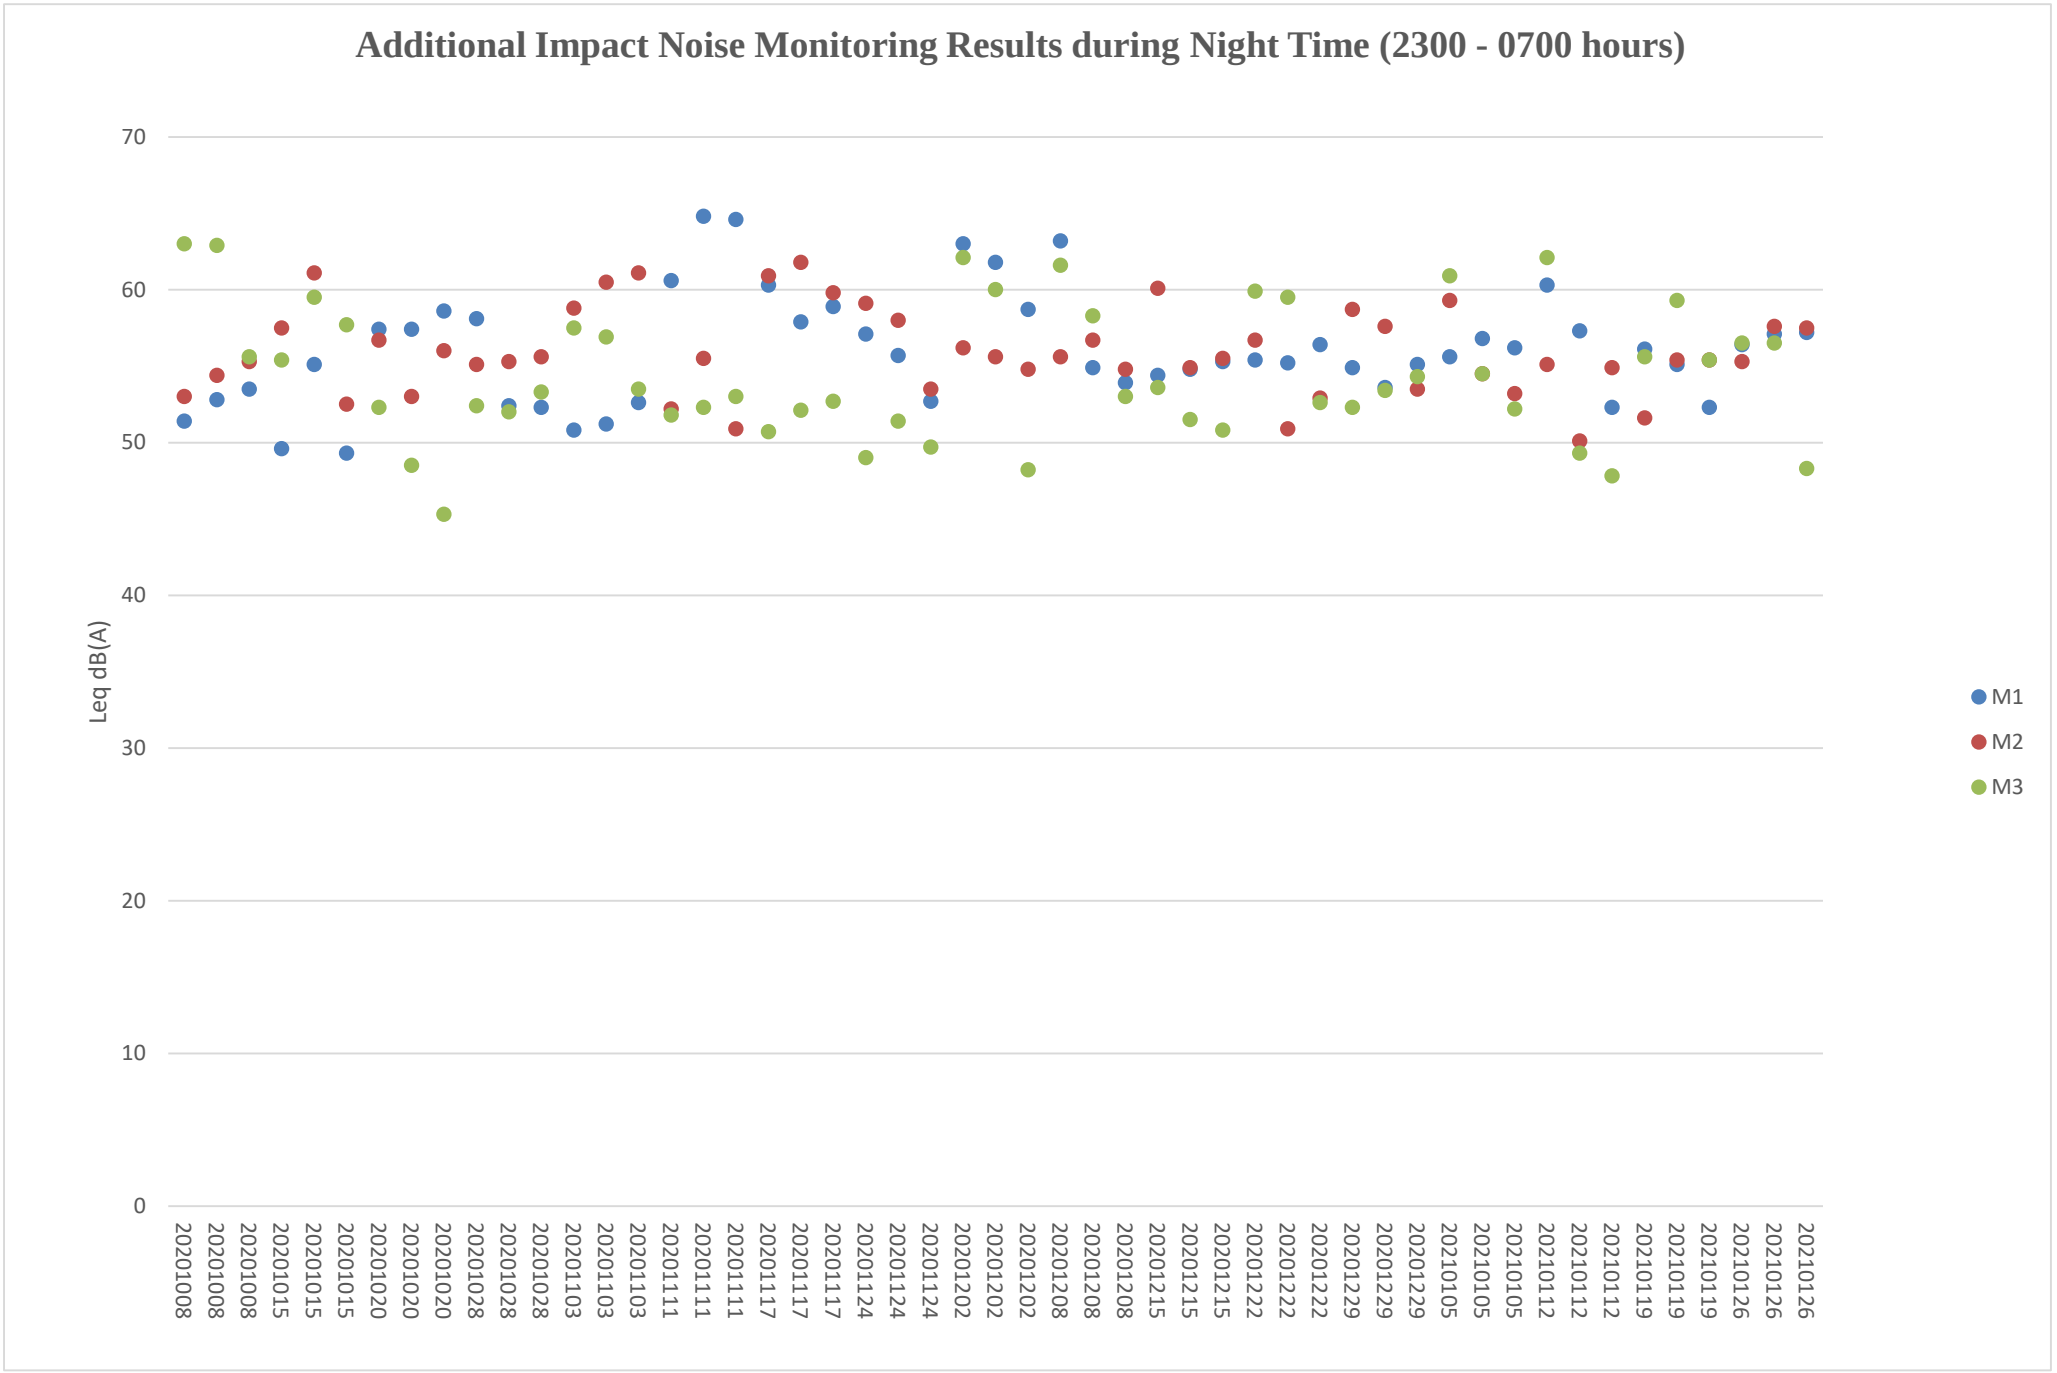
Additional Impact Noise Monitoring Results during Night Time (2300 - 0700 hours)
Leq dB(A)
70
60
50
40
30
20
10
0
M1
M2
M3
20201008
20201008
20201008
20201015
20201015
20201015
20201020
20201020
20201020
20201028
20201028
20201028
20201103
20201103
20201103
20201111
20201111
20201111
20201117
20201117
20201117
20201124
20201124
20201124
20201202
20201202
20201202
20201208
20201208
20201208
20201215
20201215
20201215
20201222
20201222
20201222
20201229
20201229
20201229
20210105
20210105
20210105
20210112
20210112
20210112
20210119
20210119
20210119
20210126
20210126
20210126

Appendix K Waste Flow Table

吉寶西格斯 - 振華聯營公司

Keppel Seghers - Zhen Hua Joint Venture

Monthly Summary Waste Flow Table for 2018 (year)

Project : Integrated Waste Management Facilities, Phase 1 Contract No.: EP/SP/66/12

Month	Actual Quantities of Inert C&D Materials Generated Monthly								Actual Quantities of C&D Wastes Generated Monthly					
	Total Quantity Generated	Hard Rock and Large Broken Concrete (see Note 1)	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill Sand	Imported Fill Public fill	Imported Fill Rock	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste		Others, e.g. general refuse (see Note 3)
	(in ,000m^3)	(in ,000m^3)	(in ,000m^3)	(in ,000m^3	(in ,000m^3)	(in ,000m^3)			(in ,000 kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in ,000L)	(in ,000 m^3)
Jan	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Feb	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Mar	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Apr	0	0	0	0	0	0	0	0	0	0	0	0	0	0
May	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Jun	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Sub-total	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Jul	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Aug	0	0	0	0	0	0	0	0	0	0	0	0	0	0.0065
Sep	0	0	0	0	0	2.9619	0	0	0	0	0	0	0	0
Oct	0	0	0	0	0	3.0771	0	0	0	0	0	0	0	0.0130
Nov	0	0	0	0	0	6.7871	0	0	0	0	0	0	0	0
Dec	0	0	0	0	0	59.0709	0	0	0	0	0	0.2000	0.8700	0
Total	0	0	0	0	0	71.8970	0	0	0	0	0	0.2000	0.8700	0.0195

Notes:
(1) Broken concrete for recycling into aggregates.
(2) Plastics refer to plastic bottles/ containers, plastic sheets/ foam from packaging materials.
(3) Use the conversion factor : 1 full load of dumping truck being equivalent to 6.5m^3 by volume.

吉寶西格斯 - 振華聯營公司
Keppel Seghers - Zhen Hua Joint Venture

Monthly Summary Waste Flow Table for 2019 (year)

Project : Integrated Waste Management Facilities, Phase 1 Contract No.: EP/SP/66/12

Month	Actual Quantities of Inert C&D Materials Generated Monthly								Actual Quantities of C&D Wastes Generated Monthly					
	Total Quantity Generated	Hard Rock and Large Broken Concrete (see Note 1)	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill Sand	Imported Fill Public fill	Imported Fill Rock	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste		Others, e.g. general refuse (see Note 3)
	(in ,000m^3)	(in ,000m^3)	(in ,000m^3)	(in ,000m^3	(in ,000m^3)	(in ,000m^3)			(in ,000 kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in ,000L)	(in ,000 m^3)
Jan	0	0	0	0	0	82.6139	0	0	0	0	0	0	0	0.0065
Feb	0	0	0	0	0	46.7821	0	0	0	0	0	0	0	0
Mar	0	0	0	0	0	97.1000	0	0.7552	0	0.2560	0	0	0	0
Apr	0	0	0	0	0	58.0413	0	0	0	0	0	0	0	0
May	0	0	0	0	0	14.5625	0	1.4648	0	0	0	0	0	0.0065
Jun	0	0	0	0	0	0	0	6.8421	0	0	0	0	0	0
Sub-total	0	0	0	0	0	299.0998	0	9.0621	0	0.2560	0	0	0	0.0130
Jul	0	0	0	0	0	0	0	0.4289	0	0	0	0	8.4000	0.0130
Aug	0	0	0	0	0	2.5775	0	10.5600	0	0	0	0	0	0
Sep	0	0	0	0	0	6.1081	0	8.4704	0	0.3530	0	0	0	0.0065
Oct	0	0	0	0	0	9.8875	0	7.1900	0	0	0	0	0	0
Nov	0	0	0	0	0	38.3088	0	19.3105	0	0	0	0	0	0.0195
Dec	0	0	0	0	0	54.3469	0	26.9807	0	0	0	0	0	0.0910
Total	0	0	0	0	0	410.3286	0	82.0026	0	0.6090	0	0	8.4000	0.1430

Notes:
(1) Broken concrete for recycling into aggregates.
(2) Plastics refer to plastic bottles/ containers, plastic sheets/ foam from packaging materials.
(3) Use the conversion factor : 1 full load of dumping truck being equivalent to 6.5m^3 by volume.

吉寶西格斯 - 振華聯營公司
Keppel Seghers - Zhen Hua Joint Venture

Monthly Summary Waste Flow Table for 2020 (year)

Project : Integrated Waste Management Facilities, Phase 1 Contract No.: EP/SP/66/12

Month	Actual Quantities of Inert C&D Materials Generated Monthly								Actual Quantities of C&D Wastes Generated Monthly					
	Total Quantity Generated	Hard Rock and Large Broken Concrete (see Note 1)	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill Sand	Imported Fill Public fill	Imported Fill Rock	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste		Others, e.g. general refuse (see Note 3)
	(in ,000m^3)	(in ,000m^3)	(in ,000m^3)	(in ,000m^3	(in ,000m^3)	(in ,000m^3)			(in ,000 kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in ,000L)	(in ,000 m^3)
Jan	0	0	0	0	0	37.1550	0	25.0812	0	0	0	0	0	0.0065
Feb	0	0	0	0	0	27.7910	0	18.8300	0	0	0	0	0	0.0065
Mar	0	0	0	0	0	22.5669	0	26.1586	0	0	0	0	7.2000	0.0065
Apr	0	0	0	0	0	12.7800	0	10.1825	0	0	0	0	0	0.0195
May	0	0	0	0	0	16.1138	0	24.3740	0	0.4220	0	0	0	0.0195
Jun	0	0	0	0	0	31.5177	0	28.3030	0	0	0	0	0	0.0065
Sub-total	0	0	0	0	0	147.9244	0	132.9293	0	0.4220	0	0	7.2000	0.0650
Jul	0	0	0	0	0	34.7856	17.0606	35.1800	0	0	0	0	0	0.0195
Aug	0	0	0	0	0	27.1375	65.5667	27.9335	0	0	0	0	0	0
Sep	0	0	0	0	0	11.9813	110.1328	43.5435	0	0	0	0	0	0.0195
Oct	0	0	0	0	0	2.8213	131.6600	22.5415	0	0	0	0	0	0.0130
Nov	0	0	0	0	0	0	162.1811	44.6475	0	0.4090	0	0	0.4000	0.0130
Dec	0	0	0	0	0	0	174.9800	57.8380	0	0	0	0	0	0.0130
Total	0	0	0	0	0	224.6501	661.5812	364.6133	0	0.8310	0	0	7.6000	0.1430

Notes:
(1) Broken concrete for recycling into aggregates.
(2) Plastics refer to plastic bottles/ containers, plastic sheets/ foam from packaging materials.
(3) Use the conversion factor : 1 full load of dumping truck being equivalent to 6.5m^3 by volume.

吉寶西格斯 - 振華聯營公司
Keppel Seghers - Zhen Hua Joint Venture

Monthly Summary Waste Flow Table for 2021 (year)

Project : Integrated Waste Management Facilities, Phase 1 Contract No.: EP/SP/66/12

Month	Actual Quantities of Inert C&D Materials Generated Monthly								Actual Quantities of C&D Wastes Generated Monthly					
	Total Quantity Generated	Hard Rock and Large Broken Concrete (see Note 1)	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill Sand	Imported Fill Public fill	Imported Fill Rock	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste		Others, e.g. general refuse (see Note 3)
	(in ,000m^3)	(in ,000m^3)	(in ,000m^3)	(in ,000m^3	(in ,000m^3)	(in ,000m^3)			(in ,000 kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in ,000L)	(in ,000 m^3)
Jan	0	0	0	0	0	0	198.1311	36.4775	0	0	0	0	0	0.0065
Feb														
Mar														
Apr														
May														
Jun														
Sub-total	0	0	0	0	0	0	198.1311	36.4775	0	0	0	0	0	0.0065
Jul														
Aug														
Sep														
Oct														
Nov														
Dec														
Total	0	0	0	0	0	0	198.1311	36.4775	0	0	0	0	0	0.0065

Notes:
(1) Broken concrete for recycling into aggregates.
(2) Plastics refer to plastic bottles/ containers, plastic sheets/ foam from packaging materials.
(3) Use the conversion factor : 1 full load of dumping truck being equivalent to 6.5m^3 by volume.

Appendix L Event / Action Plan for Coral Monitoring

Event	Action			
	ET Leader	IEC	SO	Contractor
Action Level Exceedance	1. Check monitoring data 2. Inform the IEC, SO ,and Contractor of the findings; 3. Increase the monitoring to at least once a month to confirm findings; 4. Propose mitigation measures for consideration	1. Discuss monitoring with the ET and the Contractor; 2. Review proposals for additional monitoring and any other measures submitted by the Contractor and advise the SO accordingly.	1. Discuss with the IEC additional monitoring requirements and any other measures proposed by the ET; 2. Make the agreement on the measures to be implemented.	1. Inform the SO and confirm notification of the non-compliance in writing; 2. Discuss with the ET and the IEC and propose measures to the IEC and the SO; 3. Implement the agreed measures.
Limit Level Exceedance	1. Undertake Steps 1-4 as in the Action Level Exceedance. If further exceedance of Limit Level, propose enhancement measures for consideration.	1. Discuss monitoring with the ET and the Contractor; 2. Review proposals for additional monitoring and any other measures submitted by the Contractor and advise the SO accordingly.	1. Discuss with the IEC additional monitoring requirements and any other measures proposed by the ET; 2. Make the agreement on the measures to be implemented.	1. Inform the SO and confirm notification of the non-compliance in writing; 2. Discuss with the ET and the IEC and propose measures to the IEC and the SO; 3. Implement the agreed measures.

Appendix M Event / Action Plan for White-Bellied Sea Eagle

Event	Action		
	Environmental Team	**Audit Team**	**Contractor**
Absence of White-bellied Sea Eagle during a whole day of monitoring.	Inform audit team. Increase monitoring frequency to daily.	Inform site engineer and contractor. If the absence remains: • Review construction activities and noise monitoring records of the associated period; • Identify potential causes of the absence; • Propose remedial measures, such as change of construction method and sequence; • Confirm the feasibility of the proposed remedial measures with site engineer and contractor; • Discuss with environmental team about the effectiveness of the proposed remedial measures.	Implement the agreed remedial measures.


Appendix N Exceedance Report


Statistical Summary of Exceedances in the Reporting Period

Water Quality (Regular DCM)			
Location	**Action Level**	**Limit Level**	**Total**
B1	1	0	1
B2	1	0	1
B3	0	0	0
B4	0	1	1
CR1	0	0	0
CR2	0	0	0
F1A	0	0	0
H1	0	0	0
S1	0	0	0
S2A	0	0	0
S3	0	0	0
M1	1	0	1


Noise (Day Time)			
Location	**Action Level**	**Limit Level**	**Total**
M1	0	0	0
M2	0	0	0
M3	0	0	0
Noise (Evening Time)			
Location	**Action Level**	**Limit Level**	**Total**
M1	0	0	0
M2	0	0	0
M3	0	0	0
Noise (Night Time)			
Location	**Action Level**	**Limit Level**	**Total**
M1	0	0	0
M2	0	0	0
M3	0	0	0


Incident Report on Action Level or Limit Level Non-compliance

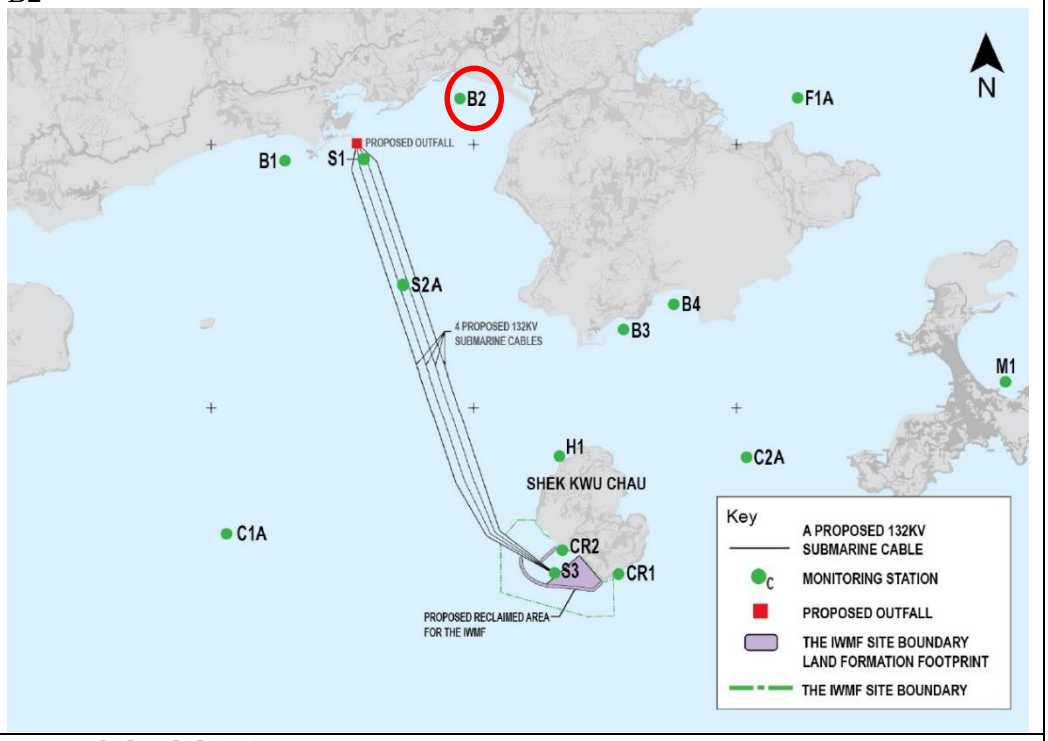Project	Integrated Waste Management Facilities, Phase 1		
Date	13 Jan 2021 (Lab result received on 18 Jan 2021)		
Time	11:02 – 14:32 (Mid-Ebb)		
Mid-Ebb			
Monitoring Location	B2 		
Parameter	Suspended Solid (SS)		
Action & Limit Levels	Action Level	Limit Level	
	≥ 8.0 mg/L	≥ 10.0 mg/L	
Measurement Level	Impact Station(s) of Exceedance	Control Stations	Impact Station(s) without Exceedance
	8.0 mg/L (B2)	6.3 mg/L (C1A) 5.8 mg/L (C2A)	6.5 mg/L (B1) 7.5 mg/L (B3) 7.0 mg/L (B4) 6.3 mg/L (F1A) 5.7 mg/L (H1) 4.8 mg/L (M1) 5.7 mg/L (CR1) 6.7 mg/L (CR2)
Possible reason for Action or Limit Level Non-compliance	Works scheduled on site on 13 Jan 2021 include reclamation works, laying of rockfill and caisson installation. Dominating sea current direction was found to be from Northwest to Southeast at waters around Shek Kwu Chau. B2 is located at unrelated stream direction (neither upstream nor downstream, far away) to the works location, exceedance of this monitoring station is deemed to be unrelated to the Project. Silt curtain checking by the Contractor was implemented on Marine Access (13 Jan 2021, 10:30am) and checking results showed that no deficiency of silt curtain was found on that day.		

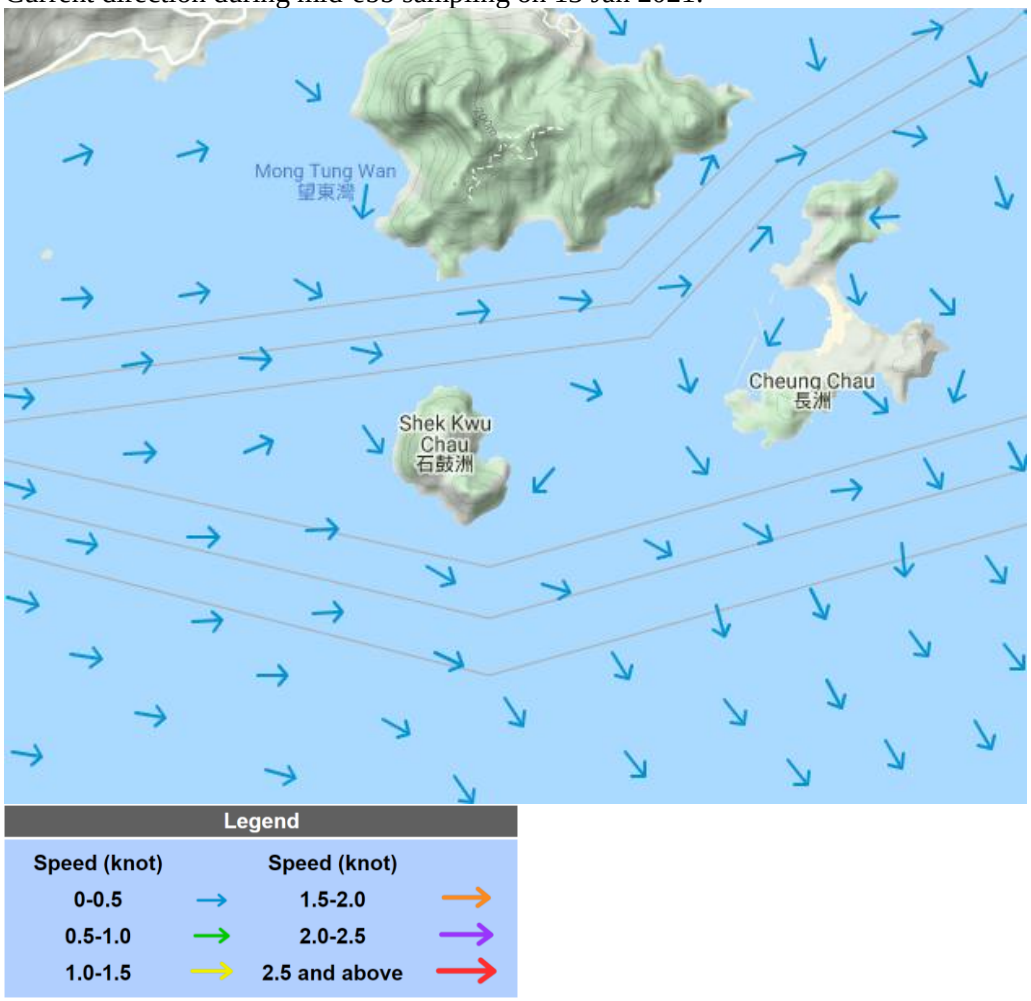	From MMO monitoring records on 13 Jan 2021, MMO team was arranged for one derrick barge (金盈 8)) and silt curtain at western marine access area on that day while no deficiency of silt curtain was found before the commencement of and during construction activity. According to the field observation by Marine Mammal Observer team & sampling team during sampling event, no silt plume was observed in the Project site. Site tidiness in the present barges in the Project site were checked during weekly site inspection on 12 Jan 2021. No major observation of improper site practices that could contribute to the increase of the suspended solids recorded.
Remarks	Current direction during mid-ebb sampling on 13 Jan 2021:  (Sourced from http://current.hydro.gov.hk/en/map.html)
Prepared by	Joe Ho
Date	1 Feb 2021

Incident Report on Action Level or Limit Level Non-compliance

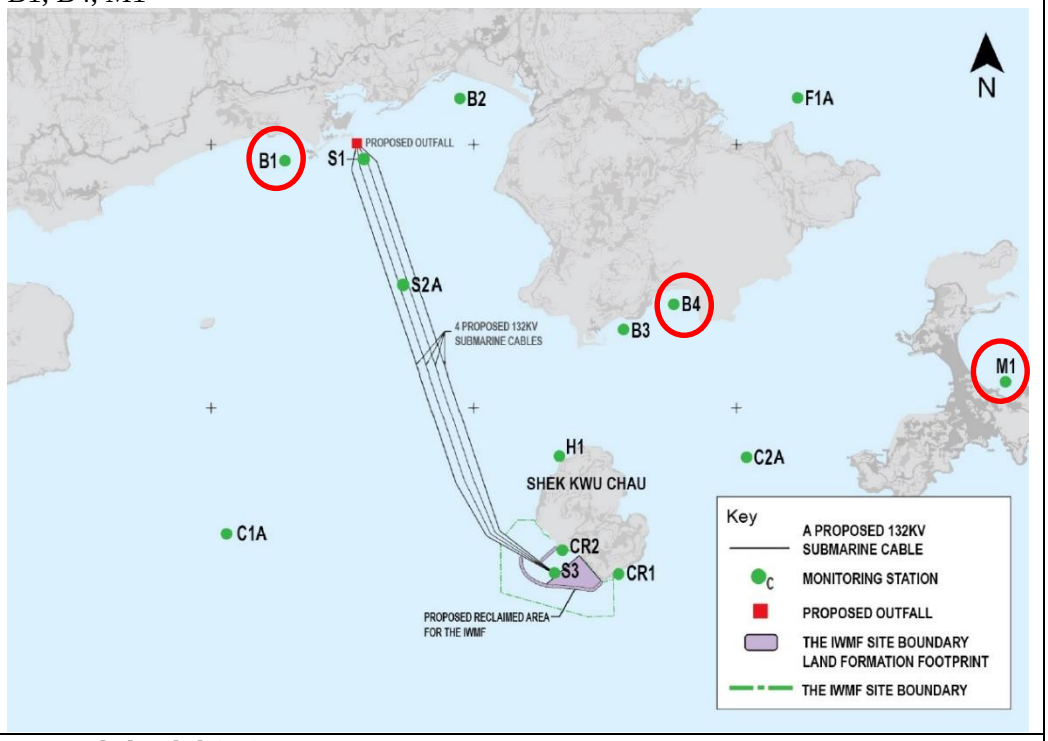Project	Integrated Waste Management Facilities, Phase 1		
Date	31 Jan 2020 (Lab result received on 3 Feb 2021)		
Time	08:00 – 11:30 (Mid-Flood)		
Mid-Flood			
Monitoring Location	B1, B4, M1  		
Parameter	Suspended Solid (SS)		
Action & Limit Levels	Action Level	Limit Level	
	≥ 9.0 mg/L (120% of C2A)	≥ 10.0 mg/L	
Measurement Level	Impact Station(s) of Exceedance	Control Stations	Impact Station(s) without Exceedance
	9.0 mg/L (B1) 11.5 mg/L (B4) 9.7 mg/L (M1)	7.7 mg/L (C1A) 7.5 mg/L (C2A)	8.0 mg/L (B2) 8.5 mg/L (B3) 8.2 mg/L (F1A) 8.3 mg/L (H1) 6.8 mg/L (CR1) 6.3 mg/L (CR2)
Possible reason for Action or Limit Level Non-compliance	Works scheduled on site on 31 Jan 2021 include reclamation works, laying of rockfill and caisson installation. Dominating sea current direction was found to be from Southeast to Northwest at waters around Shek Kwu Chau. B1, B4 and M1 are located at unrelated stream direction (neither upstream nor downstream, far away) to the works location, exceedance of this monitoring station is deemed to be unrelated to the Project. Silt curtain checking by the Contractor was implemented on Marine Access (31 Jan 2021, 07:00am) and checking results showed that no deficiency of silt curtain was found on that day. From MMO monitoring records on 31 Jan 2021, MMO team was arranged for one derrick barge (金盈 8)) and silt curtain at western marine access area on that day while		

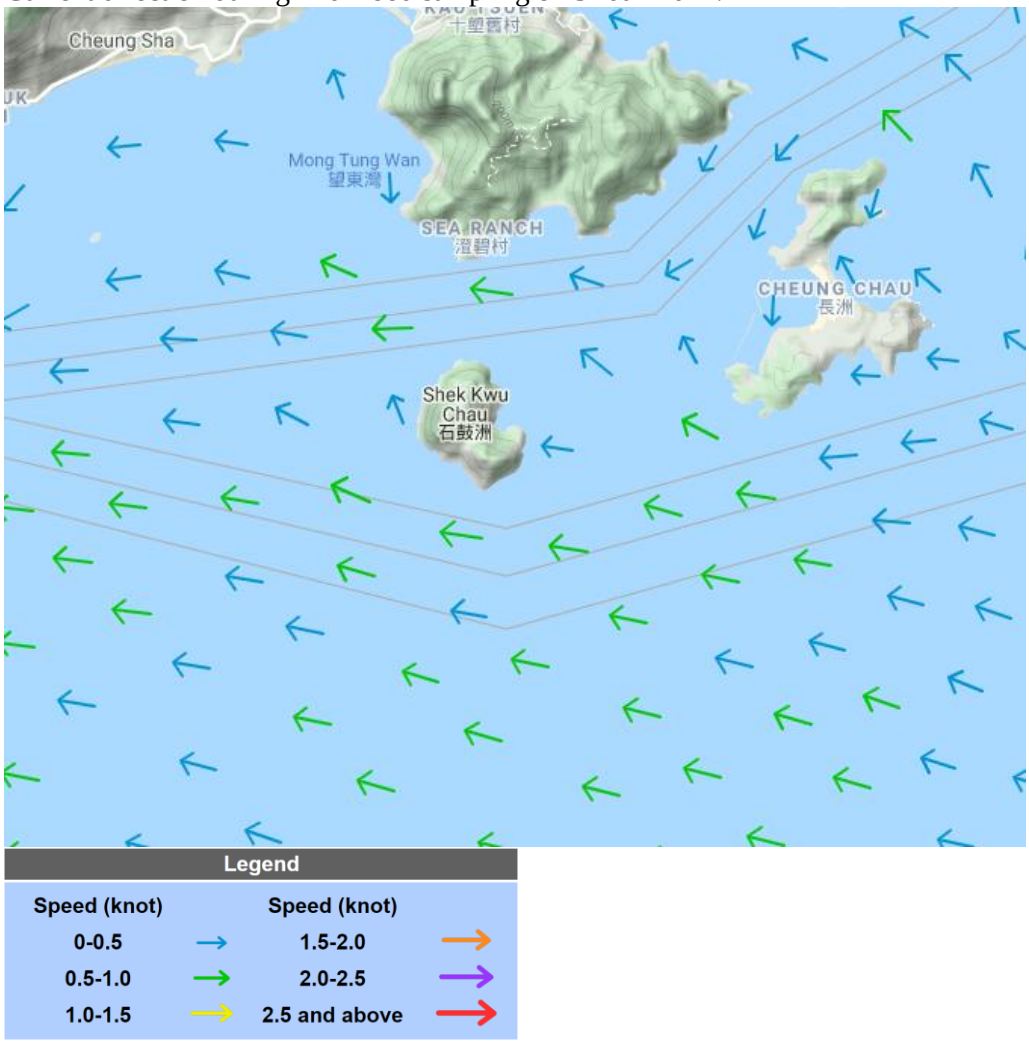	no deficiency of silt curtain was found before the commencement of and during construction activity. According to the field observation by Marine Mammal Observer team & sampling team during sampling event, no silt plume was observed in the Project site. Site tidiness in the present barges in the Project site were checked during weekly site inspection on 27 Jan 2021. No major observation of improper site practices that could contribute to the increase of the suspended solids recorded.
Remarks	Current direction during mid-flood sampling on 31 Jan 2021:  (Sourced from http://current.hydro.gov.hk/en/map.html)
Prepared by	Joe Ho
Date	4 Feb 2021

Appendix O Complaint Log

Statistical Summary of Environmental Complaints

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
1 Jan 2021- 31 Jan 2021	0	0	N/A

Statistical Summary of Environmental Summons

Reporting Period	Environmental Summons Statistics		
	Frequency	Cumulative	Details
1 Jan 2021- 31 Jan 2021	0	0	N/A

Statistical Summary of Environmental Prosecution

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Cumulative	Details
1 Jan 2021- 31 Jan 2021	0	0	N/A

Appendix P Impact Monitoring Schedule of Next Reporting Month

Impact Monitoring Schedule for IWMF

Feb-21

Sun	Mon	Tue	Wed	Thu	Fri	Sat
	1	2	3	4	5	6
	Impact Daytime, Evening & Night time Noise monitoring for M1, M2 & M3	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 13:22 - 18:33 Flood Tide: 06:39 - 13:22 Monitoring Time: Mid-ebb: 14:12 - 17:42 Mid-flood: 08:15 - 11:45 Daytime, Evening & Night time Noise monitoring for M1, M2 & M3		Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 15:00 - 20:28 Flood Tide: 07:51 - 15:00 Monitoring Time: &Mid-ebb: 15:30 - 19:00 Mid-flood: 09:40 - 13:10 Ecology monitoring for WBSE	Impact Ecology monitoring for Marine Mammals by Vessel-based Line-Transect Survey	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 05:00 - 10:00 Flood Tide: 10:00 - 16:49 Monitoring Time: *#$Mid-ebb: 08:00 - 11:30 Mid-flood: 11:39 - 15:09
7	8	9	10	11	12	13
	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 08:00 - 12:00 Flood Tide: 12:00 - 18:33 Monitoring Time: Mid-ebb: 08:15- 11:45 Mid-flood: 13:31 - 17:01 Daytime, Evening & Night time Noise monitoring for M1, M2 & M3	Impact Daytime, Evening & Night time Noise monitoring for M1, M2 & M3	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 10:00 - 13:40 Flood Tide: 13:40 - 20:00 Monitoring Time: &Mid-ebb: 10:05 - 13:35 Mid-flood: 15:05 - 18:35 Ecology monitoring for WBSE			
14	15	16	17	18	19	20
		Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 12:39 - 18:01 Flood Tide: 06:11 - 12:39 Monitoring Time: Mid-ebb: 13:35- 17:05 *Mid-flood: 08:00 - 11:30		Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 13:39 - 19:49 Flood Tide: 06:54 - 13:39 Monitoring Time: Mid-ebb: 14:59- 18:29 Mid-flood: 08:31 - 12:01 Daytime, Evening & Night time Noise monitoring for M1, M2 & M3 Ecology monitoring for WBSE	Impact Daytime, Evening & Night time Noise monitoring for M1, M2 & M3	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 15:18 - 23:59 Flood Tide: 07:00 - 15:18 Monitoring Time: &Mid-ebb: 15:30 - 19:00 Mid-flood: 09:24 - 12:54
21	22	23	24	25	26	27
	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 17:00 - 23:59 Flood Tide: 01:00 - 17:00 Monitoring Time: #$&Mid-ebb: 15:30 - 19:00 Mid-flood: 08:00 - 11:30 Daytime, Evening & Night time Noise monitoring for M1, M2 & M3	Impact Daytime, Evening & Night time Noise monitoring for M1, M2 & M3	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 14:33 - 18:07 Flood Tide: 07:18 - 14:33 Monitoring Time: Mid-ebb: 14:35- 18:05 Mid-flood: 09:10 - 12:40	Impact Ecology monitoring for WBSE	Impact Water Quality monitoring for B1, B2, B3, B4, H1, C1A, C2A, F1A, CR1, CR2, M1 Tidal Period: Ebb Tide: 14:33 - 18:07 Flood Tide: 07:18 - 14:33 Monitoring Time: Mid-ebb: 14:35- 18:05 Mid-flood: 09:10 - 12:40 Ecology monitoring for Marine Mammals by Vessel-based Line-Transect Survey	
28						

Remarks:
1. Daytime Noise Monitoring (07:00-1900), Evening Time Noise Monitoring (1900-2300), Night Time Noise Monitoring (2300-0700)
2. Water Quality Monitoring for S1,S2 and S3 will only conduct during DCM works, refer to Detailed DCM Plan

Note:
* - as per Marine Department Notice No 107 of 2018, all vessels employed for the works should stay in the works area outside the hours of works (0700 to 2300). Due to safty concern, Water Quality Monitoring would start at 0800.
- Prioritized routing: Mid-Ebb: C1→S3→CR2→CR1→H1→Remaining stations and Mid-Flood: C2→CR1→S3→CR2→H1→Remaining stations
$ - Since predicted tide is shorter than 3.5 hours, method of 90% tidal period as monitoring time is approached.
& - Due to safety concern for sampling event in night-time, method of 90% tidal period as monitoring time is approached and end at 1900.
